



## Bangladesh Modern Food Storage Facilities Project (P120583)

SOUTH ASIA | Bangladesh | Agriculture and Food Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2014 | Seq No: 22 | ARCHIVED on 22-Dec-2023 | ISR59482 |

Implementing Agencies: Directorate General of Food, Ministry of Food, Government of Bangladesh

## Key Dates

### Key Project Dates

Bank Approval Date: 30-Dec-2013

Effectiveness Date: 27-May-2014

Planned Mid Term Review Date: 05-Mar-2018

Actual Mid-Term Review Date: 07-May-2018

Original Closing Date: 30-Jun-2020

Revised Closing Date: 31-Dec-2024

## Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The overall Project development objective is to increase the grain reserve available to households to meet their post-disaster needs and improve the efficiency of grain storage management.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

## Components Table

Name

Component A – Construction of Modern Grain Storage Silo Facilities:(Cost \$323.08 M)

Component B – Support for Food and Market Planning and Monitoring Program:(Cost \$52.00 M)

Component C - Project management, Construction Supervision, Technical Assistance, Training and Strategic Studies:(Cost \$45.07 M)

Component D - Contingent Emergency Response (CERC)

## Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

## Implementation Status and Key Decisions

The following key issues and actions were identified during this Implementation Support Mission (November 16-28, 2023):

- **Expedite completion of remaining silo constructions:** Constructions of all remaining silos (Narayanganj, Barishal, Chattogram, Ashuganj and Kulna) are experiencing delays. The mission requested PMU to conduct very close monitoring including monthly field visits and follow up meetings with contractors, expedite any pending approvals and payments to ensure completion of these sites before the Project closing date (December 31, 2024)
- **Finalize the Food Stocks and Market Monitoring System (FSMMS).** The FSMMS pilots are under implementation in Rajsahi division and Chattogram district before the system goes live.



- **Operational continuity of the project without any managerial gap during the rest of project life as well as retaining key personnel/consultants towards the proper closing:** DG Food is requested to fill the vacant position at the PMU and to keep the key consultants including financial management, procurement/contract management, safeguards specialists until the project closing date.
- **Start planning for the project closure with adequate focus on evaluating project's impacts:** Given the project is approaching to the final year of its life, PMU was advised to start preparing project closure including adequate analysis of project's outcomes.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Macroeconomic	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Sector Strategies and Policies	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Technical Design of Project or Program	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Institutional Capacity for Implementation and Sustainability	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Fiduciary	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Environment and Social	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Stakeholders	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Other	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Overall	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

## Results

### PDO Indicators by Objectives / Outcomes

1. To increase the grain reserve available to households				
▶ P1. Increased grain storage capacity in public and household storage facilities (Metric ton, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	28,000.00	28,000.00	400,000.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024
Comments:	Distribution of 500,000 household silo (HHS) with 56 kg capacity completed as of 30 Nov, 2019. Hence, total HHS capacity is 500,000*56=28,000 Tones			



▶ P2. Direct Project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,560,000.00	2,560,000.00	10,000,000.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024
□ Of which female (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	48.00	48.00	50.00

## 2. To improve the efficiency of grain storage management

▶ P3. Reduction in grain storage and handling losses in public storage facilities (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024

### Intermediate Results Indicators by Components

Component A – Construction of Modern Grain Storage Silo Facilities				
▶ A1. Site development works completed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.00	8.00	7.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024
▶ A2. Public food grain silo constructed and operational (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	7.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024
Comments:	Mymensingh and Madhupur silos are completed but not yet handed over to DG Food for operation.			
▶ A3. Households provided with safe grain storage containers (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	500,000.00	500,000.00	500,000.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	30-Jun-2020
<b>► A4. Percentage women employed in construction of steel silos (relative to total labor force employed) (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	5.00	10.00	7.00	12.00
Date	30-Nov-2018	31-Oct-2021	19-Dec-2023	31-Dec-2024
<b>► A5. Targeted beneficiaries satisfied with the household silos (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	98.00	90.00	90.00
Date	30-Nov-2018	31-Oct-2021	19-Dec-2023	31-Dec-2024
<b>□ Of which female (Percentage, Custom Breakdown)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	98.00	90.00	90.00
Date	30-Nov-2018	31-Oct-2021	19-Dec-2023	31-Dec-2024
<b>► A6. Contractor workforce received training on Gender-Based Violence/ SEA (percentage of total contractor workforce) (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00
Date	30-Nov-2018	31-Oct-2021	19-Dec-2023	31-Dec-2024

**Component B – Support for Food and Market Planning and Monitoring Program**

**► B1. CSDs and LSDs connected to a centralized public food storage and distribution management system (Percentage, Custom)**

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	40.00	80.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024

Comments: Current value for B1 indicator is corrected to 0.

**► B2. Research papers completed and approved by FPMU (Number, Custom)**



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12.00	16.00	15.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024
<b>► B3. Policy notes prepared under the Food Policy Research Program published (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	8.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024

Component C - Project management, Construction Supervision, Technical Assistance, Training and Strategic Studies

**► C1. Client days of training provided by gender (Number, Custom)**

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	128,051.00	138,820.00	200,000.00
Date	01-Feb-2014	31-Oct-2021	19-Dec-2023	31-Dec-2024

% of female (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	45.34	45.00	25.00

**► C2. People living in the adjacent areas of steel silos are aware and satisfied with the presence and benefits of steel silos (Percentage, Custom)**

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	30-Nov-2018	31-Oct-2021	19-Dec-2023	31-Dec-2024

Comments: Information for this indicator will be provided by the Citizen Report Card surveys to be undertaken by a third-party monitoring firm when silos will be erected and operational.

Of which female (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	05-Apr-2020	31-Oct-2021	19-Dec-2023	31-Dec-2024

**Performance-Based Conditions**



**Data on Financial Performance**


**Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P120583	IDA-52650	Effective	USD	210.00	210.00	0.00	158.84	29.83	84%
P120583	IDA-67260	Effective	USD	202.00	202.00	0.00	83.71	115.35	42%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P120583	IDA-52650	Effective	30-Dec-2013	07-Apr-2014	27-May-2014	30-Jun-2020	31-Dec-2024
P120583	IDA-67260	Effective	31-Jul-2020	19-Oct-2020	27-Oct-2020	31-Oct-2023	31-Dec-2024

**Cumulative Disbursements**

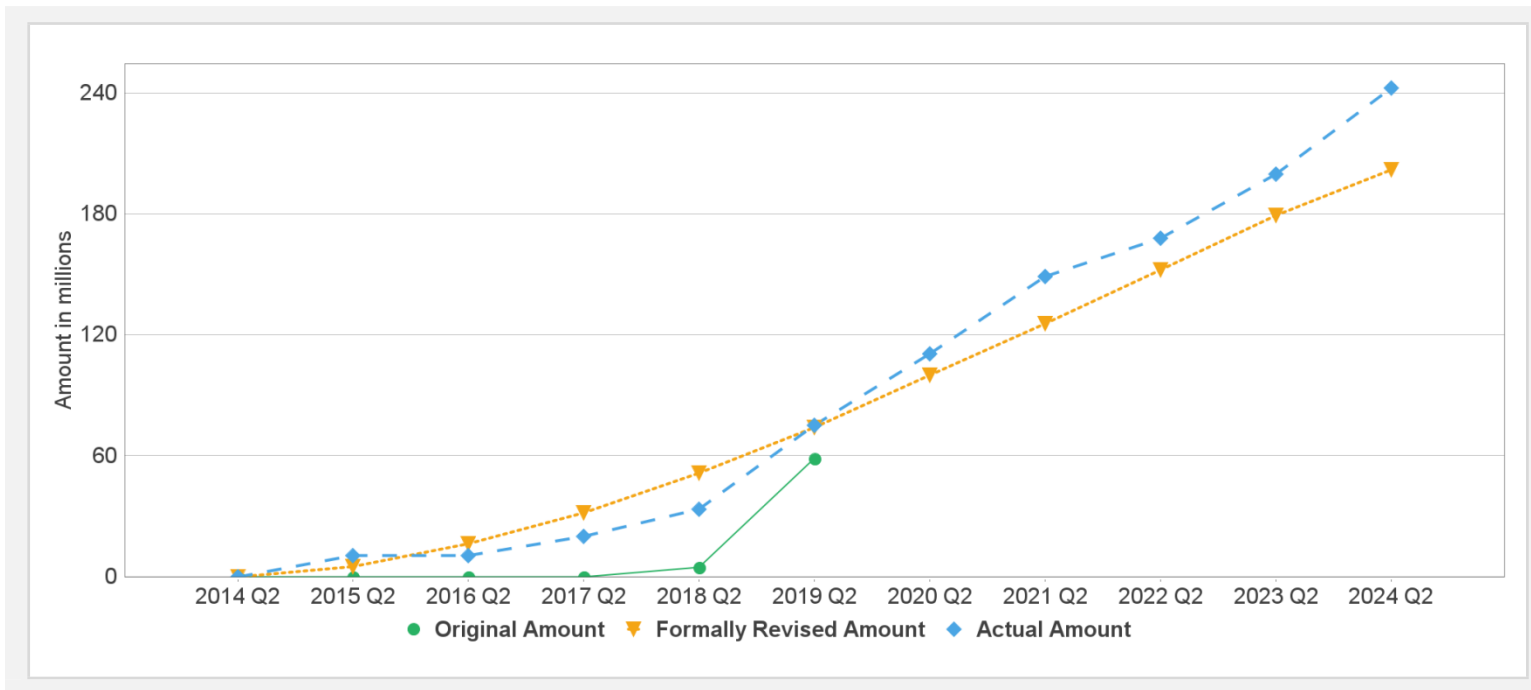



---

### **Restructuring History**

Level 2 Approved on 19-Aug-2015 ,Level 2 Approved on 12-Feb-2020 ,Level 2 Approved on 18-Sep-2023

### **Related Project(s)**

P168484-Additional Financing For Modern Food Storage Facilities Project

---
