



## Freetown Emergency Recovery Project (P166075)

AFRICA | Sierra Leone | Social, Urban, Rural and Resilience Global Practice Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2018 | Seq No: 2 | ARCHIVED on 13-Dec-2018 | ISR35179 |

Implementing Agencies: Ministry of Finance and Economic Development (MoFED), Ministry of Finance and Economic Development (MoFED)

### Key Dates

#### Key Project Dates

Bank Approval Date: 22-Feb-2018

Effectiveness Date: 13-Apr-2018

Planned Mid Term Review Date: 28-Oct-2019

Actual Mid-Term Review Date: --

Original Closing Date: 28-Feb-2021

Revised Closing Date: 28-Feb-2021

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to rehabilitate selected critical infrastructure and to strengthen government capacity for managing disaster risk.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

Component 1: Rehabilitation of Public Infrastructure and Slope Stabilization:(Cost \$7.84 M)

Component 2: Strengthening institutional capacity:(Cost \$1.80 M)

Component 3: Project Management:(Cost \$1.90 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial

### Implementation Status and Key Decisions

Overall, the FERP is progressing well and disbursement is 23% in its first six months of implementation. This is driven by the urgent earthworks under Component 1.1., carried out by UNOPS. The other two works components are procuring the design consultancies under Components 1.2 and 1.3. Component 2 is moving ahead with an Emergency Preparedness and Response Capacity Needs Assessment, which will inform institutional capacity strengthening requirements in disaster risk management.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● High	● High	● High
Macroeconomic	● Substantial	● Substantial	● Substantial
Sector Strategies and Policies	● Moderate	● Moderate	● Moderate
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Substantial	● Substantial	● Substantial
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Substantial	● Substantial	● Substantial
Other	--	--	--
Overall	● Substantial	● Substantial	● Substantial

## Results

### PDO Indicators by Objectives / Outcomes

Rehabilitate critical infrastructure				
▶Number of beneficiaries with restored or improved access to service delivery infrastructure (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	34,000-44,000
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021
▲Female beneficiaries with restored or improved access to service delivery infrastructure (Text, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40-50%
▶Number of population protected by the slope stabilization works (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	400-600
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021
▲Female beneficiaries protected by slope stabilization works (Text, Custom Supplement)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40-50%

**Strengthen government capacity for managing disaster risk**

►Disaster preparedness and contingency plan developed (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	0.00	No	Yes
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021

**Overall Comments**

The number of people protected from slope stabilization works is being calculated and will be included in the next ISR.

**Intermediate Results Indicators by Components**

**Component 1: Rehabilitation of Public Infrastructure and Slope Stabilization**

►Number of bridges reconstructed (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4-6
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021

►Length of roads rehabilitated (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4-6 km
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021

►Number of Kilometers of water piping installed (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	42-55 km
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021

**Component 2: Strengthening institutional capacity**



▶Number of individuals engaged in community disaster risk awareness and preparedness activities (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3,400-4,400
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021
▲Percentage of women engaged in community disaster risk awareness and preparedness activities (Text, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40-50%
▶Number of Government Officials trained in disaster preparedness and management (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	15-20
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021
▲Female Government Officials trained in disaster preparedness and management (Text, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20-30%

Component 3: Project Management				
▶Percentage of Greivances Addressed (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80-100%
Date	01-Mar-2018	25-May-2018	01-Nov-2018	26-Feb-2021

## Data on Financial Performance

### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P166075	IDA-D2750	Effective	USD	10.00	10.00	0.00	2.29	7.67	23%


### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
---------	----------------	--------	---------------	--------------	--------------------	--------------------	-------------------



P166075 IDA-D2750 Effective 22-Feb-2018 26-Mar-2018 13-Apr-2018 28-Feb-2021 28-Feb-2021

### Cumulative Disbursements

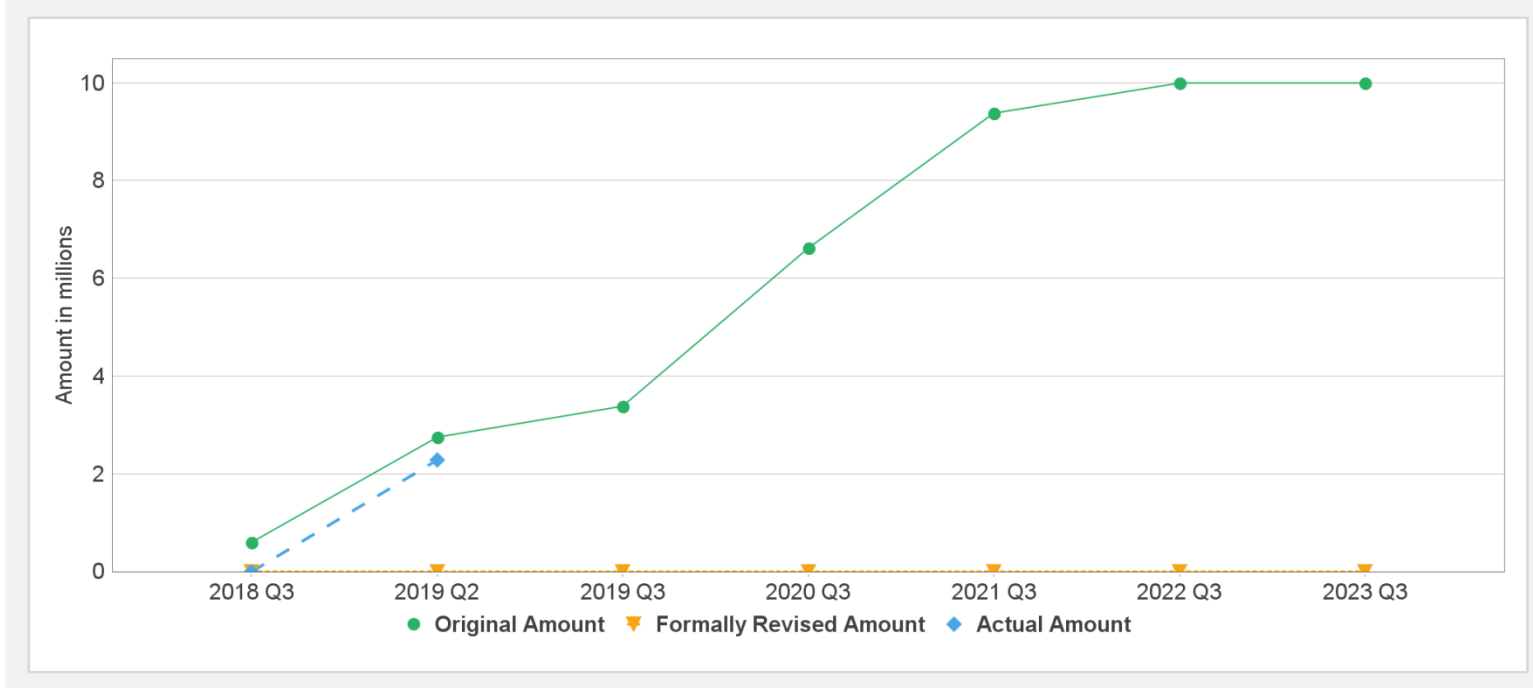

### Restructuring History

There has been no restructuring to date.

### Related Project(s)

There are no related projects.
