



## Second Irrigation and Drainage Improvement Project (P086592)

EUROPE AND CENTRAL ASIA | Kazakhstan | Water Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2013 | Seq No: 5 | ARCHIVED on 11-Nov-2015 | ISR21420 |

Implementing Agencies: Ministry of Environmental Protection

### Key Dates

#### Key Project Dates

Bank Approval Date:27-Jun-2013

Effectiveness Date:29-Jan-2015

Planned Mid Term Review Date:10-Jul-2017

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2021

Revised Closing Date:31-Dec-2021

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project development objective is to improve irrigation and drainage service delivery to support farmers in the Project areas. This will be achieved through rehabilitation and modernization of irrigation and drainage systems; improved management, operation and maintenance of these systems; and more efficient use of associated irrigated lands; all with improved participation of users in developing and managing the rehabilitated / modernized systems.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

Rehabilitation and Modernization of I&D Systems Infrastructure:(Cost \$323.38 M)

Sustainable Management, Operation and Maintenance of I&D Systems:(Cost \$6.93 M)

Agricultural Development:(Cost \$9.80 M)

Project Management, Technical Assistance, and Training:(Cost \$2.89 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory



Overall Risk Rating

● Substantial

● Substantial

## Implementation Status and Key Decisions

The project was declared effective on January 29, 2015. The PMU staff composition was completed in spring 2015. Recently in November 2015, the QCBS evaluation for the project's major TA contract has been completed (combining detailed design, construction supervision, safeguards management, and participatory irrigation management). The contract negotiations, signing, mobilization, and advance payment are expected to be completed by December 31, 2015. After that, all project activities under the four project components would start on the ground.

## Risks



### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Substantial	● Substantial
Macroeconomic	--	● Moderate	● Moderate
Sector Strategies and Policies	--	● Moderate	● Moderate
Technical Design of Project or Program	--	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Moderate	● Moderate
Environment and Social	--	● Moderate	● Moderate
Stakeholders	--	● Moderate	● Moderate
Other	--	--	--
Overall	--	● Substantial	● Substantial

## Results

### Project Development Objective Indicators

#### ► Water users provided with new/improved irrigation and drainage services (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	120000.00
Date	--	--	--	--

#### ▲ Water users provided with irrigation and drainage services - female (number) (Number, Core Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40000.00
Date	--	--	--	--

#### ► Area provided with irrigation and drainage services (ha) (Hectare(Ha), Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
--	----------	-------------------	------------------	------------



Value	0.00	0.00	0.00	100000.00
Date	--	--	--	--

▲ Area provided with irrigation and drainage services - Improved (ha) (Hectare(Ha), Core Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100000.00
Date	--	--	--	--

Overall Comments

**Intermediate Results Indicators**

▶ Number of Subprojects where detailed designs and EAs/EMPs are prepared (Component 1, supported by Components 2 and 3) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	--	--	--	--

▶ Incremental irrigation-water added (Component 1) (Cubic Meter(m3), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	870000000.00
Date	--	--	--	--



▶ Operational water user associations created and/or strengthened (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	35.00
Date	--	--	--	--

▶ Client days of training provided (number) (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	24000.00
Date	--	--	--	--

▲ Client days of training provided - Female (number) (Number, Core Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8000.00
Date	--	--	--	--

▶ Number of Subprojects where "Water Information and Communication Technology" (e.g. Remote Sensing, GIS modeling) is developed to help modernize Subproject performance (Component 2) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	--	--	--	--



- Local government units strengthened (via establishing Rural Support Units and Farmer Support Centers) to provide irrigation and agronomic advisory services (Components 2 and 3) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20.00
Date	--	--	--	--

## Overall Comments


**Data on Financial Performance****Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P086592	IBRD-82770	Effective	USD	102.90	102.90	0.00	0.00	102.90	0%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P086592	IBRD-82770	Effective	27-Jun-2013	29-Apr-2014	29-Jan-2015	31-Dec-2021	31-Dec-2021

**Cumulative Disbursements**

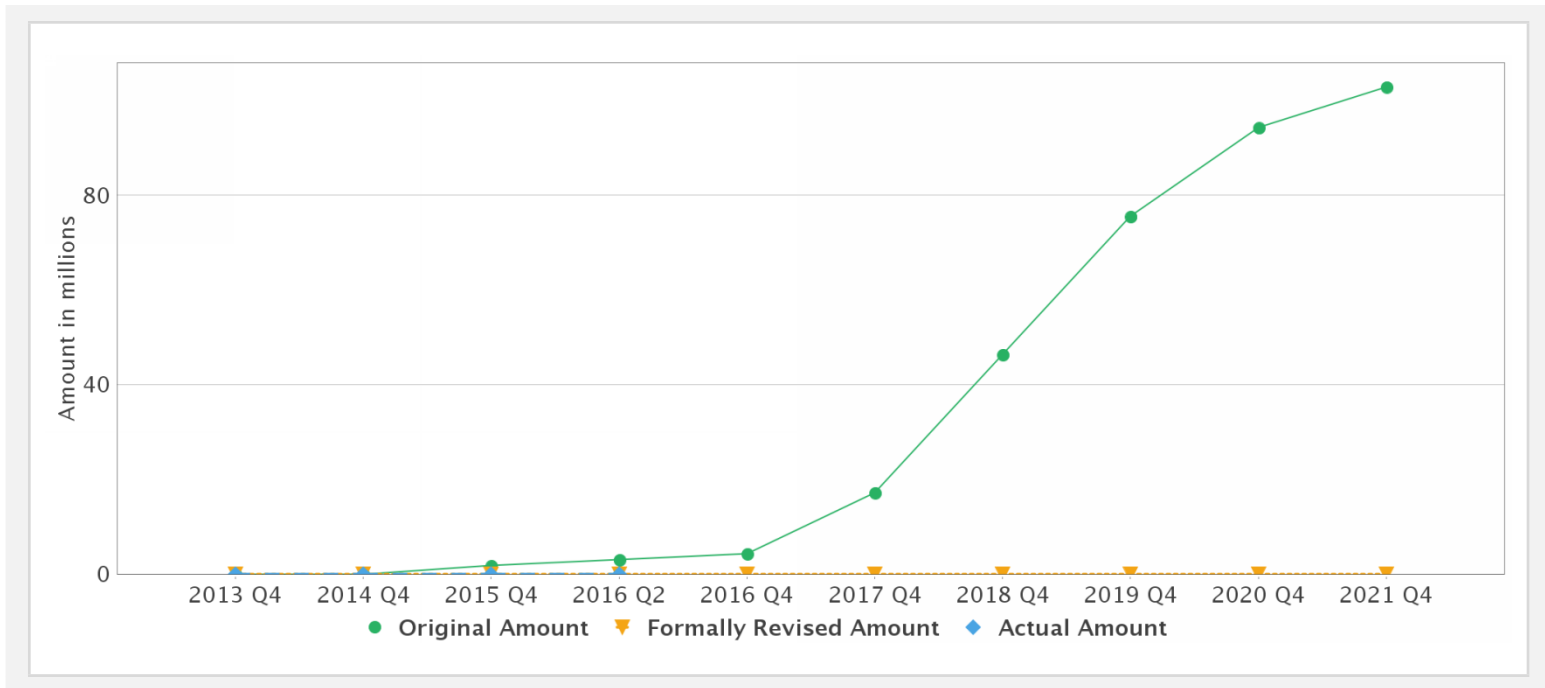

## Restructuring History

There has been no restructuring to date.

## Related Project(s)

There are no related projects.
