



Emergency Multi-Sector Rohingya Crisis Response Project (P167762)

SOUTH ASIA | Bangladesh | Urban, Resilience and Land Global Practice |
IBRD/IDA | Investment Project Financing | FY 2019 | Seq No: 6 | ARCHIVED on 21-Sep-2021 | ISR47863 |

Implementing Agencies: People's Republic of Bangladesh, Local Government Engineering Department, Ministry of Disaster Management and Relief, Department of Public Health Engineering

Key Dates

Key Project Dates

Bank Approval Date: 07-Mar-2019

Effectiveness Date: 09-Jun-2019

Planned Mid Term Review Date: 01-Aug-2022

Actual Mid-Term Review Date:

Original Closing Date: 05-Mar-2022

Revised Closing Date: 30-Jun-2024

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen the Government of Bangladesh systems to improve access to basic services and build disaster and social resilience of the displaced Rohingya population.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

To strengthen the Government of Bangladesh systems to improve access to basic services and build the disaster and social resilience of the population of Cox's Bazar district.

Components Table

Name

Component 1: Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and Gender-Based Violence Prevention:(Cost \$214.00 M)

Component 2: Strengthening Community Resilience:(Cost \$35.00 M)

Component 3: Strengthening Institutional Systems to Enhance Service Provision to the Displaced Rohingya Population:(Cost \$16.00 M)

Component 4: Contingent Emergency Response Component (CERC)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> High

Implementation Status and Key Decisions



The Emergency Multi-Sector Rohingya Crisis Response Project (EMCRP) is being implemented by three implementing agencies: Ministry of Disaster Management and Relief (MoDMR), Local Government Engineering Department (LGED), and Department of Public Health Engineering (DPHE).

The total financing is US\$ 265 million (Grant). The Original Financing is US\$ 165 million (Grant) and additional financing (AF) is US\$ 100 million (Grant).

The AF is focusing on scaling up the activities being implemented by DPHE and LGED, for both the displaced Rohingya Population and host communities. The AF became effective on June 14, 2021.

Implementation of the project is underway. The Project made strong progress towards achieving its objective despite the impact of the COVID-19 lock-down/pandemic.

- Under the mini-piped water supply schemes, the Project completed about 103 km of pipe network (transmission and distribution line) of different diameters. People are getting water from about 1763 tap stands in different camps from these mini-piped water supply schemes. Also, the Project completed the construction of 400 deep tube wells, which are currently operational. Access to improved water sources: 216,300 DRP.
- The Project constructed 2090 household toilets, 500 bio-fil toilets, and 30 community latrines (with composting biogas plants), which are currently operational. Access to improved sanitation: 40,650 DRP.
- Installation of 107 Lightning Protection Systems (LPS) was completed, which protected around 133,357 DRP.
- The Project completed the installation of 967 solar streetlights in different DRP camps.
- Firefighting and search & rescue equipment valued at US\$10.8 million was delivered to the Fire Service and Civil Defense (FSCD) and was put to use in recent fire events in the camps.
- LGED is implementing the gender-Based Violence (GBV) prevention and response component with the support of the United Nations Population Fund (UNFPA). The implementation plan has been finalized, including 12 Women Friendly Spaces (WFS) in camps and 4 in the host community.
- 5,730,231 workdays were generated through community services, 852,234 workdays were generated through community workfare.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	Substantial	Substantial	Substantial
Macroeconomic	Moderate	Moderate	Moderate
Sector Strategies and Policies	High	Moderate	Moderate
Technical Design of Project or Program	Substantial	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	Substantial	Substantial	Substantial
Fiduciary	High	Substantial	Substantial
Environment and Social	High	High	High
Stakeholders	High	High	High
Other	High	High	High
Overall	High	High	High

Results

PDO Indicators by Objectives / Outcomes



Improved access to basic services				
▶ Number of people with access to improved public infrastructure as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	131,000.00	216,300.00	780,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Number of people with access to at least one basic service as a result of this project: street lights, lightning protection, connectivity, water and sanitation, or local markets. Access to improved water sources is considered since it provides the broadest coverage for the DRP as a basic service for the reporting period. So far, the project constructed 1763 tap stands and 400 deep tube wells, each covering 100 users.			
☐ Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	131,000.00	216,300.00	640,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐ Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	68,120.00	112,476.00	332,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐ Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Improved disaster resilience				
▶ Number of people with access to climate resilient multi-purpose disaster shelters as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	81,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	<p>Number of people with access to climate resilient multipurpose disaster shelters/primary schools or climate resilient multipurpose disaster shelters/community service centers, as measured by the design capacity.</p> <p>Currently, the construction of 23 climate-resilient multipurpose disaster shelters/primary schools in two works packages (W-10 and W-11) is ongoing. The physical progress of W-10 and W-11 is 33% and 11%, respectively. Procurement of 22 climate resilient multipurpose disaster shelters/community service centers is currently under evaluation.</p>			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	55,500.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	28,860.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
<input type="checkbox"/> Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25,500.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
<input type="checkbox"/> Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12,750.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024

Improved social resilience				
► Households participating in community workfare and services (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	175,541.00	175,541.00	100,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024



Comments:	Number of eligible households participating in workfare and services activities			
<input type="checkbox"/> Households supported through the participation of DRP women in community workfare and services (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	84,226.00	84,226.00	58,000.00

Strengthened Government systems				
▶ Development of the DRP Camp Management System (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	LGED and DPHE have formed 54 local Grievance Redress Committees (GRCs) are in different camps, and all are functional. UNFPA is implementing the GBV prevention and response component of the project and is handling all GBV-related grievances. For MoDMR part, five types of GRM are in place – (i) a WFP toll-free hotline that directly records all complaints;(ii) site management “info hubs” and information centers;(iii) onsite feedback and complaints collections b cooperation partners, (iv) WFP helpdesk; and (v) Rohingya food-security committee gathers and reports general comments.			

Intermediate Results Indicators by Components

Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and GVB				
▶ Number of people with access to improved water sources as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	131,000.00	216,300.00	365,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Number of people with access to one of the following: mini piped water schemes, deep tube well, or mobile water treatment plant. Liters/person/day: In post-emergency refugee situations, the minimum allocation of water is 20 liters per person per day. This standard covers domestic and individual needs only. Coverage means dwellings no further than 200m from water points up to the maximum design standard (no more than 100 people per water point). 1763 tap stands of mini-piped water schemes and 400 deep tube wells have been constructed each covering 100 users.			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	131,000.00	216,300.00	225,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024



☐Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	68,120.00	112,476.00	117,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
▶ Number of people with access to improved sanitation provided as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	25,050.00	40,650.00	171,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Number of people with access to an improved sanitation solution provided by the project: community latrine or household toilet. Communal latrines compliant with UNHCR standards which require latrines to have cleanable slabs & superstructures, provide privacy, and allow use at any time by all users. 2090 individual toilets, 500 bio-fill latrines each covering 15 users and 30 community latrines with bio-gas plants each covering 60 users are completed and operational.			
☐Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	25,050.00	40,650.00	117,600.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13,026.00	21,138.00	61,152.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024



☐ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	54,200.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
☐ Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	27,100.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
▶ Climate resilient multi-purpose disaster shelters/primary schools constructed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Currently, the construction of 23 climate-resilient multipurpose disaster shelters/primary schools in two works packages (W-10 and W-11) is ongoing. Of which foundation works are completed for eight disaster shelters, and in the remaining sites piling works are continuing. The physical progress of W-10 and W-11 is 33% and 11%, respectively.			
▶ Climate resilient multi-purpose disaster shelters/community service centers constructed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Procurement of 22 climate resilient multipurpose disaster shelters/community service centers is currently under evaluation. The Bank cleared the safeguard screening reports for the finalized locations. Drone and GIS mapping tools came to the aid of designing these disaster shelters during COVID-19 shut down.			
▶ Climate resilient roads improved as a result of this project (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	250.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Ten roads packages have been signed so far. Implementation progress for roads packages W-13, W-14, W-19 and W-20 is reported as 60%, 75%, 28% and 25%, respectively. Site mobilization is ongoing for other packages since contracts for these packages have been signed recently. Four roads packages are at the last stages of procurement (W-21, W-22, W-24 and W-26).			



► Climate resilient access and evacuation bridges constructed as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Two works packages for the construction of Reinforced Cement Concrete (RCC) girder bridges were signed and currently under implementation. Physical progress of these packages (W-8 and W-9) currently stands at 13% and 9%.			
► Lightning protection systems installed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	103.00	107.00	975.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Installation of 107 Early Steamer Emission Lightning Protection Systems is completed in different camps in coordination with SMSD Sector and approval from the respective CICs, which protected 133,357 DRP. Contract for the 268 LPS will be signed by November 30, 2021.			
► Local markets improved (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	For improvement of six (6) Hat Bazars, survey works, screening, and a master plan and architectural design are completed, BoQ and tender documents are being finalized.			
► Solar street lights installed as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	500.00	967.00	4,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Installation of 967 solar streetlights is completed in different camps in coordination with SMSD Sector and approval from the respective CICs. Site identification is going on for the 533 solar streetlights in different DRP camps.			
► Warehouses for firefighting and search & rescue equipment constructed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024



Comments:	FSCD will coordinate with SMSD, camp focal agencies, LGED, CICs and RRRC office for finalizing the 9 locations for warehouses under EMCRP and will get approval from RRRC Office. FSCD will also support and coordinate with LGED for finalizing the design and tender documents of the warehouses.			
► Firefighting and search & rescue equipment provided to FSCD (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	<p>The following equipment procured and delivered to the FSCD:</p> <ul style="list-style-type: none"> • 10000 + 1000 Liter water tender- 5 nos. • Fire and Rescue Vehicle (medium)- 6 nos. • Towing Vehicle (Pick up type with CAF and Water)- 19 nos. • Fire Fighting portable pump (Small)- 15 nos. • Fire Service Command Vehicle- 2nos. • Fire Service Command Vehicle- 2nos. • Ambulance- 5 nos. • Fire Fighting Turn Table- 1 nos. <p>All equipment has been sent to Cox's Bazar, Ukhiya, and Teknaf fire stations and satellite fire stations in the camps and is being used in dousing the frequent fire events inside and outside the camps.</p>			
► Women and girls using GBV services as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	862.00	6,485.00	24,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	<p>Gender Based Violence (GBV) prevention and response component is being implemented by LGED with the support of United Nations Population Fund (UNFPA). The implementation plan has been finalized which includes 12 Women Friendly Spaces (WFS) in camps and 4 in the host community. Among these, 6 WFS sites that have been assessed and approved by LGED, all are now operational. Five new sites have been identified in the DRP camps and are in the approval process, and an additional two are ready for construction once restrictions are lifted. A Vulnerability Assessment has been conducted by UNFPA starting in November 2020 and quantitative data collection is completed. UNFPA has provided trainings to the GBV case workers on various topics such as psychosocial first aid, case management, and suicide prevention.</p>			
► Construction of solar PV nano-grid systems (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	22-Dec-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	<p>Draft design and BoQ for (G-18, G-19 and G-20) supply and Installation of Solar PV Nano Grid Systems have been prepared. Several meetings between the Bank team, LGED team (Energy, GIS, and design team), SMSD, and Energy and Environment Technical Working Group (EETWG) have been held regarding the installation of solar PV nano-grid systems on the rooftops of multi-purpose disaster shelters/community service centers . LGED requested the EETWG to share the beneficiary assessment for the finalized sites of the multi-purpose service centers. Approximately 60 nano-grids of the 100 could be accommodated on the rooftops of multi-purpose disaster shelters/community service centers . LGED</p>			



will take initiative in coordination with SMSD and EETWG on site allocation for the remaining nano-grid schemes.				
► Climate-resilient rubber dams constructed / improved as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	The project has identified the locations of climate-resilient rubber dams sites.			
► Emergency Operations Center (EOC) built (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Architectural and structural drawings of the FSCD building that will house the EoC are almost finalized and estimates have been prepared. LGED has shared the design and drawing with FSCD for review. After getting concurrence from FSCD on the design and BoQ, LGED will move forward with the procurement.			

Strengthening Community Resilience				
► Workdays generated through community services (person-days) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,708,463.00	5,730,231.00	6,000,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Summation of the number of person days generated through community services for all participating beneficiaries. The Project generated 5,730,231 workdays through community services.			
□ Workdays generated through community services (person days) to women (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,441,729.00	2,967,383.00	5,800,000.00
► Workdays generated through community workfare (person-days) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	51,578.00	852,234.00	3,600,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024



Comments:	Summation of the number of person days generated through community workfare for all participating beneficiaries. The Project generated 852,234 workdays through community workfare.
-----------	--

Strengthening Institutional Systems to Enhance Service Provision to the DRP				
► Beneficiaries satisfied with service delivery (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	Share of people satisfied with service delivery, out of a sample of people (not cumulative, measured within a fiscal year). This survey with a sample population is not yet undertaken.			
► Beneficiaries directly reached by communication activities as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	179,205.00	216,300.00	540,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
Comments:	216,300 DRP are reached by service activities financed by the project (access to improved water sources). The project supported awareness program on water and sanitation, hygiene promotion, and Behavior Change Communication (BCC) campaign. Communication and awareness service firm finalized the communication strategy incorporating the comments received from the key public and private stakeholders and developed action plan for implementation of the strategy.			
□ Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	179,205.00	216,300.00	400,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
□ Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	84,259.00	112,476.00	208,000.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024
□ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024





☐ Of which are host community females (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Jan-2021	31-Aug-2021	30-Jun-2024

Performance-Based Conditions

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P167762	IDA-D4190	Effective	USD	165.00	165.00	0.00	83.70	84.77	 50%
P167762	IDA-D5900	Effective	USD	100.00	100.00	0.00	0.00	103.50	 0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P167762	IDA-D4190	Effective	07-Mar-2019	08-May-2019	09-Jun-2019	05-Mar-2022	30-Jun-2024
P167762	IDA-D5900	Effective	31-Mar-2020	19-Nov-2020	14-Jun-2021	30-Jun-2024	30-Jun-2024

Cumulative Disbursements

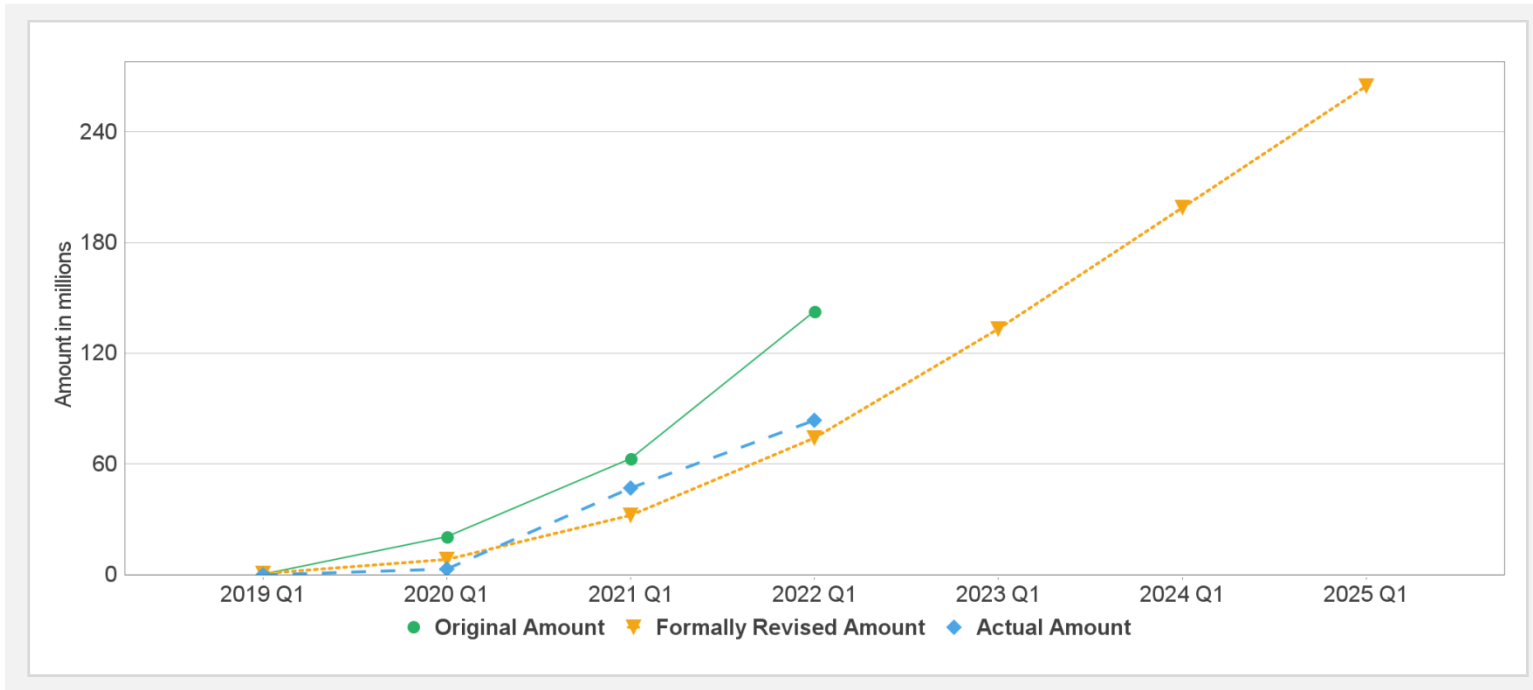

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

There has been no restructuring to date.

Related Project(s)

P171779-Emergency Multi-Sector Rohingya Crisis Response Project Additional Financing
