Implementation Status & Results Congo, Republic of Rep. of Congo - Water, Electricity & Urban Development SIL (LEN) (P106975)

| | o. of Congo - Wate N) (P106975) | r, Electricity & Urban Development SIL | Project Stage: | Implementation | Seq.No: 2 | Status: ARCHIVED | Last Mod | ified Date: 27-Jun-201 |
|------------------------|---|--|----------------|-----------------------|----------------|-------------------|-------------|------------------------|
| | ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | Country: Congo, Republic of | | Approval FY: | 2010 | | | |
| Product Line: IBRD/ID/ | ٩ | Region: AFRICA | | Lending Instr | ument: Specifi | c Investment Loan | | |
| Implementing Agency(| ies): Ministry of Pub | lic Works and Equipment | | | | | | |
| Key Dates | | | | | | | | |
| Board Approval Date | 25-Mar-2010 | Original Closing Date 31-Dec-2015 | Planned | d Mid Term Review Dat | e 20-Aug-20 | 12 Last Archiv | ed ISR Date | 23-Nov-2010 |
| Effectiveness Date | 27-Oct-2010 | Revised Closing Date 31-Dec-2015 | Actual N | Vid Term Review Date | | | | |

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To increase sustainable access to basic infrastructure and safe drinking water for the inhabitants of Brazzaville and Pointe Noire.

Has the Project Development Objective been changed since Board Approval of the Project?

○ Yes ● No

Component(s)

| Component Name | Component Cost | |
|-----------------------------------|----------------|--|
| Urban Infrastructure and Services | 13.50 | |
| Urban Water Supply | 8.80 | |
| Electricity Sector Reform | 0.70 | |

Overall Ratings

| | Previous Rating | Current Rating |
|--------------------------------------|-----------------|----------------|
| Progress towards achievement of PDO | Satisfactory | Satisfactory |
| Overall Implementation Progress (IP) | Satisfactory | Satisfactory |
| Overall Risk Rating | | |

Implementation Status Overview

The project became effective on October 27, 2010, and is off to a good start. This ISR follows the implementation support mission that ended on March 4, 2011. During the first supervision mission, the project team convened representatives of a wide range of stakeholders (including local development committees, community leaders (chefs de quartiers), and civil society) toet their feedback on project implementation. Their feedback was very positive and the objectives of the project are still relevant. Although the project was designed in a participatory approach, these consultations highlighted theeed for (i) increasing communication efforts to better inform beneficiaries and civil society in details about the project

Public Disclosure Copy

Results

(its objectives, intervention zones, possible impacts, expected results, etc.);ii) promoting recruitmentf localouth in construction sites; and (iii) raising theopulation's awareness for protecting and maintaining new/rehabilitated infrastructures, as a way to ensure sustainability of development results after the project.

Project Development Objective Indicators

| Troject Development Objective indicators | | |
|--|------|-----------|
| Indicator Name | Core | Unit of M |
| | | |

| Indicator Name | Core | Unit of Measure | | Baseline | Current | End Target |
|---|--------------|-----------------|----------|----------------------------|-------------|-----------------------------|
| Direct project beneficiaries | \times | Number | Value | 0.00 | 0.00 | 1230000.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Female beneficiaries | \mathbf{X} | Percentage | Value | | | 53.00 |
| | | Sub Type | Date | | | |
| | | Supplemental | Comments | | | |
| Satisfaction of the population with the services provided | | Percentage | Value | | | 75.00 |
| provided | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Number of people in urban areas provided with access to Improved Water Sources under the | \mathbf{X} | Number | Value | 0.00 | 0.00 | 342900.00 |
| project | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | Baseline 704,003.00 people | | Total EoP 1046903.00 people |
| Brazzaville | \times | Number | Value | 460281.00 | 0.00 | 214900.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | Baseline 460,281.00 people | | Total EoP 675,181 people |
| Pointe-Noire | \mathbf{X} | Number | Value | 243722.00 | 0.00 | 128000.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | Baseline 243,722.00 people | | Total EoP 371,722.00 people |
| Number of people in urban areas provided with access to all-season roads within a 500 meter | \mathbf{X} | Number | Value | 0.00 | 0.00 | 200000.00 |
| range under the project | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| People benefitting from improved drainage in areas served by the project | | Number | Value | 0.00 | 0.00 | 200000.00 |
| areas served by the project | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| | - | | | | | |

Public Disclosure Copy

The World Bank

| Indicator Name | Core | Unit of Measure | | Baseline | Current | End Target |
|---|----------|------------------|----------|-------------|-------------|-------------|
| People with access to improved health facilities in targeted areas | | Number | Value | 0.00 | 0.00 | 90000.00 |
| in largeleu aleas | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Pupils with access to improved school facilities in targeted areas. | | Number | Value | 0.00 | 0.00 | 13320.00 |
| in largeleu aleas. | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Annual expenditures on infrastructure maintenance in Brazzaville and Pointe Noire | | Percentage | Value | 2.00 | 2.00 | 6.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| | | | | · | | |
| Intermediate Results Indicators | | | | | | |
| Indicator Name | Core | Unit of Measure | | Baseline | Current | End Target |
| Drainage network constructed / rehabilitated | | Kilometers | Value | 0.00 | 0.00 | 0.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Roads rehabilitated, Non-rural | X | Kilometers | Value | 0.00 | 0.00 | 0.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Health facilities constructed, renovated, and/or equipped | \times | Number | Value | 0.00 | 0.00 | 111.00 |
| odelphoe | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Marketplaces renovated that are fully functionning | | Number | Value | 0.00 | 0.00 | 4.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Surface area of eroded areas treated | | Square Meter(m2) | Value | 0.00 | 0.00 | 0.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |

Public Disclosure Copy

Page 3 of 7

| Indicator Name | Core | Unit of Measure | | Baseline | Current | End Target |
|---|--------------|-----------------|----------|----------------|-------------|-------------|
| Annual increase in towns' own resources municipal taxes and return on municipal | | Percentage | Value | | | 20.00 |
| issets) | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | Not applicable | | |
| mproved community water points constructed or rehabilitated under the project | \mathbf{X} | Number | Value | 0.00 | 0.00 | 175.00 |
| si renabilitated under the project | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Brazzaville | \times | Number | Value | 0.00 | 0.00 | 100.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | | | |
| Pointe-Noire | \mathbf{X} | Number | Value | 0.00 | 0.00 | 75.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | | | |
| New piped household water connections that are resulting from the project intervention | \mathbf{X} | Number | Value | 0.00 | 0.00 | 53000.00 |
| ite resulting from the project intervention | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Brazzaville | \mathbf{X} | Number | Value | 0.00 | 0.00 | 33000.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | | | |
| Pointe-Noire | \mathbf{X} | Number | Value | 0.00 | 0.00 | 20000.00 |
| | | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Breakdown | Comments | | | |
| ength of primary water supply network built in Pointe Noire | | Kilometers | Value | 0.00 | 0.00 | 0.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | | | Comments | | | |
| ength of secondary and tertiary water supply etwork built in each city | | Kilometers | Value | | 0.00 | 0.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | | | Comments | | | |
| Brazzaville | | Kilometers | Value | | 0.00 | 0.00 |

Public Disclosure Copy

Page 4 of 7

Page 5 of 7

| | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
|---|------------|----------|-------------|-------------|-------------|
| | Breakdown | Comments | | | |
| Pointe-Noire | Kilometers | Value | | 0.00 | 0.00 |
| | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | Breakdown | Comments | | | |
| oreholes constructed under the project | Number | Value | 0.00 | 0.00 | 2.00 |
| | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | | Comments | | | |
| New tariff system designed and enforced | Yes/No | Value | No | No | Yes |
| | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | | Comments | | | |
| lew water legal and regulatory framework fully lefined and enforced | Yes/No | Value | No | No | Yes |
| | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2014 |
| | | Comments | | | |
| Connections with operating water meter. | Number | Value | | | |
| | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Comments | | | |
| razzaville | Number | Value | 4.00 | 4.00 | 43.00 |
| | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | Breakdown | Comments | | | |
| Pointe-Noire | Number | Value | 37.00 | 37.00 | 61.00 |
| | Sub Type | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | Breakdown | Comments | | | |
| Collection ratio (cash income/billed revenue) | Percentage | Value | 47.00 | 47.00 | 75.00 |
| | | Date | 31-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Comments | | | |
| Revised SNDE HR management system in blace and operational | Yes/No | Value | No | No | Yes |
| | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | Comments | | | |


| Submission of oprevious year's audit reports to clients by May 15 of each year. | | Yes/No | Value | No | No | Yes |
|---|----------|--------|----------|-------------|-------------|-------------|
| chefts by May 10 of each year. | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Timely certified accounts and financial statements. | | Yes/No | Value | No | No | Yes |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Reform plan for the electricity sector has been prepared | | Yes/No | Value | No | No | Yes |
| propulsa | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Tariff study has been completed. | | Yes/No | Value | No | No | Yes |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Legal framework for the ARSEL has been reviewed and updated. | | Yes/No | Value | No | No | Yes |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Assistance to MEH on budget implementation and ivestment planning completed. | | Yes/No | Value | No | No | Yes |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| Decline in Shortfall of Classrooms at the Primary Level (%) | \times | Number | Value | 0.00 | 0.00 | 111.00 |
| | | | Date | 30-Mar-2010 | 19-May-2011 | 31-Dec-2015 |
| | | | Comments | | | |
| | | | | | | |

Public Disclosure Copy


Data on Financial Performance (as of 14-Jun-2011)

Financial Agreement(s) Key Dates

| Project | Loan No. | Status | | Approval Date | Signing Date | | Effectiveness Da | ate | Closing Date | |
|-------------------------|-----------------------------|-----------|----------|---------------|--------------|-----------|------------------|-----|--------------|-------------|
| P106975 | IDA-47010 | Effective | : | 25-Mar-2010 | 25-May-201 | 0 | 27-Oct-2010 | | 31-Dec-201 | 5 |
| | | | | | | | | | | |
| Disbursement | s (in Millions) | | | | | | | | | |
| Disbursement Project | s (in Millions) Loan No. | Status | Currency | Original | Revised | Cancelled | Disbursed | | Undisbursed | % Disbursed |



Disbursement Graph

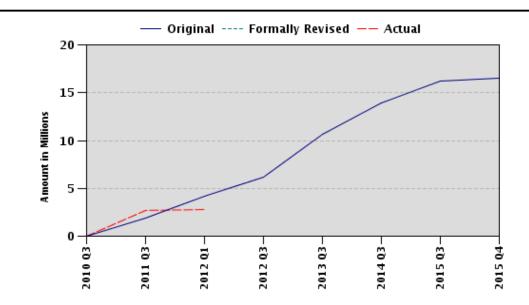

Key Decisions Regarding Implementation

Restructuring History

There has been no restructuring to date.

Related Projects

There are no related projects.
