Implementation Status & Results Report

PK-Balochistan Integrated Water Resources Management & Development Project (P154255)

SOUTH ASIA | Pakistan | Water Global Practice |

IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 12 | ARCHIVED on 23-Dec-2021 | ISR49531 |

Implementing Agencies: Government of Pakistan: Economic Affairs Division, Balochistan Planning and Development Department

Key Dates

Key Project Dates

Bank Approval Date: 28-Jun-2016 Effectiveness Date: 28-Nov-2016

Planned Mid Term Review Date: 04-Nov-2019 Actual Mid-Term Review Date: 28-Jan-2019

Original Closing Date: 31-Oct-2022 Revised Closing Date: 31-Oct-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen provincial government capacity for water resources monitoring and management and to improve community-based water management for targeted irrigation schemes in Balochistan.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Component A: Institutions, Capacity and Information:(Cost \$7.70 M)

Component B: Water, Infrastructure and Management Investments:(Cost \$92.60 M)

Component C: Project Management and Technical Assistance:(Cost \$11.70 M)

Overall Ratings

| Name | Previous Rating | Current Rating |
|--------------------------------------|----------------------------|---------------------------|
| Progress towards achievement of PDO | ■Moderately Unsatisfactory | □ Moderately Satisfactory |
| Overall Implementation Progress (IP) | □Moderately Satisfactory | □ Moderately Satisfactory |
| Overall Risk Rating | □High | □High |

Implementation Status and Key Decisions

Project Implementation has progressed significantly during the current review period from May 2021 to November 2021. Almost all major civil work contracts have been signed and civil works are progressing at a sustained pace despite insecurity challenges and the constraints of the ongoing COVID-19 pandemic.

12/23/2021 Page 1 of 6

Risks

Systematic Operations Risk-rating Tool

| Risk Category | Rating at Approval | Previous Rating | Current Rating |
|--|--------------------|-----------------|----------------|
| Political and Governance | □High | □High | □High |
| Macroeconomic | Substantial | Substantial | Substantial |
| Sector Strategies and Policies | Substantial | Substantial | Substantial |
| Technical Design of Project or Program | Substantial | Substantial | Substantial |
| Institutional Capacity for Implementation and Sustainability | □High | Substantial | Substantial |
| Fiduciary | □High | □High | □High |
| Environment and Social | □Substantial | Substantial | □Substantial |
| Stakeholders | □High | □High | □High |
| Other | □High | □High | □High |
| Overall | □High | □High | □High |

Results

PDO Indicators by Objectives / Outcomes

| Strengthen provincial govt capacity for WRM and improve community-based water management. | | | | | | | | | |
|---|--|---|--|---------------------|--|--|--|--|--|
| ► Irrigable command area with improved water management services (Hectare(Ha), Custom) | | | | | | | | | |
| | Baseline Actual (Previous) Actual (Current) End Target | | | | | | | | |
| Value | 0.00 | 4,000.00 | 10,433.00 | 26,275.00 | | | | | |
| Date | 01-Aug-2016 | 28-Oct-2021 | 06-Dec-2021 | 31-Oct-2022 | | | | | |
| ► Quality-assured hyd | Iro-met data from project basins p Baseline | oublically available in online dat Actual (Previous) | a system (Percentage, Cus Actual (Current) | stom) End Target | | | | | |
| Value | 0.00 | 0.00 | 0.00 | 90.00 | | | | | |
| Date | 01-Aug-2016 | 27-Dec-2019 | 07-Dec-2021 | 30-Jun-2022 | | | | | |
| ▶ Direct project beneficiaries (Number, Custom) | | | | | | | | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target | | | | | |
| Value | 0.00 | 0.00 | 123,400.00 | 414,000.00 | | | | | |

12/23/2021 Page 2 of 6

| Date | 24-Mar-2016 | 27-Dec-2019 | 07-Dec-2021 | 30-Jun-2022 | | | |
|-------------------|---|-------------------|------------------|-------------|--|--|--|
| □Female beneficia | □Female beneficiaries (Percentage, Custom Supplement) | | | | | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target | | | |
| Value | 0.00 | 0.00 | 57,381.00 | 46.50 | | | |

Intermediate Results Indicators by Components

| Component A: Institut | tions, Capacity and Information | | | |
|------------------------|---|--|-----------------------|----------------------|
| omponent / t. mouto | tions, suppostly and information | | | |
| ►Person-days of wa | ter management/planning training | for government staff. (Days, Co | ustom) | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target |
| Value | 0.00 | 15.00 | 15.00 | 500.00 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 27-Dec-2019 | 30-Jun-2022 |
| | | | | |
| | | | | |
| Active climate, stre | eamflow and groundwater monitoring | ng stations. (Number, Custom) | | |
| ► Active climate, stre | eamflow and groundwater monitoring Baseline | ng stations. (Number, Custom) Actual (Previous) | Actual (Current) | End Target |
| | | | Actual (Current) 0.00 | End Target 43.00 |
| Value Date | Baseline | Actual (Previous) | | |
| Value | Baseline 0.00 | Actual (Previous) 0.00 | 0.00 | 43.00 |
| Value Date | Baseline 0.00 | Actual (Previous) 0.00 27-Dec-2019 | 0.00 | 43.00 |
| Value Date | Baseline 0.00 01-Aug-2016 | Actual (Previous) 0.00 27-Dec-2019 | 0.00 | 43.00 |
| Value Date | Baseline 0.00 01-Aug-2016 padmap Document endorsed by the | Actual (Previous) 0.00 27-Dec-2019 e Cabinet. (Text, Custom) | 0.00 27-Dec-2019 | 43.00 31-Oct-2022 |

Component B: Water, Infrastructure and Management Investments

► Area provided with irrigation and drainage services. (Hectare(Ha), Custom)

| | Baseline | Actual (Previous) | Actual (Current) | End Target |
|-------|-------------|-------------------|------------------|-------------|
| Value | 0.00 | 0.00 | 18,800.00 | 50,000.00 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 07-Dec-2021 | 30-Jun-2022 |
| | | | | |

► Water users provided with new/improved irrigation & drainage services (Number, Custom)

12/23/2021 Page 3 of 6

| | Deselles | Astual (Danieus) | A atrial (Originality) | Fod Torret |
|---------------------|---|--------------------------------|------------------------|---------------------|
| Value | Baseline | Actual (Previous) | Actual (Current) | End Target |
| Value | 0.00 | 0.00 | 94,000.00 | 250,000.00 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 07-Dec-2021 | 30-Jun-2022 |
| □Percent Female | (Number, Custom Breakdown) | | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target |
| Value | 0.00 | 30.00 | 30.00 | 30.00 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 27-Dec-2019 | 30-Jun-2022 |
| ►Operational water | user associations created and/or s | strengthened (number) (Numbe | er Custom) | |
| - Operational Water | | | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target |
| Value | 0.00 | 29.00 | 29.00 | 30.00 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 27-Dec-2019 | 31-Dec-2023 |
| | | | | |
| ► Area of watershed | I restored/reforested (Hectare(Ha), | Custom) | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target |
| Value | 1,000.00 | 1,000.00 | 1,100.00 | 4,000.00 |
| | | 07 Day 2010 | 07-Dec-2021 | 31-Oct-2022 |
| Date | 01-Aug-2016 | 27-Dec-2019 | 07 800 2021 | |
| | <u> </u> | | | |
| | 01-Aug-2016 unity drinking water points installed | | | |
| | <u> </u> | | | End Target |
| | unity drinking water points installed | /rehabilitated (Number, Custom | 1) | End Target 10.00 |

| Component C: Project Management and Technical Assistance | | | | | | | | |
|--|---|-------------------|------------------|------------|--|--|--|--|
| ► Surveyed beneficiaries | ► Surveyed beneficiaries satisfied with project implementation (Percentage, Custom) | | | | | | | |
| | Baseline | Actual (Previous) | Actual (Current) | End Target | | | | |
| Value | Value 0.00 0.00 0.00 80.00 | | | | | | | |
| Date | Date 01-Aug-2016 27-Dec-2019 27-Dec-2019 31-Dec-2023 | | | | | | | |

Performance-Based Conditions

12/23/2021 Page 4 of 6

31-Oct-2022

28-Jun-2016

Data on Financial Performance

Disbursements (by loan)

| Project | Loan/Credit/TF | Status | Currency | Original | Revised | Cancelled | Disbursed | Undisbursed | % [| Disbursed |
|-----------|----------------|-----------|--------------|----------|---------|-----------------|-----------|--------------|--------------|-----------|
| P154255 | IDA-58850 | Effective | USD | 200.00 | 110.09 | 89.91 | 38.05 | 70.53 | | 35% |
| Key Dates | (by loan) | | | | | | | | | |
| Project | Loan/Credit/TF | Status | Approval Dat | e Signi | ng Date | Effectiveness D | ate Orig. | Closing Date | Rev. Closing | Date |

28-Nov-2016

31-Oct-2022


31-Aug-2016

Cumulative Disbursements

IDA-58850

Effective

P154255

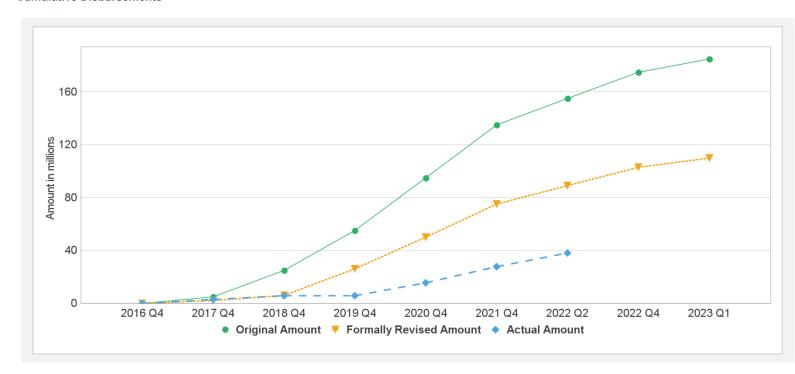

PBC Disbursement

| PBC ID PBC Type Description Coc | PBC Amount Achievement Status | nt Disbursed amount in Coc | Disbursement % for PBC |
|---------------------------------|-------------------------------|----------------------------|------------------------|
|---------------------------------|-------------------------------|----------------------------|------------------------|

12/23/2021 Page 5 of 6

Restructuring History

Level 2 Approved on 26-Jun-2019 ,Level 2 Approved on 27-Sep-2019 ,Level 2 Approved on 12-Nov-2021

Related Project(s)

There are no related projects.

12/23/2021 Page 6 of 6
