



Second Rural Transport Improvement Project (P123828)

SOUTH ASIA | Bangladesh | Transport Global Practice |
IBRD/IDA | Investment Project Financing | FY 2013 | Seq No: 20 | ARCHIVED on 27-Oct-2021 | ISR48799 |

Implementing Agencies: Local Government Engineering Department (LGED), People's Republic of Bangladesh

Key Dates

Key Project Dates

Bank Approval Date: 20-Sep-2012

Effectiveness Date: 28-Nov-2012

Planned Mid Term Review Date: 17-Dec-2015

Actual Mid-Term Review Date: 17-Dec-2015

Original Closing Date: 30-Apr-2018

Revised Closing Date: 30-Dec-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The proposed Project Development Objective is: To improve rural accessibility in project areas (covering 26 districts) and strengthen institutional capacity for sustainable rural road maintenance.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

A. Accessibility Improvement Component:(Cost \$363.19 M)

B.

Institutional Development and Enhancement Component:(Cost \$11.50 M)

C. Rural Transport Safety Component:(Cost \$2.85 M)

D. Contingent Emergency Response Component

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

Implementation Status and Key Decisions

The World Bank has approved the extension of the project's closing date from June 30, 2021 to December 30, 2022, and the Amendment to the Financing Agreement was countersigned by the Government of Bangladesh on May 6, 2021.

As of September 8, 2021, 125 contracts contract have been awarded. 18 contracts (359 km) were completed; and another 16 contracts (224 km) are closer to completion (90-99%).

Overall disbursement amounts to 90 percent of the combined Credits. LGED continues a road safety audit activity but is yet to launch the road safety awareness campaign which has been on hold due to the closure of schools in the country. LGED is also in the procurement process for



recruitment of a consultant to prepare feasibility studies for a follow-on project that would focus on resilience and asset management. Sustainability of infrastructures requires LGED's proactive management oversight and better balance between capital-recurrent expenditure.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Macroeconomic	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Sector Strategies and Policies	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Technical Design of Project or Program	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Institutional Capacity for Implementation and Sustainability	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Fiduciary	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Environment and Social	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Stakeholders	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Other	--	--	--
Overall	--	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

Results

PDO Indicators by Objectives / Outcomes

Improve rural accessibility and strengthen capacity for sustainable rural road maintenance				
►Benefitting population living within 2 km of all season upazila and union roads improved under RTIP2 in 26 project districts (Number in millions) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.10	9.10	9.10
Date	31-Dec-2012	05-Oct-2020	21-Oct-2021	30-Dec-2022
Comments:	PDO revised indicator after restructuring The end target will remain			



sa
me
as
the
bas
elin
e
val
ue
as
no
imp
rov
em
ent
wor
k
will
be
tak
en
und
er
AF
duri
ng
201
9-
22.

► Increase of upazila and union roads under RPM and PBMC sub-components of RTIP II in good condition (IRI below 7) in 26 project districts (5, 861 km of paved roads) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	58.80	58.80	80.00
Date	20-Sep-2012	05-Oct-2020	21-Oct-2021	30-Dec-2022

Comments:
Ye
ar
202
0
dat
a
are
not
yet
due
and
sur
vey
not
yet



co mpl ete d.				
► Increase in level of satisfaction from road users in the project influence area. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3.14	86.00	15.00
Date	12-Oct-2012	05-Oct-2020	21-Oct-2021	30-Dec-2022
Comments:	Satisfaction Base-line:69% Satisfaction End-line: 86% (Survey Completed in March 2021)			
► Increase in maintenance budget needs met for the rural roads (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.35	110.00	10.00
Date	20-Sep-2012	05-Oct-2020	21-Oct-2021	30-Dec-2022
Comments:	Incr eas ed 8.3 5% (co mp are d to bas elin e yea r val ue 11. 76 %) 20. 11 % bud get nee ds met			



in
 201
 9.

The
 re
 has
 been
 a
 3.4
 %
 increase
 in
 budget
 needs
 that
 met
 than
 in
 the
 previous
 year.

(In
 201
 9,
 Needed:
 19,
 695
 .5
 crore)
 Allocation:
 396
 1.5
 crore)

(Need
 for
 FY
 201
 8-
 19
 &
 201
 9-



20 Calculation for year 2020 will be done after receiving allocation for FY 2020-21
 wa 20.11% budget needs met in 2019-20.
 s 42.27 % budget needs met in 2020-2021
 res
 pec
 tive
 ly
 18,
 486
 cr
 &
 20,
 905
 cr)
 (All
 oca
 tion
 for
 FY
 201
 8-
 19
 &
 201
 9-
 20
 wa
 s
 res
 pec
 tive
 ly
 3,2
 18
 cr
 &
 4,7
 05
 cr)

► Increase in population living within 2 km of all season upazila and union roads improved under RTIP II in 26 project districts (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.80	16.41	2.80
Date	20-Sep-2012	28-Jul-2020	21-Oct-2021	30-Apr-2019
Comments:	Indicator was replaced at the time of restructuring			

Intermediate Results Indicators by Components



A. Accessibility Improvement Component				
► Construction of ghats. (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	10.00	10.00	10.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
► Rehabilitation of inland waterways (pilot). (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	47.00	47.00	46.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	Achievement is more than target			
► Rehabilitation and periodic maintenance + Performance Based Maintenance Contract (PBMC) roads. (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,488.70	4,488.70	4,428.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	Achievement is more than target			
► Upgrading of UZR's (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	459.45	459.45	450.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	Achievement is more than target.			
► Improvement of UNRs. (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	417.18	417.18	370.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	Achievement is more than target.			



► Climate-Resilient Rehabilitation of Roads (UZRs and UNRs) (Kilometers) (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	79.67	359.00	1,300.00
Date	31-Dec-2018	05-Oct-2020	21-Oct-2021	30-Dec-2022
Comments:	Additional intermediate indicator added to reflect the AF. Out of 1433 km, works on 79.67 km has been completed, around 1000 km is under procurement and some are on going contracts and 300 km roads are under discussion and to be finalized as per revised proposal from LGED.			
► Percentage of civil works contracts monitored in e-Project Management System (ePMS) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	15.00	60.00	60.00
Date	27-Jan-2021	27-Jan-2021	21-Oct-2021	30-Dec-2022
B. Institutional Development and Enhancement Component				
► Business Plan developed on the Maintenance Policy. (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Draft Policy.	Business Plan Drafted	Business Plan Implemented	Business Plan Operational.
Date	20-Sep-2012	28-Jul-2020	30-Jun-2021	30-Jun-2021
► Implementation of ORA-linked Action Plan. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.00	80.00	80.00	80.00
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
► LGED implementation of comprehensive IT-based maintenance management system (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Functionally limited non-networked RIS	IT-based MMS functional	IT-based MMS functional	IT-based MMS is functional
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
► LGED implementation of Integrated Decision Support System (IDSS). (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	None	Existing PMIS and ePMS software upgraded	Existing PMIS and ePMS software upgraded	Existing PMIS and ePMS software upgraded
Date	20-Sep-2012	05-Oct-2020	30-Jun-2021	30-Jun-2021
► Percentage of women employed in road works (relative to total labor force employed in road construction) (Percentage) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	13.00	13.79	13.79	15.00
Date	12-Jul-2018	05-Oct-2020	30-Jun-2021	30-Jun-2021
► Contractor's workforce trained on ESHS, OHS and GBV Code of Conduct (Percentage) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	12-Jul-2018	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	This endeavor will be taken by SuPRB all over the country. EOI for the consultancy for OHS training has been published in 2021.			
► GRM in place and active at all time in all works contracts (Percentage) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00
Date	12-Jul-2018	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	The GRM developed by the parent project is still active and being followed.			
► Road safety audit carried out for all roads rehabilitated under AF, incorporating safety and security in transportation for women (Percentage) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	10.00	100.00
Date	12-Jul-2018	05-Oct-2020	21-Oct-2021	30-Jun-2021
Comments:	LGED is revising the TORs for the recruitment of a Road Safety Audit as per comments from the WB. Project's D&S Road Safety audit by BUET. But the cost for auditing 100% roads surpasses budget.			
► Sub-projects with participation of direct beneficiaries and project affected people in citizen engagement process (Percentage) (Percentage, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	50.00	50.00	80.00
Date	12-Jul-2018	05-Oct-2020	30-Jun-2021	30-Jun-2021
Comments:	LGED conducts public consultaion with project beneficiaries and project affected people through its sociologists. Cit			

Performance-Based Conditions

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed	
P123828	IDA-51070	Closed	USD	302.00	301.03	0.97	274.74	0.00	<div style="width: 100%; height: 15px; background-color: green;"></div>	100%
P123828	IDA-63270	Effective	USD	100.00	100.00	0.00	63.46	37.26	<div style="width: 63%; height: 15px; background-color: green;"></div>	63%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P123828	IDA-51070	Closed	20-Sep-2012	23-Oct-2012	28-Nov-2012	30-Apr-2018	30-Apr-2019
P123828	IDA-63270	Effective	05-Oct-2018	06-Dec-2018	12-Dec-2018	30-Jun-2021	30-Dec-2022

Cumulative Disbursements

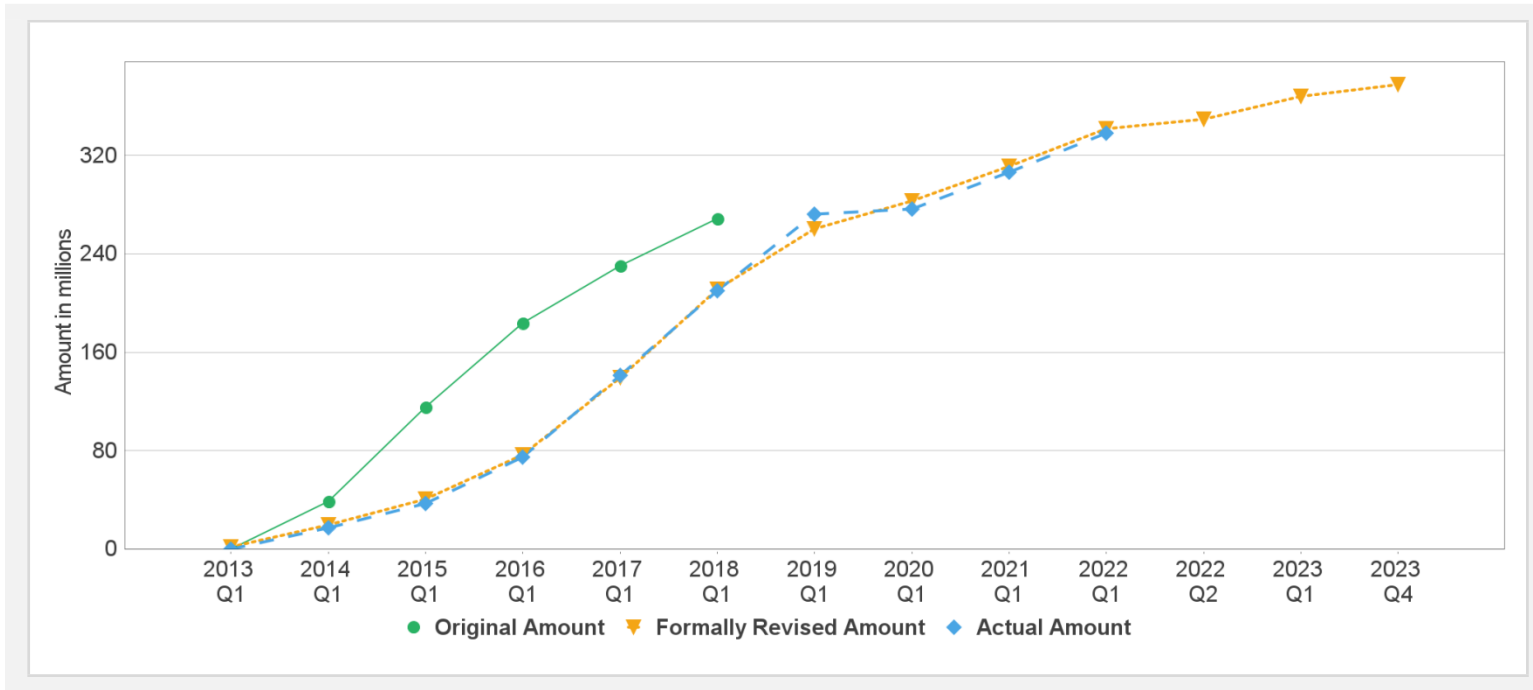

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

Level 2 Approved on 06-Sep-2016 ,Level 2 Approved on 17-Apr-2018 ,Level 2 Approved on 17-Mar-2021

Related Project(s)

P166295-Additional Financing for Second Rural Transport Improvement Project
