



ELECTRICITY ACCESS EXPANSION PROJECT (P151618)

EAST ASIA AND PACIFIC | Solomon Islands | Energy & Extractives Global Practice |
Recipient Executed Activities | Investment Project Financing | FY 2017 | Seq No: 2 | ARCHIVED on 17-May-2017 | ISR27929 |

Implementing Agencies:

Key Dates

Key Project Dates

Bank Approval Date:20-Jul-2016

Effectiveness Date:02-Nov-2016

Original Closing Date:30-Jun-2018

Revised Closing Date:30-Jun-2018

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to increase access to electricity services in low-income areas of Solomon Islands.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Satisfactory

Implementation Status and Key Decisions

The project was approved in July 20, 2016. It was declared effective and implementation formally commenced on November 2, 2016. The first connections were completed in January 2017 and project implementation is expected to accelerate over the next few months.



Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	● Moderate	● Substantial

Comments

There is substantial risk linked to the institutional capacity for implementation. SP has been advised to recruit a project manager asap.

Results

Project Development Objective Indicators

►Direct project beneficiaries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	91.00	14,620.00
Date	05-Apr-2016	30-Nov-2016	09-May-2017	30-Jun-2018

▲Female beneficiaries (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	44.00	7,050.00

►People in urban and peri urban areas of Honiara provided with access to electricity by household connection -Grid (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	91.00	12,113.00
Date	30-Apr-2016	30-Nov-2016	09-May-2017	30-Jun-2018



► People provided with access to electricity from minigrid connections by household connection - Other renewable sources (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2,507.00
Date	30-Apr-2016	30-Nov-2016	09-May-2017	30-Jun-2018

Overall Comments

Intermediate Results Indicators

► Community contribution in the total project costs (percentage) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	400.00	234,500.00
Date	04-May-2016	30-Nov-2016	09-May-2017	30-Jun-2018

▲ Total community contribution (US\$) (Amount(USD), Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	400.00	234,500.00




►Number of LED bulbs distributed and installed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,250.00
Date	04-May-2016	30-Nov-2016	09-May-2017	30-Jun-2018

Overall Comments

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P151618	TF-A2923	Effective	USD	2.23	2.23	0.00	0.01	2.21	 1%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P151618	TF-A2923	Effective	20-Jul-2016	15-Aug-2016	02-Nov-2016	30-Jun-2018	30-Jun-2018

Cumulative Disbursements

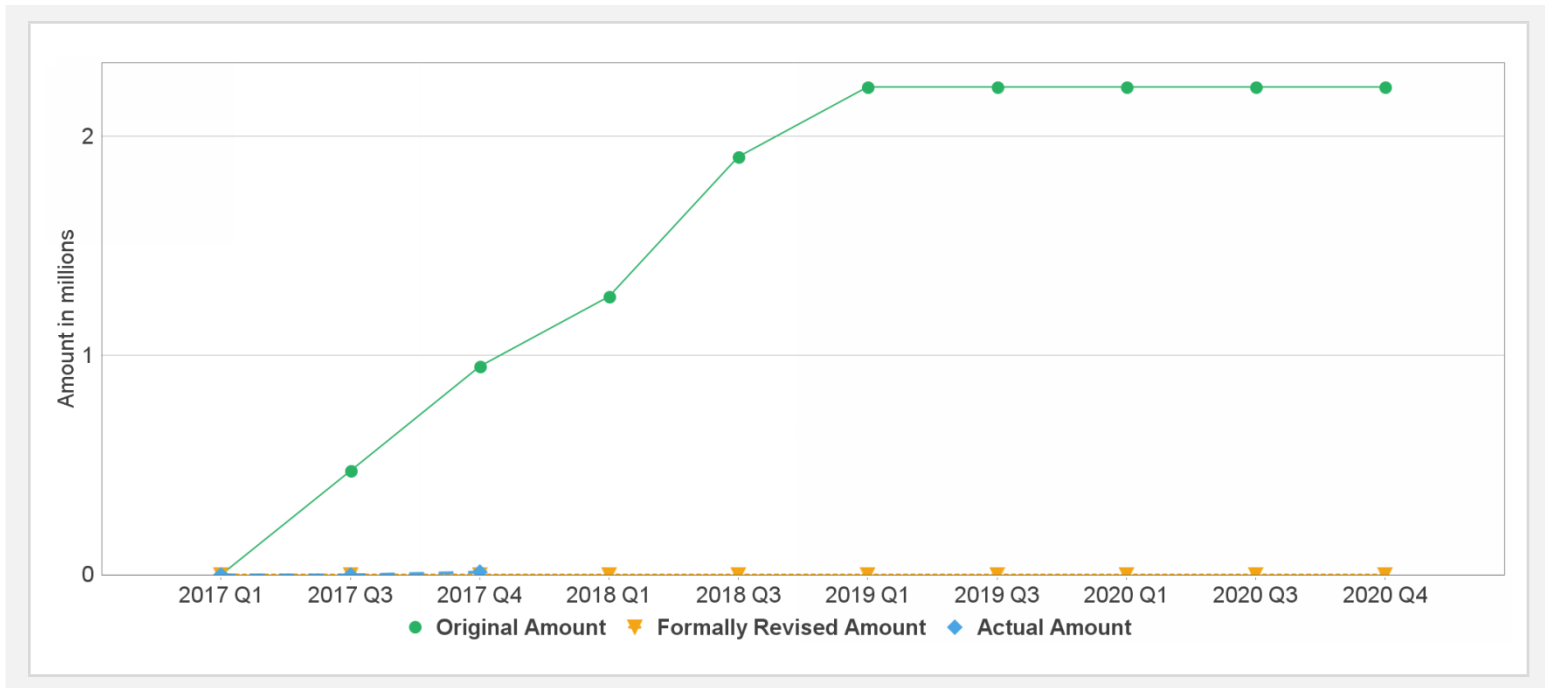

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
