



## Myanmar Flood and Landslide Emergency Recovery Project (P158194)

EAST ASIA AND PACIFIC | Myanmar | Social, Urban, Rural and Resilience Global Practice Global Practice | IBRD/IDA | Investment Project Financing | FY 2017 | Seq No: 1 | ARCHIVED on 13-Oct-2016 | ISR24912 |

Implementing Agencies: Ministry of Agriculture, Livestock, and Irrigation, Ministry of Construction

## Key Dates

## Key Project Dates

Bank Approval Date:14-Jul-2016

Effectiveness Date:--

Planned Mid Term Review Date:15-Jan-2019

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2021

Revised Closing Date:31-Dec-2021

## Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To support the recovery in priority areas affected by the 2015 floods and landslides in Myanmar and, in the event of another Eligible Crisis or Emergency, to provide immediate and effective response to said Eligible Crisis or Emergency.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

## Components

Name

Component 1: Resilient Rehabilitation of National Roads:(Cost \$105.00 M)

Component 2: Resilient Rehabilitation of Rural Roads and Livelihoods Support:(Cost \$70.00 M)

Component 3: Provision of Eligible Goods:(Cost \$15.00 M)

Component 4: Project Management and Knowledge Support:(Cost \$10.00 M)

Component 5: Contingent Emergency Response

## Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory



Overall Risk Rating

--

● Substantial

## Implementation Status and Key Decisions

The project is in the early stages of implementation. Progress toward meeting effectiveness conditions is ongoing and the project is on track to enter effectiveness in November 2016.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● High	--	● High
Macroeconomic	● Moderate	--	● Moderate
Sector Strategies and Policies	● Moderate	--	● Moderate
Technical Design of Project or Program	● Substantial	--	● Substantial
Institutional Capacity for Implementation and Sustainability	● High	--	● High
Fiduciary	● High	--	● High
Environment and Social	● Moderate	--	● Substantial
Stakeholders	● Substantial	--	● Substantial
Other	● Substantial	--	● Substantial
Overall	● Substantial	--	● Substantial

## Results

### Project Development Objective Indicators

#### ► Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1154500.00
Date	17-Oct-2016	--	--	31-Dec-2021

#### ▲ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
--	----------	-------------------	------------------	------------



Value	0.00	--	0.00	50.00
-------	------	----	------	-------

► Length of road rehabilitated (rural/non-rural) (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	555.00
Date	17-Oct-2016	--	--	31-Dec-2021

► Number of workdays generated (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	865000.00
Date	17-Oct-2016	--	--	31-Dec-2021

▲ Workdays generated by women (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	50.00

Overall Comments

**Intermediate Results Indicators**



► Roads rehabilitated, Non-rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	155.00
Date	17-Oct-2016	--	--	31-Dec-2021

► Improved disaster and climate resilient designs and standards for national roads developed (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	17-Oct-2016	--	--	31-Dec-2021

► Roads rehabilitated, Rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	400.00
Date	17-Oct-2016	--	--	31-Dec-2021

► Length of road maintained (rural) (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	300.00
Date	17-Oct-2016	--	--	31-Dec-2021



► Goods procured and distributed as outlined in the CERIP (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	01-Sep-2016	--	--	31-Dec-2021

► Grievances registered related to delivery of project benefits addressed (%) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	95.00
Date	17-Oct-2016	--	--	31-Dec-2021

Overall Comments

## Data on Financial Performance


### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P158194	IDA-58890	Not Effective	XDR	142.60	142.60	0.00	0.00	142.60	0%

### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P158194	IDA-58890	Not Effective	14-Jul-2016	--	--	31-Dec-2021	31-Dec-2021

### Cumulative Disbursements

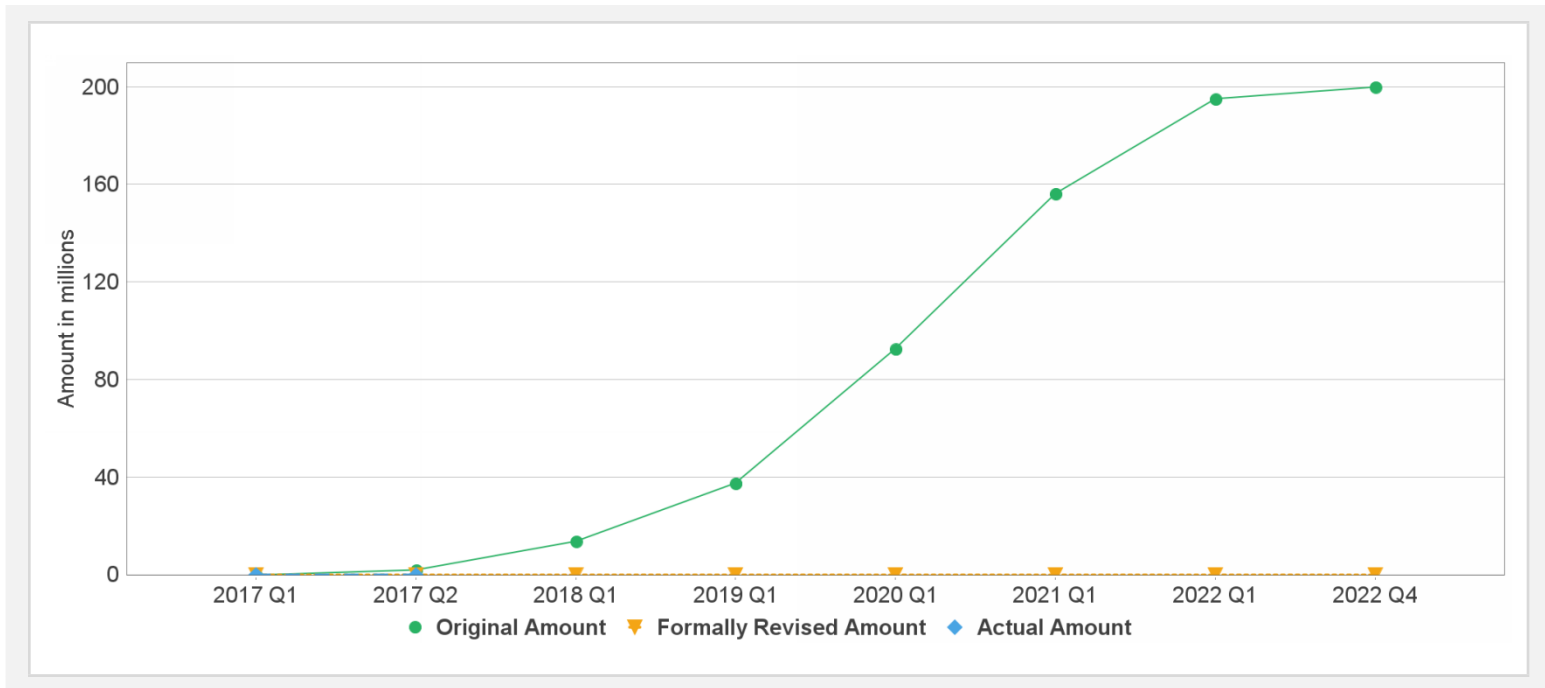

## Restructuring History

There has been no restructuring to date.

## Related Project(s)

There are no related projects.
