Implementation Status & Results Report

Honduras Tropical Cyclones Eta and Iota Emergency Recovery Project (P175977)

LATIN AMERICA AND CARIBBEAN | Honduras | Urban, Resilience and Land Global Practice | IBRD/IDA | Investment Project Financing | FY 2021 | Seq No: 3 | ARCHIVED on 07-Apr-2022 | ISR50633 |

Implementing Agencies: Republic of Honduras, SEDECOAS (Secretaría de Desarrollo Comunitario, Agua y Saneamiento)

Key Dates

Key Project Dates

Bank Approval Date: 18-Dec-2020 Effectiveness Date: 04-Jun-2021

Planned Mid Term Review Date: -- Actual Mid-Term Review Date:

Original Closing Date: 31-Dec-2026 Revised Closing Date: 31-Dec-2026

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to support Honduras' response and recovery needs and strengthen institutional capacity to manage a resilient and inclusive recovery and reconstruction.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Component 1: Emergency relief, response and public health and safety operations: (Cost \$17.30 M)

Component 2: Resilient rehabilitation and reconstruction of public and community infrastructure and

resumption of public services:(Cost \$121.70 M)

Component 3: Institutional support to the Government recovery and reconstruction program: (Cost \$11.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	□Satisfactory	Satisfactory
Overall Implementation Progress (IP)	□Satisfactory	Moderately Satisfactory
Overall Risk Rating	□Substantial	Substantial

Implementation Status and Key Decisions

The Project was approved by the World Bank on December 18, 2020. The Project Financing Agreement was signed on March 9 and became effective on June 4, 2021. The Government has established the Project Implementation Unit and is finalizing the safeguards instruments. The government transition resulting from the November 2021 elections has impacted the progress of project activities although these are expected to resume promptly now that the new Minister for the Fondo Hondureno de Inversion Social/SEDECOAS has been appointed.

4/7/2022 Page 1 of 7

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	Substantial	Substantial	Substantial
Macroeconomic	Substantial	Substantial	Substantial
Sector Strategies and Policies	□Moderate	Substantial	Substantial
Technical Design of Project or Program	□Moderate	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	□High	□High	□High
Fiduciary	□High	□High	□High
Environment and Social	□High	□High	□High
Stakeholders	Substantial	Substantial	Substantial
Other	Substantial	Substantial	Substantial
Overall	□Substantial	□Substantial	□Substantial

Results

PDO Indicators by Objectives / Outcomes

Support Honduras' response and recovery needs

	Baseline	Actual (Previous)	Actual (Current)	End Target
alue	0.00	0.00	0.00	100,000.00
Pate	09-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026
Comments:		measure the number of people be of services from the GoH financed	•	elihoods through emerge
□Percentage of whi	ch are women (Percentage, Cu	stom Supplement)		
□Percentage of whi	ch are women (Percentage, Cu Baseline	stom Supplement) Actual (Previous)	Actual (Current)	End Target
□Percentage of whi	ch are women (Percentage, Cu	stom Supplement)		
ue	Baseline 0.00	Actual (Previous) 0.00	Actual (Current) 0.00	End Target 48.00
Value	Baseline	Actual (Previous) 0.00	,	-

4/7/2022 Page 2 of 7

Value	0.00	0.00	0.00	TBD			
December to the configuration of the configuration							
People benefiting from	n restored public services in a i	resilient manner (Number, Cust	om)				
	Baseline	Actual (Previous)	Actual (Current)	End Target			
/alue	0.00	0.00	0.00	800,000.00			
Pate	09-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026			
comments:	This indicator will measure the number of people benefiting from restored public services in a resilient manner financed by this Project.						
	,						
□Percentage of which	are women (Percentage, Cust	tom Supplement)					
□Percentage of which	,	tom Supplement) Actual (Previous)	Actual (Current)	End Target			
□Percentage of which	are women (Percentage, Cust		Actual (Current)	End Target 48.00			
Value	are women (Percentage, Cust Baseline	Actual (Previous) 0.00	,				
Value	are women (Percentage, Cust Baseline 0.00	Actual (Previous) 0.00	,				

strengthen institutional capacity to manage resilientand inclusive reconstruction and recovery from

► Local recovery participatory planning processes (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target		
Value	0.00	0.00	0.00	20.00		
Date	09-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026		
Comments:	This indicator will measure the number of local recovery participatory planning processes. Local planning process might include, among others local stakeholders, local governments and organizations of IPs and ADs.					

Overall Comments

Under component 1, while there was significant disbursement, the client has yet to come up with an assessment of the beneficiaries of the emergency goods that were reimbursed under the project. There was no progress under Component 2 - as such all related indicators remain the same.

Intermediate Results Indicators by Components

Emergency relief, response and public health and safety operations

▶ People benefiting from food/non food items distribution (Text, Custom)

4/7/2022 Page 3 of 7

	Baseline	Actual (Previous)	Actual (Current)	End Target		
Value	0.00	0.00	0.00	72,000		
Date	09-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2021		
This indicator will measure the number of people benefiting from food-non food items distribution financed by the Project.						
	by the Project.					
	by the Project. h are IPs/ADs (Text, Custom Br	eakdown)				
	, ,	eakdown) Actual (Previous)	Actual (Current)	End Target		
	h are IPs/ADs (Text, Custom Br	,	Actual (Current) 0.00	End Target		

Date	02-1107-2020	12-14161-2021	12-11/101-2021	31-Dec-2020
Resilient rehab. and re	construction of public and comn	nunity infra. and resumption of p	oublic services	
► Number of repaired,	reconstructed or new public inf	rastructure (Number, Custom)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	200.00
Date	09-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026
Comments:	This indicator will n this Project.	neasure the number of repaired	, reconstructed or new publ	ic infrastructure financed b
► People benefiting fro	om restored access to an all-sea	ason road (Text, Custom)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80,000
Date	02-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026
Comments:	This indicator will n financed by the Pro	neasure the number of people b	enefitting from restored acc	cess to an all-season road
□Percentage of which	ch are women (Text, Custom Su	upplement)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	48.00
□Percentage of which	ch are IPs and ADs (Text, Custo	om Breakdown)		
i ercentage of white	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	TBD
Date	02-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026
Date	02-1404-2020	12-IVIQI-202 I	12 WIGH 2021	01-D00-2020

4/7/2022 Page 4 of 7

	Baseline	Actual (Previous)	Actual (Current)	End Target		
/alue	0.00	0.00	0.00	85.00		
Date	02-Nov-2020	12-Mar-2021	12-Mar-2021	31-Dec-2026		
Comments:	This indicator will measure the average citizen satisfaction rate with at least one subproject provided under component 2					

Staff trained in reco	very planning and/or project mar	nagement (Text, Custom)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
/alue	0.00	0.00	0.00	200.00
Date	02-Feb-2021	12-Mar-2021	12-Mar-2021	31-Dec-2026
Comments:	This indicator will m financed by the Pro and local governme	neasure the number of staff trai egject. Trained Staff can include ent personnel.	ned in recovery planning an personnel from the PIU, staf	d/or project management ffrom the PIU institution,
□Percentage of whi	ch are women (Percentage, Cus	tom Supplement)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	48.00
Value	Baseline 0.00	Actual (Previous) 0.00	Actual (Current) 0.00	End Target TBD
Date	02-Feb-2021	12-Mar-2021	12-Mar-2021	31-Dec-2026
	ion and communication outputs r Baseline	Actual (Previous)	Actual (Current)	ustom) End Target 500.00
Value	0.00	0.00	0.00	500.00
Date	01-Feb-2021	12-Mar-2021	12-Mar-2021	31-Dec-2026
Comments:		neasure the number of informat program financed by the Project		
➤ Grievances respond	ded to in the stipulated time (Per	centage, Custom)		

4/7/2022 Page 5 of 7

Value	0.00	0.00	0.00	100.00		
Date	01-Feb-2021	12-Mar-2021	12-Mar-2021	31-Dec-2026		
Comments:	The indicator will measure the proportion of grievances responded to in the stipulated time, as defined by the safeguards documents.					


Performance-Based Conditions

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	%	Disbursed
P175977	IDA-68220	Effective	USD	150.00	150.00	0.00	15.64	134.36		10%
Key Dates	Key Dates (by loan)									
Project	Loan/Credit/TF	Status	Approval Date	e Signi	ng Date	Effectiveness D	ate Orig.	Closing Date	Rev. Closing	Date
P175977	IDA-68220	Effective	18-Dec-2020	08-M	ar-2021	04-Jun-2021	31-De	ec-2026	31-Dec-2026	3

Cumulative Disbursements

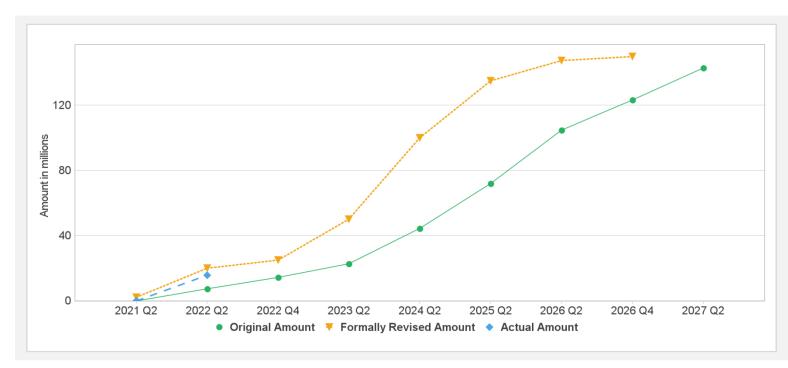

4/7/2022 Page 6 of 7

Restructuring History	R	estr	uctu	rina	His	torv
-----------------------	---	------	------	------	-----	------

Level 2 Approved on 16-Dec-2021

Related Project(s)

There are no related projects.

4/7/2022 Page 7 of 7
