

Log-In Georgia (P169698)

EUROPE AND CENTRAL ASIA | Georgia | Digital Development Global Practice | IBRD/IDA | Investment Project Financing | FY 2021 | Seq No: 1 | ARCHIVED on 23-Nov-2020 | ISR44110 |

Implementing Agencies: Ministry of Economy and Sustainable Development, Communications Commission, Open Net NNLE, Georgia, Ministry of Finance

Key Dates

Key Project Dates

Bank Approval Date: 28-Aug-2020

Planned Mid Term Review Date: 03-Mar-2023

Original Closing Date: 31-Dec-2025

Effectiveness Date: --

Actual Mid-Term Review Date:

Revised Closing Date: 31-Dec-2025

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To increase access to affordable broadband internet, and to promote its use by individuals and enterprises, in selected rural settlements.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Public Disclosure Authorized

Components Table

Name

Increasing access to broadband:(Cost \$76.63 M)

Promoting the use of broadband-enabled digital services:(Cost \$2.50 M)

Project implementation support:(Cost \$0.77 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO		□Satisfactory
Overall Implementation Progress (IP)		□Satisfactory
Overall Risk Rating		□Moderate

Implementation Status and Key Decisions

The progress towards achievement of PDO is Satisfactory given that there are no material risks at this time to undermine achievement of the PDO. The implementation progress is Satisfactory because the key activities related to make the Project effective are progressing, and because the Project Implementing Entity (PIE) and Implementing Agencies (IA) are undertaking preparatory work for various activities financed under the Project.

11/23/2020 Page 1 of 7



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	□Moderate		□Moderate
Macroeconomic	Moderate		□Moderate
Sector Strategies and Policies	Moderate		□Moderate
Technical Design of Project or Program	Moderate		□Moderate
Institutional Capacity for Implementation and Sustainability	Substantial		Substantial
Fiduciary	□Substantial		□Substantial
Environment and Social	□Moderate		□Moderate
Stakeholders	Substantial		Substantial
Other	Substantial		Substantial
Overall	□Moderate		Moderate

Results

PDO Indicators by Objectives / Outcomes

Increased access to broadband internet

► People provided with broad	band internet access (Num	ber (Thousand), Custom)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	400.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Comments:	Total of individuals in	the rural settlements connecte	ed by the Project activities	under Subcomponent 1.1.

Improved affordability of broadband internet

▶ Reduction in unit price of broadband in connected rural settlements (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	50.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025

11/23/2020 Page 2 of 7



Comments:

Reduction in unit price of fixed broadband subscriptions in rural settlements connected to the Open Net network, as compared with 2020 baseline.

Promoting use of broadband-enabled digital services

► Share of individuals in connected rural settlements using the Internet for specific purposes (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	24.00		24.00	50.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Comments:	the Internet for the following	are of individuals surveyed in ng purposes: Seeking health- g for a job or sending a job a	related information; Findir	ng information about

□Share of females in connected rural settlements using the Internet for specific purposes (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	36.00		36.00	70.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025

□ Share of persons with disabilities in connected rural settlements using the Internet for specific purposes (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	10.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025

► Share of enterprises in connected rural settlements using the Internet for specific purposes (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	15.00		15.00	30.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Comments:	settlements that report us electronically (e.g., forms	are of surveyed enterprises (ving the Internet for specific puter for customs or VAT declarational electronic payment, in the second second electronic payment, in the second el	irposes: Had a website; Su on); Declare VAT complete	ubmit completed forms ely electronically without

□ Share of women-owned enterprises in connected rural settlements using the Internet for specific purposes (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00		10.00	20.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025

11/23/2020 Page 3 of 7



Intermediate Results Indicators by Components

_	roadband			
►Length of fiber optic	network cable deployed (route-k	m) (Kilometers, Custom)		
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	5,000.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Comments:	Estimated maximun network design at P	n route kilometers of fiber optic roject appraisal.	cable deployed by the Proj	ect. Estimated based on
►Legal and regulatory Custom)	y instruments to foster competition	n and private investment in ele	ctronic communications ma	rkets adopted (Number,
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	3.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Comments:	infrastructure sharin	nd regulatory instruments by the ig, introduce innovative technol in processes for the construction	ogies and services, set up t	he single information poin
		at in acutified as an army afficient	(Porcontago Custom)	
► Share of installed te	lecommunications equipment that	at is certified as energy efficient	. (Percentage, Custom)	
Share of installed te	Baseline	Actual (Previous)	Actual (Current)	End Target
		-	-	End Target 90.00
/alue	Baseline	-	Actual (Current)	
Value Date	Baseline 0.00 01-Oct-2020 Share of network ec	-	Actual (Current) 0.00 18-Nov-2020 total costs of equipment pro	90.00 31-Dec-2025
Value Date Comments:	Baseline 0.00 01-Oct-2020 Share of network ec	Actual (Previous) quipment installed (by share of by Energy Star or equivalent st	Actual (Current) 0.00 18-Nov-2020 total costs of equipment pro	90.00 31-Dec-2025
Value Date Comments:	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified	Actual (Previous) quipment installed (by share of by Energy Star or equivalent st	Actual (Current) 0.00 18-Nov-2020 total costs of equipment pro	90.00 31-Dec-2025
Value Date Comments: ➤ People provided with	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified h access to the Internet (Number	Actual (Previous) quipment installed (by share of by Energy Star or equivalent st	Actual (Current) 0.00 18-Nov-2020 total costs of equipment proandards.	90.00 31-Dec-2025 ocured under Subcompone
Value Date Comments: ➤ People provided with Value	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified h access to the Internet (Number	Actual (Previous) quipment installed (by share of by Energy Star or equivalent st	Actual (Current) 0.00 18-Nov-2020 total costs of equipment proandards. Actual (Current)	90.00 31-Dec-2025 ocured under Subcompone End Target
Value Date Comments: ▶ People provided with Value Date	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified that access to the Internet (Number Baseline 0.00	Actual (Previous) quipment installed (by share of the	Actual (Current) 0.00 18-Nov-2020 total costs of equipment proandards. Actual (Current) 0.00 18-Nov-2020	90.00 31-Dec-2025 Decured under Subcompone End Target 300,000.00
Value Date Comments: ▶ People provided with Value Date	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified that access to the Internet (Number Baseline 0.00 01-Oct-2020	Actual (Previous) quipment installed (by share of the	Actual (Current) 0.00 18-Nov-2020 total costs of equipment proandards. Actual (Current) 0.00 18-Nov-2020	90.00 31-Dec-2025 Decured under Subcompone End Target 300,000.00
Value Date Comments: ➤ People provided with Value Date	Baseline 0.00 01-Oct-2020 Share of network ed 1.1) that is certified that access to the Internet (Number Baseline 0.00 01-Oct-2020 that benefitted from new access	Actual (Previous) quipment installed (by share of the by Energy Star or equivalent start, Corporate) Actual (Previous) to Internet service. (Number, Corporate)	Actual (Current) 0.00 18-Nov-2020 total costs of equipment proandards. Actual (Current) 0.00 18-Nov-2020 orporate Breakdown)	90.00 31-Dec-2025 Decured under Subcompone End Target 300,000.00 31-Dec-2025

11/23/2020 Page 4 of 7



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	100,000.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
omoting the use of b	proadband-enabled digital service	es		
Number of settleme	ents covered by use-case promot	ion program (Number, Custom)	
	Baseline	Actual (Previous)	Actual (Current)	End Target
alue	0.00		0.00	500.00
ate	01-Oct-2020		18-Nov-2020	31-Dec-2025
omments:	Number of connect	ed rural settlements where acti	vities under Subcomponent	2.2 are conducted
Surveyed beneficia Percentage, Custom	ries of activities offered in Subco	mponents 2.2 and 2.3 who rep	ort that the activities were re	sponsive to their needs
	Baseline	Actual (Previous)	Actual (Current)	End Target
'alue	0.00		0.00	80.00
ate	01-Oct-2020		18-Nov-2020	31-Dec-2025
	This citizen engage	ement indicator will measure the	e share of participants who r	enort being satisfied with
comments:	the responsiveness	s of needs assessment, particip 2 and 2.3 to their needs.		
	the responsiveness	s of needs assessment, particip 2 and 2.3 to their needs.		
	the responsiveness Subcomponents 2.	s of needs assessment, particip 2 and 2.3 to their needs.		
	the responsiveness Subcomponents 2. aries who are women (Percentage	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown)	atory planning and other CE	activities conducted und
□Of which, benefici	the responsiveness Subcomponents 2. aries who are women (Percentage) Baseline	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous)	Actual (Current)	activities conducted und
□Of which, benefici Value Date	the responsiveness Subcomponents 2. Taries who are women (Percentage Baseline 0.00	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous)	Actual (Current) 0.00 18-Nov-2020	End Target 80.00
□Of which, benefici Value Date	the responsiveness Subcomponents 2. Taries who are women (Percentage Baseline 0.00 01-Oct-2020	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous)	Actual (Current) 0.00 18-Nov-2020	End Target 80.00
□Of which, benefici Value Date □Of which, benefici	the responsiveness Subcomponents 2. aries who are women (Percentage Baseline 0.00 01-Oct-2020 01-Oct-	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous) e minorities (Percentage, Custo	Actual (Current) 0.00 18-Nov-2020 m Breakdown)	End Target 80.00 31-Dec-2025
□Of which, benefici Value Date □Of which, benefici Value	the responsiveness Subcomponents 2. aries who are women (Percentage Baseline 0.00 01-Oct-2020 aries who are members of ethnice Baseline	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous) minorities (Percentage, Custo Actual (Previous)	Actual (Current) 0.00 18-Nov-2020 m Breakdown) Actual (Current)	End Target 80.00 31-Dec-2025 End Target
□Of which, benefici Value Date □Of which, benefici Value Date	the responsiveness Subcomponents 2. aries who are women (Percentage Baseline 0.00 01-Oct-2020 daries who are members of ethnica Baseline 0.00	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous) minorities (Percentage, Custo Actual (Previous)	Actual (Current) 0.00 18-Nov-2020 m Breakdown) Actual (Current) 0.00 18-Nov-2020	End Target 80.00 31-Dec-2025 End Target 80.00
□Of which, benefici Value Date □Of which, benefici Value Date	the responsiveness Subcomponents 2. aries who are women (Percentage Baseline 0.00 01-Oct-2020 daries who are members of ethnica Baseline 0.00 01-Oct-2020	s of needs assessment, particip 2 and 2.3 to their needs. ge, Custom Breakdown) Actual (Previous) minorities (Percentage, Custo Actual (Previous)	Actual (Current) 0.00 18-Nov-2020 m Breakdown) Actual (Current) 0.00 18-Nov-2020	End Target 80.00 31-Dec-2025 End Target 80.00

11/23/2020 Page 5 of 7



Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
►Number of benefic	iaries of accessible technologies u	nder Subcomponent 2.3 (Numb	per (Thousand), Custom)	
r tumbor or boriono	ianes of acceptable techniciogies a	ider edbeemperion: 2.0 (i taini	oor (Tribubuna), Gubtom)	
	Danalina	Astrol (Dassisse)	A = t = = 1 (C = = = = = t)	Fred Tarret
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00		0.00	1.000.00
				.,000.00
Date	01-Oct-2020		18-Nov-2020	31-Dec-2025
Date	01-001-2020		10 1407-2020	31-000 2029
Comments:	Number of persons v	vith disabilities that benefit thro	ough accessible technology	provided through the pilot
Comments:	program in Subcomp		-	

Performance-Based Conditions


Data on Financial Performance

Disbursements (by loan)

P169698	IBRD-91610	Not Effective	28-Aug-2020	31-Aı	ıg-2020		31-De	c-2025	31-Dec-2025	
Project	Loan/Credit/TF	Status	Approval Date	e Signi	ng Date	Effectiveness D	oate Orig. (Closing Date	Rev. Closing Date	
Key Dates (by Ioan)										
P169698	IBRD-91610	Not Effective	USD	40.00	40.00	0.00	0.00	40.00	09	
Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disburse	

Cumulative Disbursements

11/23/2020 Page 6 of 7

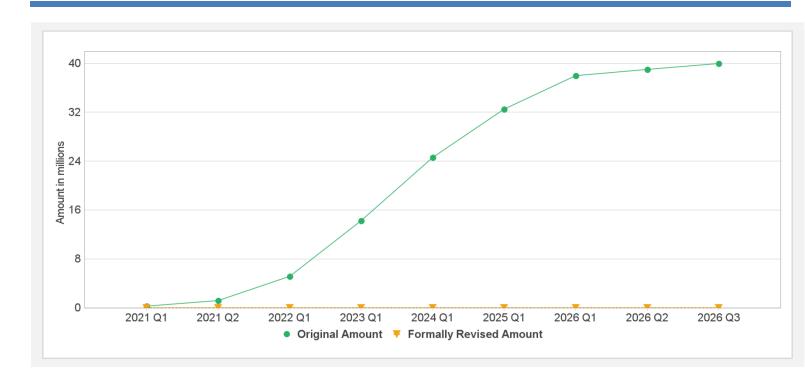

PBC Disbursement

PBC ID PBC Type Description Coc PBC Amount Status Disbursed amount in Coc PBC Amount Status Disbursed amount in Coc PBC

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.

11/23/2020 Page 7 of 7
