Somali Urban Investment Planning (P150374)

AFRICA EAST | Somalia | Urban, Resilience and Land Global Practice |

Recipient Executed Activities | Investment Project Financing | FY 2016 | Seq No: 9 | ARCHIVED on 26-Jan-2021 | ISR45123 |

Implementing Agencies: Ministry of Finance, Mogadishu Municipality, Baidoa Municipality, Kismayo Municipality

Key Dates

Key Project Dates

Bank Approval Date: 04-Feb-2016 Effectiveness Date: 16-Jan-2019

Planned Mid Term Review Date: 22-May-2020 Actual Mid-Term Review Date: 22-May-2020

Original Closing Date: 31-Dec-2021 Revised Closing Date: 31-Dec-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To provide (i) an assessment of the feasibility of, and preliminary plans for, selected urban investment and institutional strengthening activities in southern Somalia, Puntland and Somaliland, and (ii) enhanced project preparation and implementation capacity of participating agencies.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Public Disclosure Authorized

Board Approved Revised Project Development Objective (If project is formally restructured)

To provide: (i) an assessment of the feasibility of, and preliminary plans for, selected urban investment and institutional strengthening activities in targeted cities, and (ii) enhanced project preparation and implementation capacity of participating agencies.

Components Table

Name

Technical Studies:(Cost \$1.94 M)

Project Implementation Capacity Support:(Cost \$1.06 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	□Satisfactory	□Satisfactory
Overall Implementation Progress (IP)	Satisfactory	□Satisfactory
Overall Risk Rating	□High	□High

Implementation Status and Key Decisions

The Somali Urban Investment Planning Project Additional Financing (SUIPP-AF) supports the preparation of feasibility studies and preliminary engineering designs of priority urban investments in the municipalities of Kismayo and Baidoa that will be financed under the Somalia Urban

1/26/2021 Page 1 of 4

Resilience Project Phase II (SURP-II). The project is fully disbursed and despite disbursement delays, all planned activities have been successfully completed or near complete.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	□High	□High	□High
Macroeconomic	Low	Low	□Low
Sector Strategies and Policies	Low	Low	Low
Technical Design of Project or Program	□Moderate	□Moderate	Moderate
Institutional Capacity for Implementation and Sustainability	□High	□High	□High
Fiduciary	□Moderate	□Moderate	□Moderate
Environment and Social	□Low	Low	□Low
Stakeholders	□High	□High	□High
Other	□High	□High	□High
Overall	□High	□High	□High

Results

PDO Indicators by Objectives / Outcomes

Feasibity studies, preliminary and detailed design studies for specific urban investments conducted

▶ Feasibility, preliminary design, and detailed design studies for specific urban investments: secondary roads in Kismayo and Baidoa (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	5.00
Date	28-Aug-2015	15-Jul-2020	21-Jan-2021	31-Dec-2021

Institutional assessments of participating agencies conducted

► Institutional assessments of participating agencies (Number, Custom)

Baseline	Actual (Previous)	Actual (Current)	End Target

1/26/2021 Page 2 of 4

Value	0.00	5.00	5.00	5.00
Date	28-Aug-2015	15-Jul-2020	21-Jan-2021	31-Dec-2021

Project implementation units established in targeted cities

▶ Project implementation units established in targeted cities (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	5.00
Date	28-Aug-2015	15-Jul-2020	21-Jan-2021	31-Dec-2021

Intermediate Results Indicators by Components

Component 1: Technical Studies

▶ Contracting for Feasibility Studies and Institutional Assessments (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4.00	4.00	4.00
Date	01-Mar-2016	15-Jul-2020	21-Jan-2021	31-Dec-2021

Component 2: Project Implementation Capacity Support

▶ Establishment of Project Implementation Units (PIUs) in target cities (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	5.00
Date	01-Mar-2016	15-Jul-2020	21-Jan-2021	31-Dec-2021

Performance-Based Conditions

Data on Financial Performance


Disbursements (by loan)

Project Loan/Credit/TF Status Currency Original Revised Cancelled Disbursed Undisbursed % Disbursed

1/26/2021 Page 3 of 4

P150374	TF-A8878	Effective	USD	1.06	1.06	0.00	1.06	0.00		100%
Key Dates	(by loan)									
Project	Loan/Credit/TF	Status	Approval Date	Signing D	ate E	Effectiveness Date	Orig. Clos	ing Date	Rev. Closing	Date
P150374	TF-A8878	Effective	27-Nov-2018	22-Dec-20	018 1	16-Jan-2019	31-Dec-20)21	31-Dec-2021	l

Cumulative Disbursements

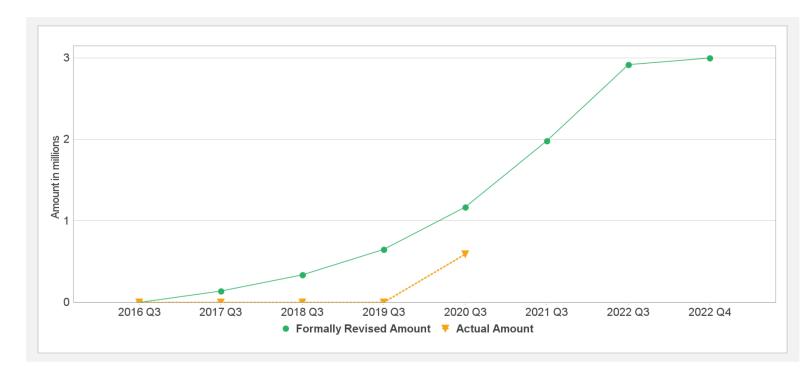

PBC Disbursement

PBC ID	DDC Tyroo	Description	Coo	PBC Amount	Achievement	Disbursed amount in	Disbursement %
FBC ID	гвс туре	Description	Coc	FBC AIIIOUIII	Status	Coc	for PBC

Restructuring History

Level 2 Approved on 06-Jun-2017 ,Level 2 Approved on 08-Dec-2017 ,Level 2 Approved on 04-Jun-2018

Related Project(s)

P166591-Somali Urban Investment Planning Project Additional Financing

1/26/2021 Page 4 of 4
