



## Emergency Multi-Sector Rohingya Crisis Response Project (P167762)

SOUTH ASIA | Bangladesh | Urban, Resilience and Land Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2019 | Seq No: 7 | ARCHIVED on 15-Mar-2022 | ISR50235 |

Implementing Agencies: People's Republic of Bangladesh, Local Government Engineering Department, Ministry of Disaster Management and Relief, Department of Public Health Engineering

### Key Dates

#### Key Project Dates

Bank Approval Date: 07-Mar-2019

Effectiveness Date: 09-Jun-2019

Planned Mid Term Review Date: 01-Feb-2023

Actual Mid-Term Review Date:

Original Closing Date: 05-Mar-2022

Revised Closing Date: 30-Jun-2024

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen the Government of Bangladesh systems to improve access to basic services and build disaster and social resilience of the displaced Rohingya population.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

To strengthen the Government of Bangladesh systems to improve access to basic services and build the disaster and social resilience of the population of Cox's Bazar district.

### Components Table

Name

Component 1: Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and Gender-Based Violence Prevention:(Cost \$214.00 M)

Component 2: Strengthening Community Resilience:(Cost \$35.00 M)

Component 3: Strengthening Institutional Systems to Enhance Service Provision to the Displaced Rohingya Population:(Cost \$16.00 M)

Component 4: Contingent Emergency Response Component (CERC)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> High

### Implementation Status and Key Decisions



The Emergency Multi-Sector Rohingya Crisis Response Project (EMCRP) is being implemented by three implementing agencies: Ministry of Disaster Management and Relief (MoDMR), Local Government Engineering Department (LGED), and Department of Public Health Engineering (DPHE).

The total financing is US\$ 265 million (Grant). The Original Financing is US\$ 165 million (Grant) and Additional Financing (AF) is US\$ 100 million (Grant).

The AF is focusing on scaling up the activities being implemented by DPHE and LGED, for both the displaced Rohingya Population and host communities. The AF became effective on June 14, 2021.

Implementation of the project is underway. The Project made strong progress towards achieving its objective despite the impact of the COVID-19 lock-down/pandemic.

- Under the mini-piped water supply schemes, the project completed about 102 km of pipe network (transmission and distribution line) of different diameters. People are getting water from about 1763 tap stands in different camps from these mini-piped water supply schemes. Also, the project completed construction of 400 deep tube wells, which are currently operational. Access to improved water sources: 216,300 DRP.
- The Project constructed 2,966 household toilets, 500 bio-fill toilets, and 30 community latrines (with composting biogas plants), which are currently operational. Access to improved sanitation: 53,790 DRP.
- Improvement of 17 kilometers climate resilient roads is completed. Out of 17 km climate resilient access roads constructed, about 10km of roads are in host community, which also serve as access roads to the DRP camps.
- Installation of 107 Lightning Protection Systems (LPS) was completed, which protected around 133,357 DRP.
- The project completed the installation of 1,265 solar streetlights in different DRP camps.
- Firefighting and search & rescue equipment valued at US\$10.8 million was delivered to the Fire Service and Civil Defense (FSCD)' Cox's Bazar, Ukhiya, and Teknaf fire stations and satellite fire stations in the camps and was put to use in recent fire events in the DRP camps. This equipment is also being used outside the camps for host communities in Ukhiya, and Teknaf.
- LGED is implementing the Gender-Based Violence (GBV) prevention and response component with the support of United Nations Population Fund (UNFPA). As a result of the project, 10,500 women and girls are using GBV services through seven Women Friendly Spaces (WFS). Out of these seven WFSs, three are outside DRP camps serving 4,500 women and girls from the host community.
- 7,017,206 workdays were generated through community services, 1,656,707 workdays were generated through community workfare.

**Risks**

**Systematic Operations Risk-rating Tool**

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	□ Substantial	□ Substantial	□ Substantial
Macroeconomic	□ Moderate	□ Moderate	□ Moderate
Sector Strategies and Policies	□ High	□ Moderate	□ Moderate
Technical Design of Project or Program	□ Substantial	□ Substantial	□ Substantial
Institutional Capacity for Implementation and Sustainability	□ Substantial	□ Substantial	□ Substantial
Fiduciary	□ High	□ Substantial	□ Substantial
Environment and Social	□ High	□ High	□ High
Stakeholders	□ High	□ High	□ High
Other	□ High	□ High	□ High
Overall	□ High	□ High	□ High

**Results**



PDO Indicators by Objectives / Outcomes

Improved access to basic services				
▶ Number of people with access to improved public infrastructure as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	216,300.00	216,300.00	780,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Number of people with access to at least one basic service as a result of this project: street lights, lightning protection, connectivity, water and sanitation, or local markets. Access to improved water sources is considered since it provides the broadest coverage for the DRP as a basic service for the reporting period. So far, the project constructed 1763 tap stands and 400 deep tube wells, each covering 100 users in DRP camps.			
□ Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	216,300.00	216,300.00	640,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□ Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	112,476.00	112,476.00	332,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□ Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Improved disaster resilience				



▶ Number of people with access to climate resilient multi-purpose disaster shelters as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	81,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	<p>Number of people with access to climate resilient multipurpose disaster shelters/primary schools or climate resilient multipurpose disaster shelters/community service centers, as measured by the design capacity.</p> <p>Currently, the construction of 23 climate-resilient multipurpose disaster shelters/primary schools in two works packages (W-10 and W-11) is ongoing. The physical progress of W-10 and W-11 is 55% and 37%, respectively. Tenders have been floated for 22 climate resilient multipurpose disaster shelters/community service centers as well as 17 multi-purpose disaster shelters.</p>			
☐ Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	55,500.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
☐ Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	28,860.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
☐ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25,500.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
☐ Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12,750.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Improved social resilience				
▶ Households participating in community workfare and services (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	175,541.00	175,541.00	100,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Number of eligible households participating in workfare and services activities			
<input type="checkbox"/> Households supported through the participation of DRP women in community workfare and services (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	84,226.00	84,226.00	58,000.00

<b>Strengthened Government systems</b>				
<b>► Development of the DRP Camp Management System (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	For MoDMR part, five types of GRM are in place – (i) a WFP toll-free hotline that directly records all complaints;(ii) site management “info hubs” and information centers;(iii) onsite feedback and complaints collections b cooperation partners, (iv) WFP helpdesk; and (v) Rohingya food-security committee gathers and reports general comments.			

### Intermediate Results Indicators by Components

<b>Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and GVB</b>				
<b>► Number of people with access to improved water sources as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	216,300.00	216,300.00	365,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Number of people with access to one of the following: mini piped water schemes, deep tube well, or mobile water treatment plant. Liters/person/day: In post-emergency refugee situations, the minimum allocation of water is 20 liters per person per day. This standard covers domestic and individual needs only. Coverage means dwellings no further than 200m from water points up to the maximum design standard (no more than 100 people per water point). 1763 tap stands of mini-piped water schemes and 400 deep tube wells have been constructed each covering 100 users.			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	216,300.00	216,300.00	225,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	112,476.00	112,476.00	117,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<input type="checkbox"/> Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<input type="checkbox"/> Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<b>► Number of people with access to improved sanitation provided as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	40,650.00	53,790.00	171,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Number of people with access to an improved sanitation solution provided by the project: community latrine or household toilet. Communal latrines compliant with UNHCR standards which require latrines to have cleanable slabs & superstructures, provide privacy, and allow use at any time by all users. 2966 individual toilets, 500 bio-fil latrines each covering 15 users and 30 community latrines with bio-gas plants each covering 60 users are completed and operational.			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	40,650.00	53,790.00	117,600.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	21,138.00	27,971.00	61,152.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	54,200.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	27,100.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
▶Climate resilient multi-purpose disaster shelters/primary schools constructed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Currently, the construction of 23 climate-resilient multipurpose disaster shelters/primary schools in two works packages (W-10 and W-11) is ongoing and physical progress of the contract packages is reported 55% and 37% respectively.			
▶Climate resilient multi-purpose disaster shelters/community service centers constructed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	The package W-4: Construction of 22 Multipurpose Community and Service Center (MPSC) is split into 2 packages namely W-4 which includes 10 MPSC and W-4.A which includes 12 MPSC as per the type design. Tenders were floated for these two packages on December 30, 2021.			
▶Climate resilient roads improved as a result of this project (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	17.00	250.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	14 roads packages have been signed so far. Under W-13 and W-14 packages, 1.08 km and 6.380 km road works have been completed. Also, under W-19 and W-20 packages, 2.31 km and 7.11 km road			



works have been completed respectively. Implementation progress for roads packages W-13, W-14, W-19 and W-20 is reported as 80%, 85%, 57% and 75% respectively. Out of 17 km climate resilient access roads constructed, about 10km of roads are in host community, which also serve as access roads to the DRP camps.

► Climate resilient access and evacuation bridges constructed as a result of the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Physical progress of 2 Reinforced Cement Concrete (RCC) girder bridge packages (W-8 and W-9) currently stands at 42% and 48% respectively.			

► Lightning protection systems installed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	107.00	107.00	975.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Installation of 107 Early Steamer Emission Lightning Protection Systems is completed in different camps in coordination with SMSD Sector and approval from the respective CICs, which protected 133,357 DRP. Contract for the 268 LPS will be signed by April 12, 2022.			

► Local markets improved (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	For improvement of 6 Hat Bazars, survey works, screening, and a master plan and architectural design are completed, BoQ and tender documents have been finalized and tender for 3 hat-bazars were floated on December 30, 2021.			

► Solar street lights installed as a result of the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	967.00	1,265.00	4,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Installation of 1265 solar streetlights is completed in different camps in coordination with SMSD Sector and approval from the respective CICs and installation for remaining 235 are underway. Another package for 2500 nos. solar street lights is currently under evaluation.			

► Warehouses for firefighting and search & rescue equipment constructed (Number, Custom)





	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Preliminary locations for 9 satellite fire stations (package W-2) have been identified in coordination with SMSD, UNHCR and IOM. Design of the satellite stations is also completed and FSCD reviewed it. Currently screening reports and BoQ are under preparation. It is agreed that LGED will start the procurement process by March 15, 2022.			
<b>► Firefighting and search &amp; rescue equipment provided to FSCD (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	<p>The following equipment procured and delivered to the FSCD:</p> <ul style="list-style-type: none"> <li>• 10000 + 1000 Liter water tender- 5 nos.</li> <li>• Fire and Rescue Vehicle (medium)- 6 nos.</li> <li>• Towing Vehicle (Pick up type with CAF and Water)- 19 nos.</li> <li>• Fire Fighting portable pump (Small)- 15 nos.</li> <li>• Fire Service Command Vehicle- 2nos.</li> <li>• Fire Service Command Vehicle- 2nos.</li> <li>• Ambulance- 5 nos.</li> <li>• Fire Fighting Turn Table- 1 nos.</li> </ul> <p>All equipment has been sent to Cox's Bazar, Ukhiya, and Teknaf fire stations and satellite fire stations in the camps and is being used in dousing the frequent fire events inside (DRP) and outside the camps (host community).</p>			
<b>► Women and girls using GBV services as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	6,485.00	10,500.00	24,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	The Gender Based Violence (GBV) prevention and response component is being implemented by LGED with the support of the United Nations Population Fund (UNFPA). Since the last mission, there has been good progress. A total of 7 Women Friendly Spaces (WFS) sites are operational. Another two WFS are under construction and will be operational by March 2022.. Out of these seven WFSs, three are outside DRP camps serving 4,500 women and girls from the host community. To date, a total of 129,963 women and girls were reached through UNFPA's programming for both the DRP and surrounding host communities.			
<b>► Construction of solar PV nano-grid systems (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	22-Dec-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024



Comments:	LGED has published the Invitation for Bids for the first package for nano-grid (35 nano-grids) on January 20, 2022. The sites will be finalized by March 2022 and the contractor is expected to be on board by April 2022.			
<b>► Climate-resilient rubber dams constructed / improved as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	The project has identified the locations of climate-resilient rubber dams sites.			
<b>► Emergency Operations Center (EOC) built (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Architectural and structural drawings of the FSCD building that will house the EoC have been finalized and estimates have been prepared. LGED has shared the design and drawing with FSCD for review and got concurrence. It is agreed that LGED will start the procurement process by March 15, 2022.			

<b>Strengthening Community Resilience</b>				
<b>► Workdays generated through community services (person-days) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5,730,231.00	7,017,206.00	6,000,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Summation of the number of person days generated through community services for all participating beneficiaries. The Project generated 7,017,206 workdays through community services.			
<b>□ Workdays generated through community services (person days) to women (Number, Custom Supplement)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,967,383.00	3,541,555.00	5,800,000.00
<b>► Workdays generated through community workfare (person-days) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	852,234.00	1,656,707.00	3,600,000.00



Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Summation of the number of person days generated through community workfare for all participating beneficiaries. The Project generated 1,656,707 workdays through community workfare.			

Strengthening Institutional Systems to Enhance Service Provision to the DRP				
<b>► Beneficiaries satisfied with service delivery (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	Share of people satisfied with service delivery, out of a sample of people (not cumulative, measured within a fiscal year). This survey with a sample population is not yet undertaken.			
<b>► Beneficiaries directly reached by communication activities as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	216,300.00	216,300.00	540,800.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
Comments:	216,300 DRP are reached by service activities financed by the project (access to improved water sources). The project supported awareness program on water and sanitation, hygiene promotion, and Behavior Change Communication (BCC) campaign. Communication and awareness service firm finalized the communication strategy incorporating the comments received from the key public and private stakeholders and developed action plan for implementation of the strategy.			
<b>□ Of which are DRP (Number, Custom Breakdown)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	216,300.00	216,300.00	400,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<b>□ Of which are DRP females (Number, Custom Breakdown)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	112,476.00	112,476.00	208,000.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
<b>□ Of which are host community (Number, Custom Breakdown)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00



Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024
□ Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	31-Aug-2021	31-Jan-2022	30-Jun-2024

### Performance-Based Conditions

#### Data on Financial Performance


##### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P167762	IDA-D4190	Effective	USD	165.00	165.00	0.00	89.51	77.21	54%
P167762	IDA-D5900	Effective	USD	100.00	100.00	0.00	10.63	91.67	10%

##### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P167762	IDA-D4190	Effective	07-Mar-2019	08-May-2019	09-Jun-2019	05-Mar-2022	30-Jun-2024
P167762	IDA-D5900	Effective	31-Mar-2020	19-Nov-2020	14-Jun-2021	30-Jun-2024	30-Jun-2024

### Cumulative Disbursements

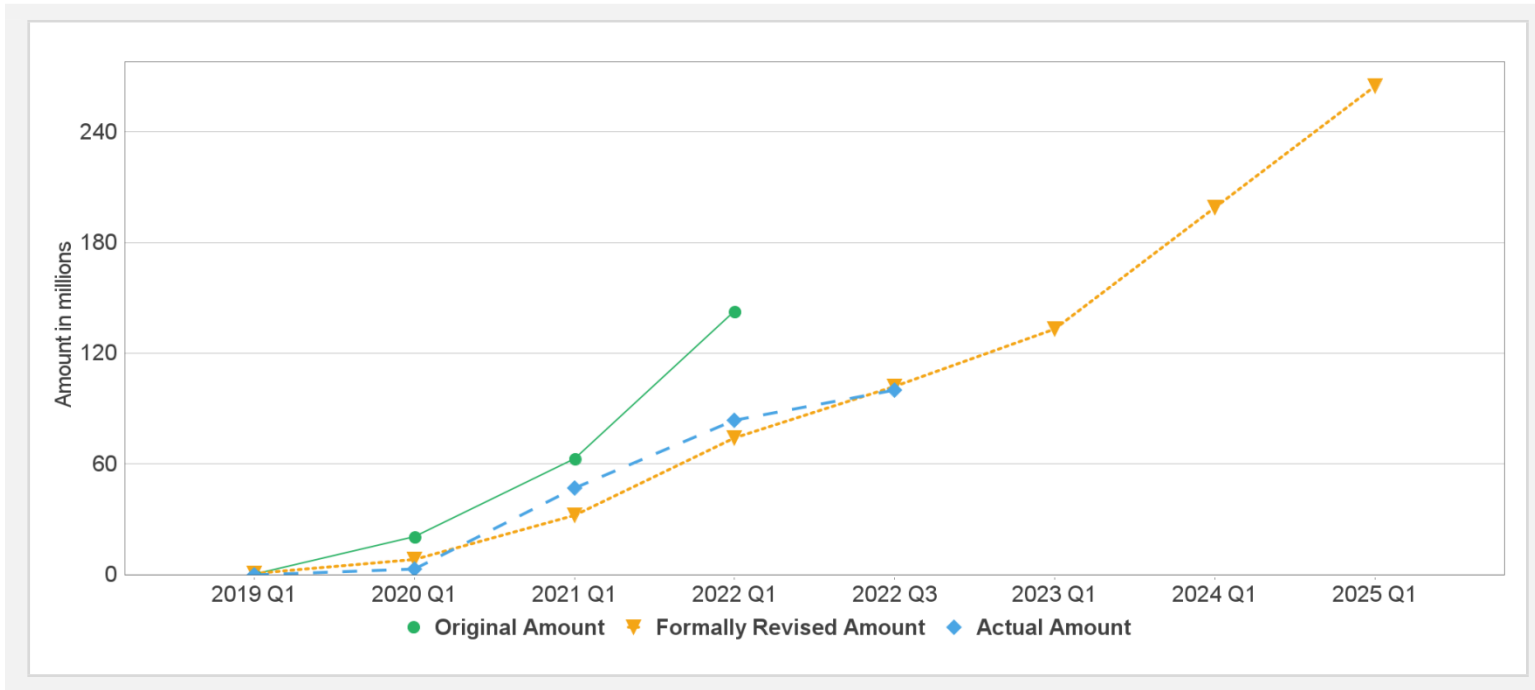

### PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

### Restructuring History

There has been no restructuring to date.

### Related Project(s)

P171779-Emergency Multi-Sector Rohingya Crisis Response Project Additional Financing
