



## Emergency Multi-Sector Rohingya Crisis Response Project (P167762)

SOUTH ASIA | Bangladesh | Urban, Resilience and Land Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2019 | Seq No: 4 | ARCHIVED on 17-Sep-2020 | ISR42837 |

Implementing Agencies: People's Republic of Bangladesh, Local Government Engineering Department, Ministry of Disaster Management and Relief, Department of Public Health Engineering

### Key Dates

#### Key Project Dates

Bank Approval Date: 07-Mar-2019

Effectiveness Date: 09-Jun-2019

Planned Mid Term Review Date: --

Actual Mid-Term Review Date:

Original Closing Date: 05-Mar-2022

Revised Closing Date: 30-Jun-2024

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen the Government of Bangladesh systems to improve access to basic services and build disaster and social resilience of the displaced Rohingya population.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

To strengthen the Government of Bangladesh systems to improve access to basic services and build the disaster and social resilience of the population of Cox's Bazar district.

### Components Table

Name

Component 1: Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and Gender-Based Violence Prevention:(Cost \$214.00 M)

Component 2: Strengthening Community Resilience:(Cost \$35.00 M)

Component 3: Strengthening Institutional Systems to Enhance Service Provision to the Displaced Rohingya Population:(Cost \$16.00 M)

Component 4: Contingent Emergency Response Component (CERC)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> High

### Implementation Status and Key Decisions



In response to a request from the Government of Bangladesh, the World Bank, from the IDA18 Regional Sub-window for Refugees and Host Communities, made available grant-based support for the Emergency Multi-Sector Rohingya Crisis Response Project (Grant Financing of US\$165 million). The project was approved in March 2019.

The Emergency Multi-Sector Rohingya Crisis Response Project (EMCRP) is being implemented by three implementing agencies: Ministry of Disaster Management and Relief (MoDMR), Local Government Engineering Department (LGED) and Department of Public Health Engineering (DPHE).

The World Bank Board approved the project on March 7, 2019. The Financing Agreement was signed on May 8, 2019. The Project has been Effective since June 9, 2019.

The Project underwent restructuring and an Additional Financing (AF) of US\$ 100 million was approved in March 2020. The AF is focusing on scaling up of the activities being implemented by DPHE and LGED, for both the displaced Rohingya Population and host communities. The AF also utilized grant financing from the IDA 18 Regional Sub-window for Refugees and Host Communities.

The total financing is US\$ 265 million (Grant).

Implementation is underway. The project has made strong, early progress towards achieving its objective; however progress has slowed down in recent months due to the COVID-19 lock-down/pandemic.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	Substantial	Substantial	Substantial
Macroeconomic	Moderate	Moderate	Moderate
Sector Strategies and Policies	High	Moderate	Moderate
Technical Design of Project or Program	Substantial	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	Substantial	Substantial	Substantial
Fiduciary	High	Substantial	Substantial
Environment and Social	High	High	High
Stakeholders	High	High	High
Other	High	High	High
Overall	High	High	High

## Results

### PDO Indicators by Objectives / Outcomes

Improved access to basic services

► Number of people with access to improved public infrastructure as a result of the project (Number, Custom)

Baseline

Actual (Previous)

Actual (Current)

End Target



Value	0.00	0.00	0.00	780,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of people with access to at least one basic service as a result of this project: street lights, lightning protection, connectivity, water and sanitation, or local markets.			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	640,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	332,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

Improved disaster resilience

► Number of people with access to climate resilient multi-purpose disaster shelters as a result of the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	81,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of people with access to climate resilient multipurpose disaster shelters/primary schools or climate resilient multipurpose disaster shelters/community service centers, as measured by the design capacity.			

Of which are DRP (Number, Custom Breakdown)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	55,500.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	28,860.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25,500.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12,750.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

**Improved social resilience**

► Households participating in community workfare and services (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

Comments: Number of eligible households participating in workfare and services activities

Households supported through the participation of DRP women in community workfare and services (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	58,000.00

**Strengthened Government systems**

► Development of the DRP Camp Management System (Yes/No, Custom)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	05-Mar-2019	24-Jun-2020	24-Jun-2020	30-Jun-2024
Comments:	Documentation and presentation of the camp governance improvement strategy which entails the strengthening of the camp level capacity and tools, as well as enhancing the DRP volunteer network as the main service interface (for GRM, behavior changing communication and outreach) with the Rohingya population.			

### Intermediate Results Indicators by Components

Strengthening Delivery of Basic Services, Resilient Infrastructure, Emergency Response, and GVB				
▶ Number of people with access to improved water sources as a result of the project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	22,500.00	365,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of people with access to one of the following: mini piped water schemes, deep tube well, or mobile water treatment plant. Liters/person/day: In post-emergency refugee situations, the minimum allocation of water is 20 liters per person per day. This standard covers domestic and individual needs only. Coverage means dwellings no further than 200m from water points up to the maximum design standard (no more than 100 people per water point).			
☐ Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	22,500.00	225,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
☐ Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	11,700.00	117,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
☐ Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
☐ Of which are host community females (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<b>► Number of people with access to improved sanitation provided as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1,500.00	171,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of people with access to an improved sanitation solution provided by the project: community latrine or household toilet. Communal latrines compliant with UNHCR standards which require latrines to have cleanable slabs & superstructures, provide privacy, and allow use at any time by all users.			
<input type="checkbox"/> Of which are DRP (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1,500.00	117,600.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are DRP females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	780.00	61,152.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	54,200.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<input type="checkbox"/> Of which are host community females (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	27,100.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<b>► Climate resilient multi-purpose disaster shelters/primary schools constructed (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00



Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of climate resilient multi-purpose disaster shelters/primary schools constructed (cumulative). Average design capacity per shelter is 1,500 people.			
<b>► Climate resilient multi-pupose disaster shelters/community service centers constructed (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of climate resilient multi-purpose disaster shelters/community service centers improved. A service center is an existing space in the camp providing a public service in the camp, inter alia: relief administration and distribution, childcare, informal education, woman friendly spaces, and information sessions. Each center serves approximately 700 people.			
<b>► Climate resilient roads improved as a result of this project (Kilometers, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	250.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<b>► Climate resilient access and evacuation bridges constructed as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of climate resilient bridges providing access to the camps or the ability to evacuate to a shelter or a medical center constructed under the Project. The total length of the bridges under the project is estimated at 345 m.			
<b>► Lightning protection systems installed (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	975.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of early Steamer Emission Lightning Protection Systems installed in and around the camps to reduce the risk of lightning strikes resulting from extreme hydro-meteorological events. Coverage is estimated as 532,000 people: 0.03 square km (coverage radius 97m); Population density inside the camp: 48,000/ square kilometer			
<b>► Local markets improved (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00



Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of local markets (hat bazars) in and around camps improved including footpaths, lights, water and drainage, and other improvements. The markets are estimated to serve 193,000 people based on 50% of the total population of 11 camps considering that DRP will use existing makeshift markets alongside the roads.			
<b>► Solar street lights installed as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of solar street lights installed to help increase safety and improve energy efficiency. Total 1500 street lights			
<b>► Warehouses for firefighting and search &amp; rescue equipment constructed (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of warehouses constructed in strategic locations for storage and efficient deployment of firefighting and search & rescue equipment			
<b>► Firefighting and search &amp; rescue equipment provided to FSCD (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	The following equipment procured and delivered to the FSCD: 6 fire and rescue vehicles, 15 portable firefighting pumps, 4 fire services command vehicles, 5 ambulances, 6 rescue boats, and 1 firefighting turn table			
<b>► Women and girls using GBV services as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	24,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Using services refers to women and girls who use GBV services including inter alia the following: use psychosocial support activities/sessions (individual, group), participate in GBV information sharing sessions and trainings as part of a service provision activity (including door-to-door), and/or are referred to services (i.e. health). Average coverage per center is estimated at 1,500 women and girls.			
<b>► Construction of solar PV nano-grid systems (Number, Custom)</b>				





	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	22-Dec-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<b>► Climate-resilient rubber dams constructed / improved as a result of the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
<b>► Emergency Operations Center (EOC) built (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

Strengthening Community Resilience				
<b>► Workdays generated through community services (person-days) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	157,649.00	6,000,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Summation of the number of person days generated through community services for all participating beneficiaries			
<b>□ Workdays generated through community services (person days) to women (Number, Custom Supplement)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	32,746.00	5,800,000.00
<b>► Workdays generated through community workfare (person-days) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3,600,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Summation of the number of person days generated through community workfare for all participating beneficiaries			



Strengthening Institutional Systems to Enhance Service Provision to the DRP

► Beneficiaries satisfied with service delivery (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Share of people satisfied with service delivery, out of a sample of people (not cumulative, measured within a fiscal year).			

► Beneficiaries directly reached by communication activities as a result of the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	157,649.00	540,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
Comments:	Number of DRP that are reached by service activities funded by the project. The service activities include the dissemination of face to face messages designed through the project including: points of access for services, gender based violence prevention, hygiene practices, and others.			

☐ Of which are DRP (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	157,649.00	400,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

☐ Of which are DRP females (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	48,655.00	208,000.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

☐ Of which are host community (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	140,800.00
Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024

☐ Of which are host community females (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70,400.00



Date	05-Mar-2019	24-Jun-2020	14-Sep-2020	30-Jun-2024
------	-------------	-------------	-------------	-------------

**Performance-Based Conditions**

**Data on Financial Performance**


**Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P167762	IDA-D4190	Effective	USD	165.00	165.00	0.00	44.61	123.35	27%
P167762	IDA-D5900	Not Effective	USD	100.00	100.00	0.00	0.00	99.49	0%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P167762	IDA-D4190	Effective	07-Mar-2019	08-May-2019	09-Jun-2019	05-Mar-2022	05-Mar-2022
P167762	IDA-D5900	Not Effective	31-Mar-2020	--	--	30-Jun-2024	30-Jun-2024

**Cumulative Disbursements**

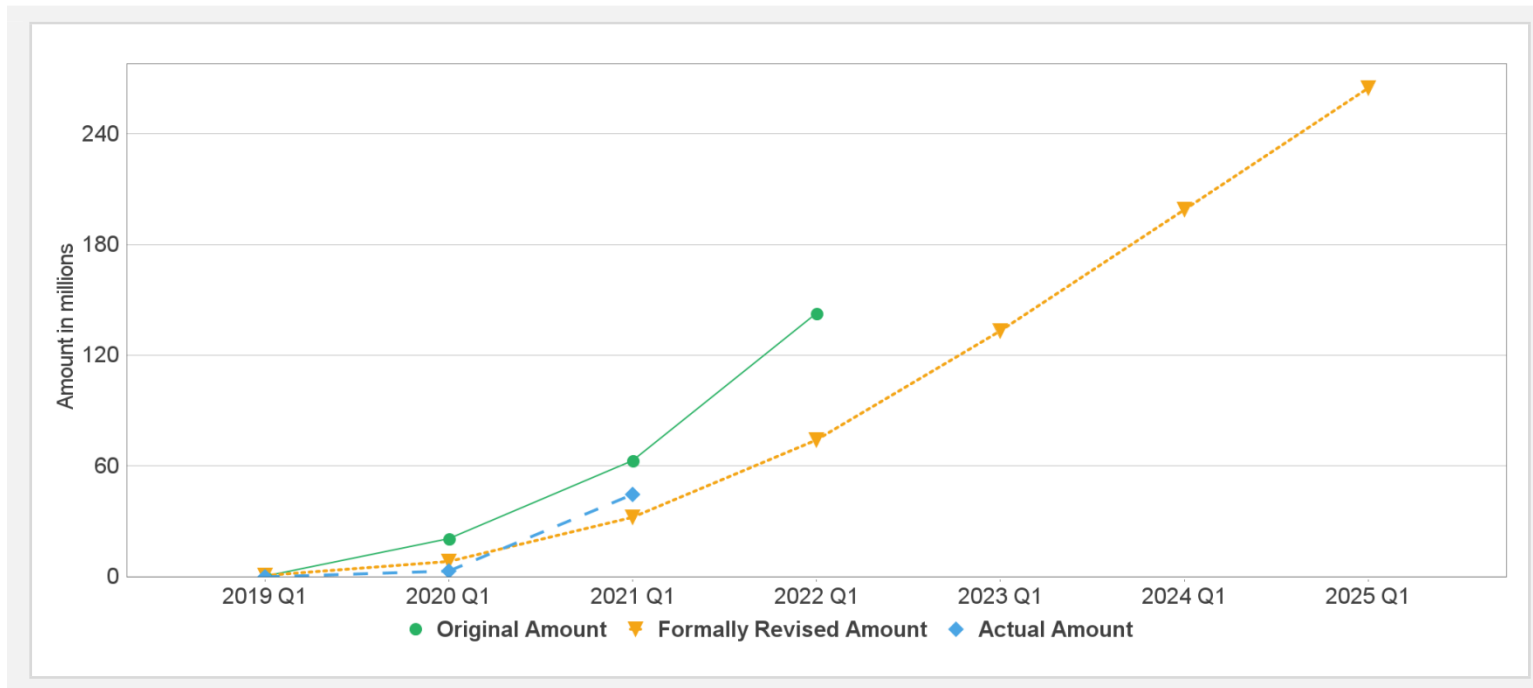



---

### PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

---

### Restructuring History

There has been no restructuring to date.

### Related Project(s)

P171779-Emergency Multi-Sector Rohingya Crisis Response Project Additional Financing

---
