



## Preparation of a Program Towards Sustainable Flood Management in the Greater Metro Manila Area Project (P145237)

EAST ASIA AND PACIFIC | Philippines | Water Global Practice |  
 Recipient Executed Activities | Investment Project Financing | FY 2015 | Seq No: 9 | ARCHIVED on 23-Dec-2020 | ISR45090 |

Implementing Agencies: Department of Public Works and Highways, Department of Finance

**Key Dates****Key Project Dates**

Bank Approval Date: 16-Sep-2014

Effectiveness Date: 19-Jun-2015

Original Closing Date: 31-Jan-2017

Revised Closing Date: 30-Jun-2021

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

The objective is to prepare priority projects, identified by the flood management master plan, that aim to improve flood management and resilience in and around Metro Manila.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory

**Implementation Status and Key Decisions**

Consultants have been recruited to support DPWH with the preparation of feasibility studies and subsequently designs for priority interventions for flood management improvement in the Pasig-Marikina River Basin. Alternatives have been analyzed and final feasibility studies were prepared as per terms of reference. The feasibility studies will allow government to make a decision how to proceed with flood management in the river basin. Draft designs are expected by the end of March 2021. Environmental and social consultants are preparing relevant safeguards documents.

**Risks****Overall Risk Rating**

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

**5. Results**

**Project Development Objective Indicators**

► Proposals for Upper Marikina River structural measures fully designed that are technically, economically, socially, and environmentally sound and that are ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date	22-Dec-2014	31-Dec-2019	30-Nov-2020	30-Jun-2021

► Proposals for an integrated flood forecasting and early warning system fully designed and ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	31-Dec-2019	30-Nov-2020	30-Jun-2021

► Proposals for institutional arrangements for sustainable flood management in the Greater Metro Manila Area acceptable to the Government of the Philippines and key stakeholders and ready for implementa (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	31-Dec-2019	30-Nov-2020	30-Jun-2021

**Intermediate Results Indicators**

► Feasibility study for the proposed interventions in Upper Marikina River completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.00	2.00	2.00
Date	22-Dec-2014	31-May-2019	30-Sep-2020	30-Sep-2020

► Mid-term report with draft proposals for institutional arrangements for sustainable flood management completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	31-Dec-2019	30-Nov-2020	31-Mar-2021

**Data on Financial Performance****Disbursements (by loan)**




Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P145237	TF-18611	Effective	USD	2.73	2.73	0.00	0.52	2.21	19%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145237	TF-18611	Effective	04-Jun-2015	19-Jun-2015	19-Jun-2015	31-Jan-2017	30-Jun-2021

**Cumulative Disbursements**

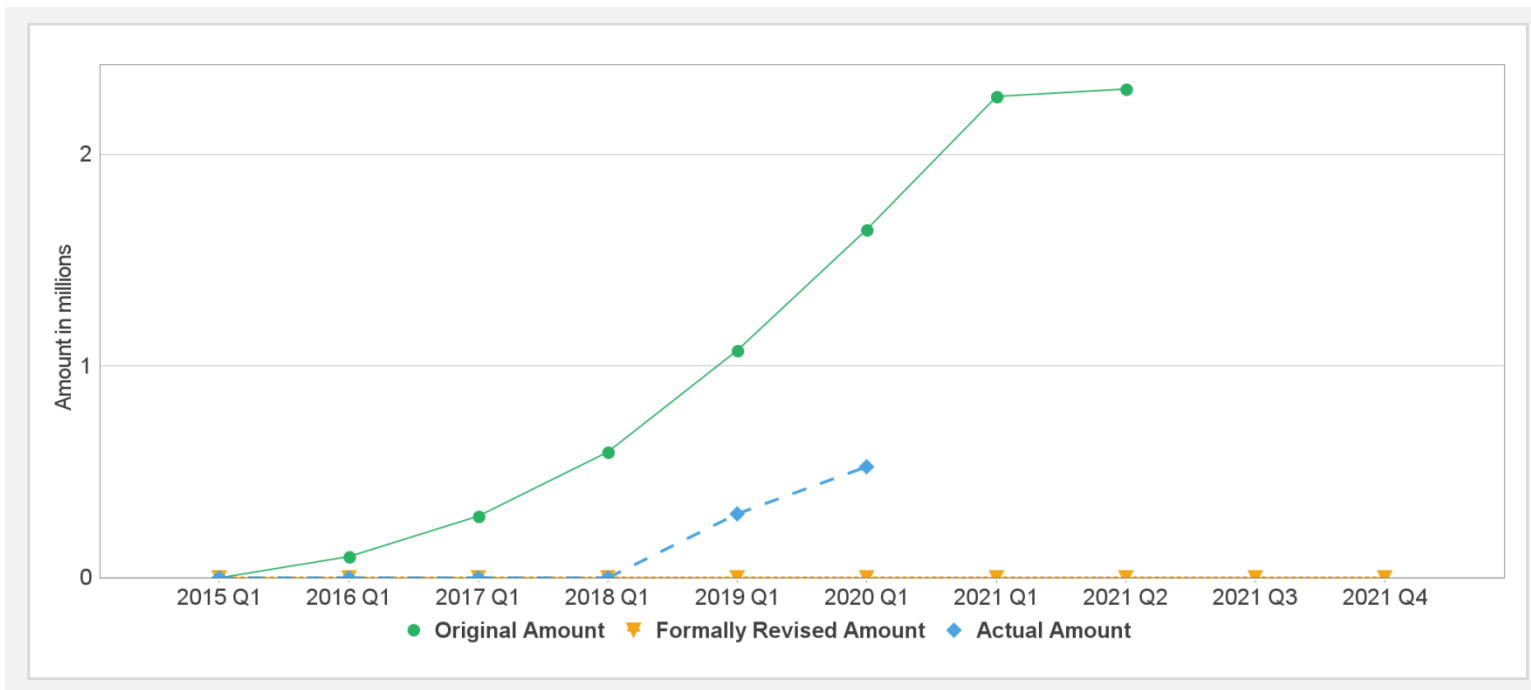

**Restructuring History**

Level 2 Approved on 24-Jan-2017 ,Level 2 Approved on 30-Jan-2018 ,Level 2 Approved on 31-Jan-2020 ,Level 2 Approved on 08-Jul-2020

**Related Project(s)**

There are no related projects.
