

**Implementation Status & Results
Azerbaijan
Second Rural Investment Project (P122944)**

Operation Name: Second Rural Investment Project (P122944)	Project Stage: Implementation	Seq.No: 1	Status: ARCHIVED	Archive Date: 22-Jan-2013
Country: Azerbaijan	Approval FY: 2013			
Product Line: IBRD/IDA	Region: EUROPE AND CENTRAL ASIA	Lending Instrument: Specific Investment Loan		
Implementing Agency(ies): State Agency for Agricultural Credits (SAAC)				

Key Dates

Board Approval Date	05-Jul-2012	Original Closing Date	30-Sep-2017	Planned Mid Term Review Date	Last Archived ISR Date
Effectiveness Date	04-Dec-2012	Revised Closing Date	30-Sep-2017	Actual Mid Term Review Date	

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to improve access to and use of community-driven rural infrastructure and expand economic activities for rural households. This would be achieved through: (i) the provision of grants to finance eligible demand-driven micro-projects in rural infrastructure; (ii) the provision of training and consultants' services to support micro-project development by enhancing the capacity of engaged local stakeholders in all aspects of micro-project program development; (iii) building opportunities for rural employment and livelihood support services through the provision of training and consultants' services to carry out pilot livelihood support services in six communities; and, (iv) supporting project management capacity at the Project Management Unit and its Regional Operations Offices for the purposes of effective management, implementation and monitoring and evaluation of Project activities.

Has the Project Development Objective been changed since Board Approval of the Project?

Yes No

Component(s)

Component Name	Component Cost
Rural Community Infrastructure	18.90
Technical Assistance for Rural Infrastructure	4.73
Project Management and Results Monitoring	6.37

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO		Satisfactory
Overall Implementation Progress (IP)		Satisfactory
Overall Risk Rating		Low

Implementation Status Overview

AzRIP-2 was approved by the Board on July 5, 2012, signed by the Government of Azerbaijan on October 19, 2012 and declared effective as of December 4, 2012. Retroactive

finance has been in place since AzRIP-AF closing date of March 31, 2012. 15 communities have progressed up to training stage (social mobilization complete); 7 CPs up to appraisal stage; 18 CPs in tendering stage; 1 CP up to technical implementation stage and 1 CP completed (Potable Water Supply).

Locations

Country	First Administrative Division	Location	Planned	Actual
Azerbaijan	Beylaqan Rayonu	Beylagan Rayon	✓	
Azerbaijan	Yardimli Rayonu	Yardimli Rayon	✓	
Azerbaijan	Salyan Rayonu	Salyan Rayon	✓	
Azerbaijan	Sabirabad Rayonu	Sabirabad Rayon	✓	
Azerbaijan	Saatli Rayonu	Saatly Rayon	✓	
Azerbaijan	Bilasuvar Rayonu	Bilasuvar Rayon	✓	
Azerbaijan	Neftcala Rayonu	Neftchala Rayon	✓	
Azerbaijan	Masalli Rayonu	Masally Rayon	✓	
Azerbaijan	Lerik Rayonu	Lerik Rayon	✓	
Azerbaijan	Lankaran Rayonu	Lankaran Rayon	✓	
Azerbaijan	Imisli Rayonu	Imishli Rayon	✓	
Azerbaijan	Calilabad Rayonu	Jalilabad Rayon	✓	
Azerbaijan	Astara Rayonu	Astara Rayon	✓	
Azerbaijan	Agcabadi Rayonu	Aghjabadi Rayon	✓	
Azerbaijan	Tartar Rayonu	Tartar Rayon	✓	
Azerbaijan	Zardab Rayonu	Zardab Rayon	✓	
Azerbaijan	Zaqatala Rayonu	Zaqatala Rayon	✓	
Azerbaijan	Yevlax Rayonu	Yevlakh Rayon	✓	
Azerbaijan	Oguz Rayonu	Oghuz Rayon	✓	
Azerbaijan	Ucar Rayonu	Ujar Rayon	✓	
Azerbaijan	Tovuz Rayonu	Tovuz Rayon	✓	
Azerbaijan	Samaxi Rayonu	Shamakhi Rayon	✓	

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Country	First Administrative Division	Location	Planned	Actual
Azerbaijan	Saki Rayonu	Shaki Rayon	✓	
Azerbaijan	Samkir Rayonu	Shamkir Rayon	✓	
Azerbaijan	Kurdamir Rayonu	Kurdamir Rayon	✓	
Azerbaijan	Qabala Rayonu	Qabala Rayon	✓	
Azerbaijan	Qusar Rayonu	Qusar Rayon	✓	
Azerbaijan	Quba Rayonu	Quba Rayon	✓	
Azerbaijan	Xacmaz Rayonu	Khachmaz Rayon	✓	
Azerbaijan	Qazax Rayonu	Qazakh Rayon	✓	
Azerbaijan	Goranboy Rayonu	Goranboy Rayon	✓	
Azerbaijan	Qax Rayonu	Qakh Rayon	✓	
Azerbaijan	Ismayilli Rayonu	Ismayilli Rayon	✓	
Azerbaijan	Goycay Rayonu	Goychay Rayon	✓	
Azerbaijan	Daskasan Rayonu	Dashkasan Rayon	✓	
Azerbaijan	Balakan Rayonu	Balakan Rayon	✓	
Azerbaijan	Barda Rayonu	Barda Rayon	✓	
Azerbaijan	Abseron Rayonu	Absheron Rayon	✓	
Azerbaijan	Agsu Rayonu	Aghsu Rayon	✓	
Azerbaijan	Agdas Rayonu	Aghdash Rayon	✓	
Azerbaijan	Gadabay Rayonu	Gadabay Rayon	✓	
Azerbaijan	Agstafa Rayonu	Aghstafa Rayon	✓	
Azerbaijan	Qobustan Rayonu	Gobustan Rayon	✓	
Azerbaijan	Samux Rayonu	Samukh Rayon	✓	
Azerbaijan	Siyazan Rayonu	Siazan Rayon	✓	
Azerbaijan	Xizi Rayonu	Khizi Rayon	✓	
Azerbaijan	Haciqabul Rayonu	Hajigabul Rayon	✓	

Public Disclosure Copy

Results

Project Development Objective Indicators

No PDO Indicators have been entered for the project.

Intermediate Results Indicators

No IO Indicators have been entered for the project.

Data on Financial Performance (as of 26-Dec-2012)


Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P122944	IBRD-81890	Effective	05-Jul-2012	19-Oct-2012	04-Dec-2012	30-Sep-2017	30-Sep-2017

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P122944	IBRD-81890	Effective	USD	30.00	30.00	0.00	1.07	28.93	4.00

Disbursement Graph

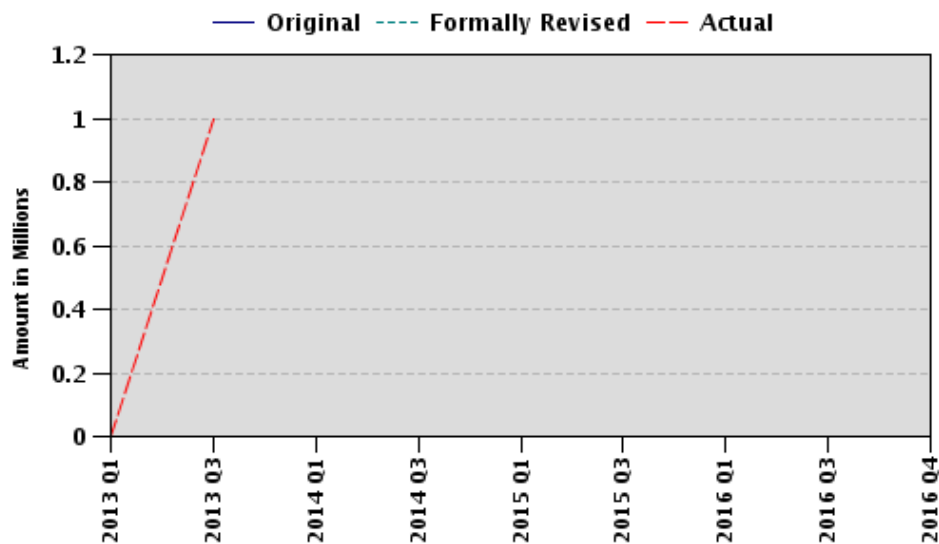

Key Decisions Regarding Implementation

New design features in AzRIP-2 include an important innovation represented by an improved Grievance Redress Mechanism, a means for improving governance and anti-corruption over the course of project implementation. New livelihood pilots included under the Project will be launched in 2013.

Restructuring History

There has been no restructuring to date.

Related Projects

There are no related projects.
