



## Irrigation and Land Market Development Project (P133828)

EUROPE AND CENTRAL ASIA | Georgia | Water Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2014 | Seq No: 10 | ARCHIVED on 28-Jun-2019 | ISR37614 |

Implementing Agencies: Ministry of Environment Protection and Agriculture, Ministry of Justice, GEORGIA

### Key Dates

#### Key Project Dates

Bank Approval Date: 23-May-2014

Effectiveness Date: 13-Mar-2015

Planned Mid Term Review Date: 03-Jul-2017

Actual Mid-Term Review Date: 03-Aug-2017

Original Closing Date: 31-Jul-2019

Revised Closing Date: 31-Jul-2021

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to (i) improve delivery of irrigation and drainage services in selected areas and (ii) develop improved policies and procedures as a basis for a national program of land registration.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

Component 1 Irrigation and Drainage Improvement:(Cost \$45.65 M)

Component 2 Land Market Development:(Cost \$2.25 M)

Component 3 Project Management:(Cost \$2.10 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Moderate	● Moderate

### Implementation Status and Key Decisions

The Project became effective in March 2015. Implementation Progress to date remains as Moderately Satisfactory despite good progress made in several key areas such as progress with construction works, strengthening of irrigation and drainage institutions and the piloting of systematic land registration procedures. It is crucial for the project to accelerate the water user legislative process and full registration of land parcels. It also critical to coordinate land registration and irrigation development once the Bank has taken a decision regarding a request for Additional Financing.





## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Moderate	● Moderate
Macroeconomic	--	● Moderate	● Moderate
Sector Strategies and Policies	--	● Moderate	● Moderate
Technical Design of Project or Program	--	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	--	● Moderate	● Moderate
Fiduciary	--	● Moderate	● Moderate
Environment and Social	--	● Low	● Moderate
Stakeholders	--	● Moderate	● Moderate
Other	--	--	--
Overall	--	● Moderate	● Moderate



## Results

### PDO Indicators by Objectives / Outcomes

To improve delivery of irrigation and drainage services in selected areas				
▶ Absolute volume of irrigation water supplied to Project rehabilitated schemes (million m3 to first Project schemes) (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	67 million m3	67 million m3	81.3 million cubic meters	95 million m3
Date	23-May-2014	29-Sep-2017	10-May-2019	31-Jul-2021
Comments:	Total volume of 2018 irrigation water supplied to three pilot irrigation schemes.			
▶ Area provided with irrigation and drainage services (ha) (Hectare(Ha), Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,636.00	4,713.00	20,000.00
Date	23-May-2014	06-Dec-2017	10-May-2019	31-Jul-2021
Comments:	Data from 2018 irrigation season			
▲ Area provided with irrigation and drainage services - Improved (ha) (Hectare(Ha), Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,636.00	4,713.00	20,000.00
Date	23-May-2014	06-Dec-2017	06-Dec-2017	31-Jul-2021
To develop improved policies and procedures as a basis for a national program of land registration.				
▶ Recommended policies and procedures for national program of land registration submitted to government (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	The corpus of registration regulations and procedures in place	Guidelines for Systematic Land Registration were adopted by NAPR in May 2017	Guidelines for Systematic Land Registration were adopted by NAPR in May 2017	Recommended policies and procedures for national program submitted
Date	23-May-2014	29-Sep-2017	21-Jun-2018	02-Sep-2019
Comments:	There is an ongoing process for preparation of the modifications to current legislation based on lessons learnt during the pilot project implementation.			

### Intermediate Results Indicators by Components



Component 1 Irrigation and Drainage Improvement				
▶Water users provided with new/improved irrigation and drainage services (number) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,642.00	2,693.00	24,000.00
Date	23-May-2014	06-Dec-2017	10-May-2019	31-Jul-2021
Comments:	<p>The reported number of water user represents only those with a formal delivery contract with GA. This number constitutes an estimated 28 percent of all water user provided with irrigation and drainage services in the project schemes. The total number of water users is expected to rise as rehabilitation works of the secondary and tertiary levels evolve.</p> <p>Previous number of female water users has been reported incorrectly. The actual number of female users constitute about 18% of the total number of water users with formal contracts with GA.</p>			
▲Water users provided with irrigation and drainage services - female (number) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,442.00	485.00	2,400.00
Date	23-May-2014	06-Dec-2017	10-May-2019	31-Jul-2021
▶National irrigation and drainage strategy prepared and endorsed (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No strategy	24. The National Irrigation Strategy to 2025 was approved by the Minister of Agriculture on May 23rd 2017	24. The National Irrigation Strategy to 2025 was approved by the Minister of Agriculture on May 23rd 2017	Strategy finalized and endorsed by government
Date	23-May-2014	29-Sep-2017	29-Sep-2017	31-Jul-2019
Component 2 Land Market Development				
▶Number of land titles registered in project pilot areas (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	14,000.00	13,438.00	19,660.00	48,000.00
Date	23-May-2014	06-Dec-2017	10-Jun-2019	31-Jul-2019
Comments:	<p>The indicator is currently partially achieved by 40.9%. The process of title registration includes 3 sets of activities: survey, preparation of registration package and public awareness, and registration, which is the final stage of the process. Currently, 41,383 parcels have been recognized and surveyed. This number indicates a potential of registered land parcels. If all the surveyed parcels will be registered the number of land titles registered in pilot areas can reach 86 percent by the end of the project. The previously envisaged target of 48,000 land plots is not anymore realistic and needs revision to account for ongoing land plot consolidation.</p>			



Component 3 Project Management				
▶Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13,201.00	18,155.00	50,000.00
Date	23-May-2014	29-Sep-2017	10-May-2019	31-Jul-2021
Comments:	Currently there are 18,155 project beneficiaries for land markets component.			
▲Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	33.60	33.60	5,000.00

## Data on Financial Performance


### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P133828	IDA-54560	Effective	USD	50.00	50.00	0.00	23.31	21.64	52%

### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P133828	IDA-54560	Effective	23-May-2014	21-Nov-2014	13-Mar-2015	31-Jul-2019	31-Jul-2021

### Cumulative Disbursements

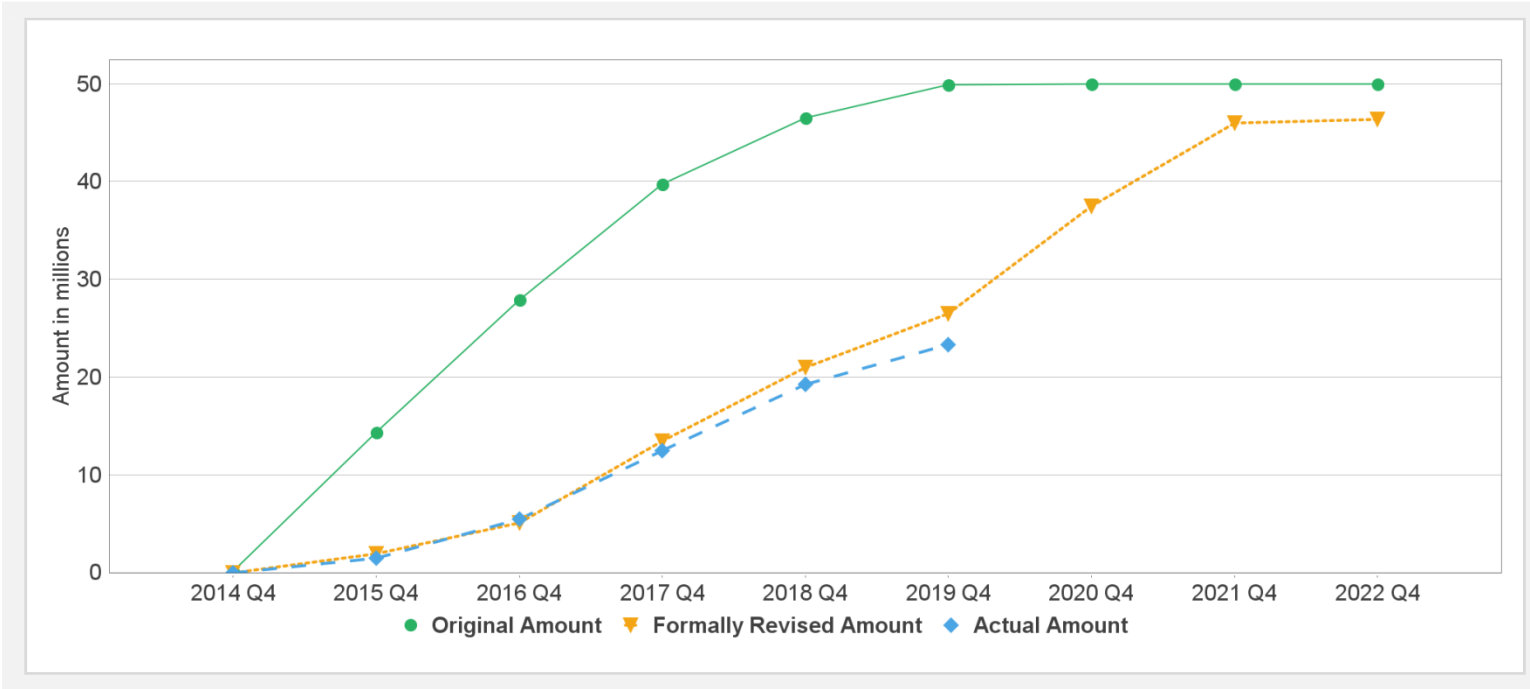

### Restructuring History

Level 2 Approved on 07-Jun-2018

### Related Project(s)

There are no related projects.
