



Turkey Organized Industrial Zones Project (P171645)

EUROPE AND CENTRAL ASIA | Turkey | Finance, Competitiveness and Innovation Global Practice | IBRD/IDA | Investment Project Financing | FY 2021 | Seq No: 2 | ARCHIVED on 25-Jan-2022 | ISR49227 |

Implementing Agencies: Republic of Turkey, Ministry of Industry and Technology

Key Dates

Key Project Dates

Bank Approval Date: 25-Jan-2021

Effectiveness Date: 20-Jul-2021

Planned Mid Term Review Date: 26-May-2023

Actual Mid-Term Review Date:

Original Closing Date: 31-Dec-2026

Revised Closing Date: 31-Dec-2026

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The PDO is to increase the efficiency, environmental sustainability and competitiveness of select Organized Industrial Zones (OIZs) in Turkey.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Supporting the infrastructure and the enabling environment for OIZ sustainability, competitiveness and efficiency:(Cost \$290.00 M)

Technical assistance, capacity building and project management:(Cost \$10.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

The project became effective on July 20, 2022. Since then the Bank and MoIT teams have been working toward establishing a Project Implementation Unit (PIU) in MoIT, finalizing various documents and engaging with OIZs and other stakeholders, such as OSBUK and regional development agencies. The first call for OIZ sub-project applications was launched on November 2, 2021 via the online MEYDIP platform. So far, 33 sub-project applications have been received and are currently being evaluated. The Bank team will conduct a supervision mission January 18-21 to assist with outstanding issues.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Macroeconomic	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Substantial
Sector Strategies and Policies	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Technical Design of Project or Program	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Institutional Capacity for Implementation and Sustainability	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Fiduciary	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Substantial
Environment and Social	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Stakeholders	<input type="checkbox"/> Low	<input type="checkbox"/> Low	<input type="checkbox"/> Low
Other	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Overall	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Results

PDO Indicators by Objectives / Outcomes

Increase the efficiency, environmental sustainability and competitiveness of select OIZs in Turkey				
▶ Water savings from OIZ green investments (Cubic meters/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	6,628,000.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
▶ Energy savings from OIZ both basic and green infrastructure investments (MWh/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	16,579.68
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
▶ Annual reduction in CO2 emissions due to supported investments (Metric tons/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	--	0.00	18,434.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Share of OIZs that attract new investments (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	30.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026

Intermediate Results Indicators by Components

Supporting infrastructure and the enabling environment for OIZ sustainability, comp. and efficiency				
► Number of firms that benefit from OIZ basic and/or green infrastructure investments (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,000.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Renewable energy generated due to OIZ green infrastructure investments (MWh/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	32,600.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Wastewater treated in new/upgraded facilities (Cubic meters/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	29,200,000.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Number of employees trained in the innovation centers and model factories (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2,160.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026



► Proportion of private sector investments facilitated in OIZs as compared to disbursed loan for infrastructure development (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	3.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Number of collaborative projects supported between OIZ firms and academia/research establishments (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	10.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► The establishment of a database/system to track, collect and disaggregate gender-related data (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026

Technical assistance and capacity building				
► Number of laws/standards/regulations or amendments to current regulations enacted to support Green OIZ development (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Number of OIZs certified as Green OIZs (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	10.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026
► Number of firms reporting that they benefit from improved OIZ basic, green and competitiveness infrastructure (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,000.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026



► Number of firms reporting that they understand the benefits of certified Green OIZs (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	700.00
Date	25-Jan-2021	--	10-Jan-2022	31-Dec-2026

Performance-Based Conditions

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P171645	IBRD-92050	Effective	USD	300.00	300.00	0.00	1.16	298.80	0.4%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P171645	IBRD-92050	Effective	25-Jan-2021	26-Feb-2021	20-Jul-2021	31-Dec-2026	31-Dec-2026

Cumulative Disbursements

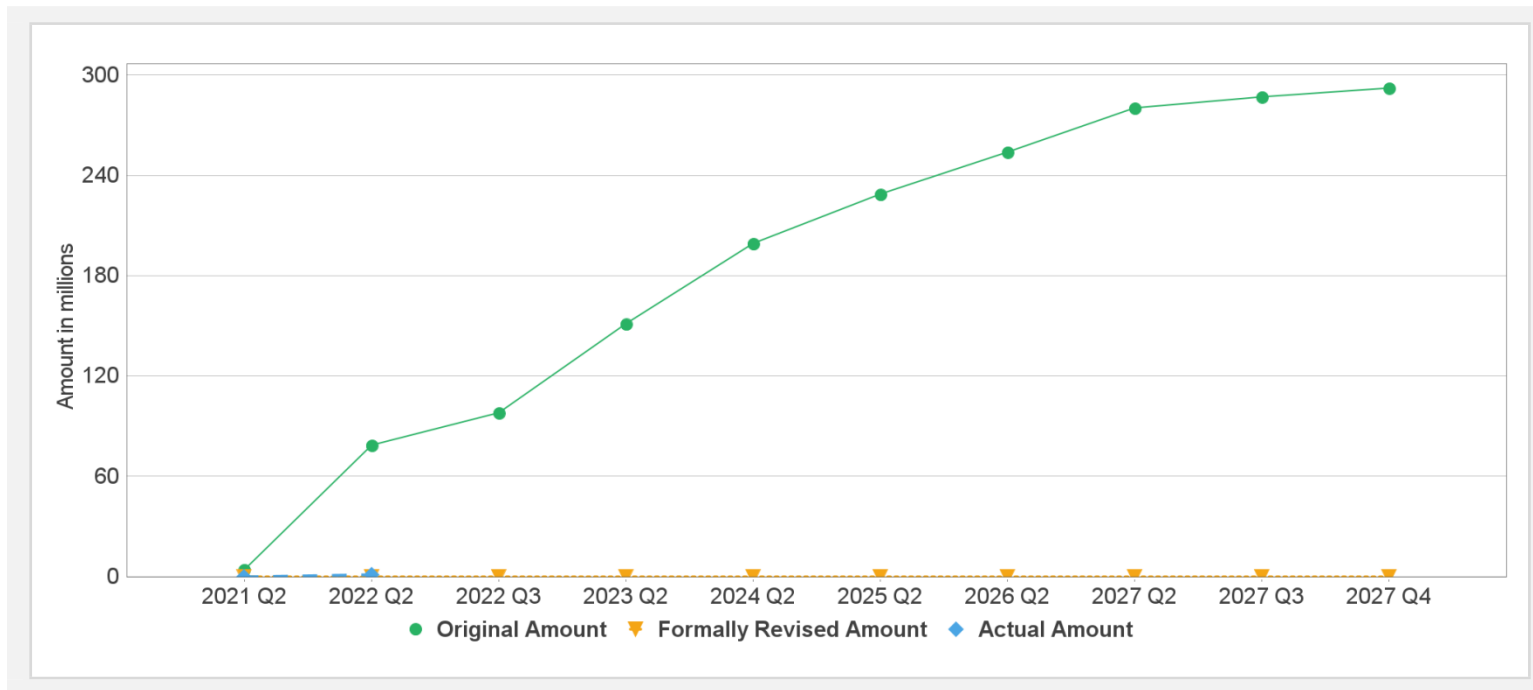



PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
