



Lao PDR Southeast Asia Disaster Risk Management Project (P160930)

EAST ASIA AND PACIFIC | Lao People's Democratic Republic | Social, Urban, Rural and Resilience Global Practice Global Practice | IBRD/IDA | Investment Project Financing | FY 2018 | Seq No: 1 | APPROVED | ISR29183 |

Implementing Agencies:

Key Dates

Key Project Dates

Bank Approval Date:06-Jul-2017

Effectiveness Date:--

Planned Mid Term Review Date:24-Feb-2020

Actual Mid-Term Review Date:--

Original Closing Date:31-Oct-2022

Revised Closing Date:31-Oct-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To reduce the impacts of flooding in Muang Xay and enhance the Government's capacity to provide hydro-meteorological services and disaster response.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Integrated Urban Flood Risk Management:(Cost \$13.50 M)

Hydromet Modernization and Early Warning Systems:(Cost \$10.00 M)

Financial Planning for Disaster Resilience:(Cost \$6.00 M)

Knowledge and Coordination:(Cost \$1.50 M)

Contingent Emergency Response

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Substantial



Implementation Status and Key Decisions

The project was approved by the World Bank Board on July 6, 2017. Steps towards meeting effectiveness conditions are being taken.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	--	● Substantial
Macroeconomic	● Substantial	--	● Substantial
Sector Strategies and Policies	● Moderate	--	● Moderate
Technical Design of Project or Program	● Substantial	--	● Substantial
Institutional Capacity for Implementation and Sustainability	● Substantial	--	● Substantial
Fiduciary	● High	--	● High
Environment and Social	● Moderate	--	● Moderate
Stakeholders	● Moderate	--	● Moderate
Other	--	--	--
Overall	● Substantial	--	● Substantial

Results

Project Development Objective Indicators

► Percentage of urban population in Muang Xay protected from floods (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	30.00	--	30.00	70.00
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

▲ of which are female (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	50.00	--	50.00	50.00
-------	-------	----	-------	-------

► Satisfaction of weather information end-users increased (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

► Lao PDR has information and capacity to access sovereign disaster risk insurance (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

Overall Comments

Intermediate Results Indicators

► Length of embankment rehabilitated (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	8.00
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022



► Risk informed spatial and urban plans for a city in the Nam Ou Basin developed (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

► Accuracy of weather forecast improved (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

► Validated hydromet data is accessible on a centralized online data management platform (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

► National disaster risk finance strategy developed (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022



► Participants in consultation activities during project implementation (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	500.00
Date	02-Oct-2017	--	31-Jul-2017	30-Jun-2022

▲ of which women (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	40.00

► Grievances registered related to delivery of project benefits addressed (%) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	80.00
Date	30-Jun-2017	--	31-Jul-2017	30-Jun-2022

▲ Grievances related to delivery of project benefits that are addressed-(number) (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	100.00

Overall Comments



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P160930	IDA-61200	Not Effective	USD	30.00	30.00	0.00	0.00	30.79	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P160930	IDA-61200	Not Effective	06-Jul-2017	--	--	31-Oct-2022	31-Oct-2022

Cumulative Disbursements

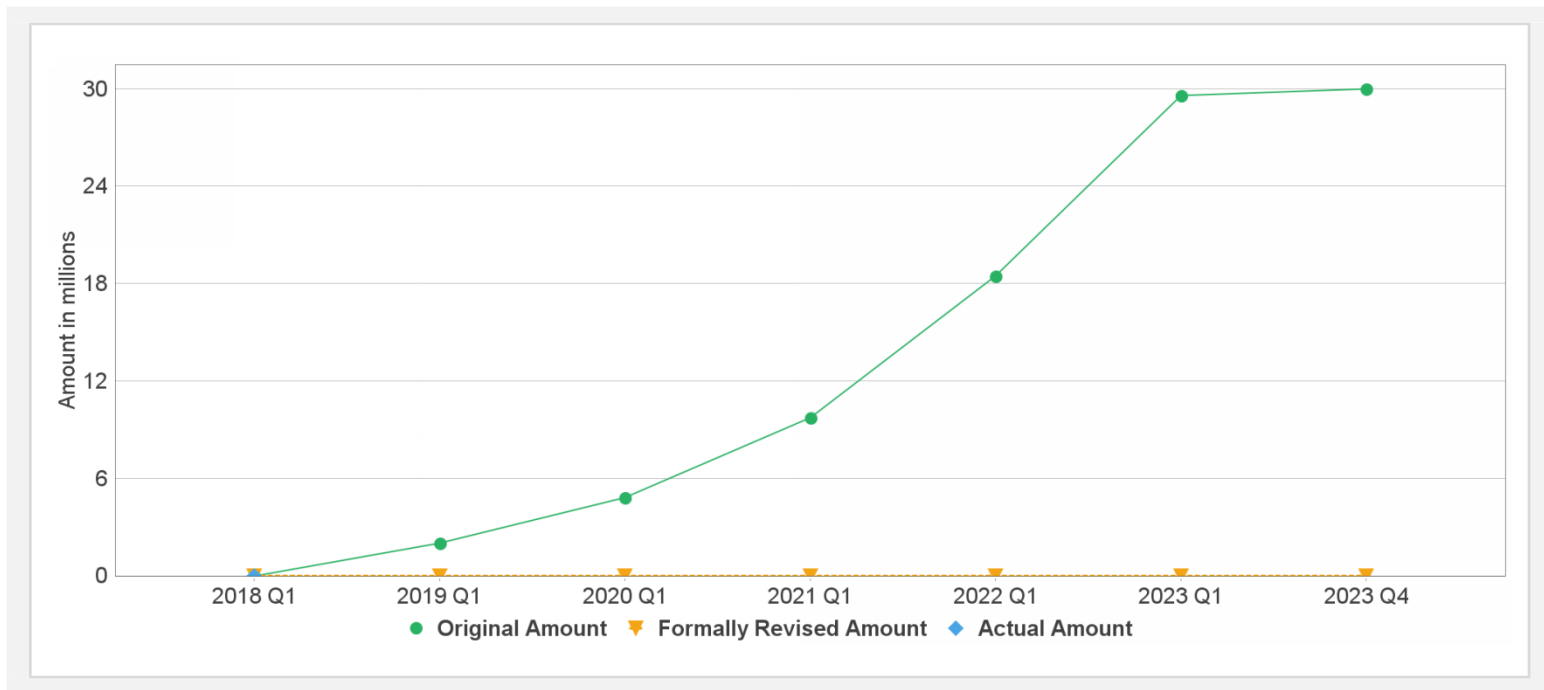

Restructuring History

There has been no restructuring to date.

Related Project(s)



There are no related projects.
