Public Disclosure Authorized

Lebanon Emergency Assistance Project (P509428)

MID EAST,NORTH AFRICA,AFG,PAK | Lebanon | IBRD/IDA | Investment Project Financing (IPF) | FY 2025 | Seq No: 4 | Archived on 29-Jun-2026 | ISR08362

Implementing Agencies: Council for Development and Reconstruction

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Decision package on 24-Jun-2025)

The Proposed Project Development Objective (PDO) is to enable sustainable recovery and restore lifeline services and critical infrastructure in conflict-affected areas of Lebanon.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name
Immediate Response :(Cost 80,000,000.00)
Rapid Recovery of Public Lifeline Services and Public Critical Infrastructure :(Cost 420,000,000.00)
Sustainable and Robust Reconstruction of Public Critical Infrastructure & Public Lifeline Services :(Cost 475,000,000.00)
Project Management :(Cost 25,000,000.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	Satisfactory	Satisfactory
Overall Implementation Progress (IP)	Satisfactory	Satisfactory
Overall Risk Rating	High	High

4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

The Lebanon Emergency Assistance Project (LEAP) was approved by the World Bank's Board of Directors on June 24, 2025, and the Loan Agreement was signed on August 25, 2025. Following parliamentary ratification on December 19, 2025, the project was declared effective on February 26, 2026.

Initial implementation is underway, with the first disbursement to the Designated Account processed on May 13, 2026. Given the current operational context, the project is prioritizing procurement and preparatory activities that can be undertaken immediately, positioning investments for accelerated execution once access and security conditions allow. Initial efforts have successfully established the Project Implementation Unit (PIU) within the Council for Development and Reconstruction (CDR), with core staff contracted and additional personnel identified for mobilization as implementation scales up.

The project is advancing immediate procurement packages for emergency response services, telecommunications, and the rehabilitation of schools currently used as shelters. Additionally, stage 1 Framework Agreements (FAs) are being launched to pre-identify contractors for civil works and consulting services, enabling rapid deployment as physical access becomes possible. An engineering firm has been mobilized to conduct an ongoing Investment Needs Assessment. This will update damage and recovery needs across key sectors (including water, energy, transport, health, and education) to guide the prioritization of area-based reconstruction activities. Critical technical assistance and planning activities under procurement, including rubble management design and technical assistance and the procurement of high-resolution satellite imagery to assess road access. To ensure robust fiduciary oversight and transparent implementation, procurement is also underway for a Third-Party Monitoring Agent and supplemental WB expanded supervision oversight through a Lender's Engineer.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 24 Jun 2025	Last Approved Rating ISR Seq. 03 - 23 Feb 2026	Proposed Rating
Political and Governance	High	High	High
Macroeconomic	High	High	High
Sector Strategies and Policies	Substantial	Substantial	Substantial
Technical Design of Project or Program	Substantial	Substantial	Substantial

Institutional Capacity for Implementation and Sustainability	High	High	High
Fiduciary	High	High	High
Environment and Social	Substantial	Substantial	Substantial
Stakeholders	High	High	High
Other	Moderate	Moderate	Moderate
Overall	High	High	High

6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Green Recovery								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Total volume of rubble sustainably managed (Cubic Meter (m3))	0	Jan/2025	0	10-Sep-2025	0	10-Sep-2025	5,000,000	Dec/2027

Restoration of lifeline services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People provided with restored lifeline services and critical infrastructure under the Project (Number)	0	Jan/2025	0	10-Sep-2025	0	10-Sep-2025	1,200,000	Dec/2030

6.2 Intermediate Results Indicators by Components

Immediate Response								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Sites for hazardous materials are established that meet international standards (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	1	May/2026

Percentage of Rubble Material Recycled (Percentage)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	70	Nov/2030
Net GHG Emissions (tCO2eq/year)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	35,000	Nov/2030
Sites for unrecyclable materials are established that meet international standards (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	6	Nov/2026

Rapid Recovery of Public Lifeline Services and Public Critical Infrastructure

Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People provided with water (CSC) (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	850,000	Dec/2030
Pregnant women receiving antenatal care from a qualified provider at a restored Health Care Facility (Primary Care Center or Hospital) (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	130,000	Nov/2030
Students supported with better education through repaired and restored schools (CSC) (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	64,000	Nov/2030
People benefiting from improved access to sustainable transport infrastructure and services (CSC) (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	100,000	Nov/2030

People provided with access to electricity (CSC) (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	150,000	Nov/2030
Renewable energy capacity enabled (CSC) (Gigawatt)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	0.03	Nov/2030
Net Greenhouse Gas Emissions (CSC) (tCO2eq/year)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	12,960	Nov/2030

Sustainable and Robust Reconstruction of Public Critical Infrastructure & Public Lifeline Services

Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Number of Green and Climate Ready Investments Ready for Works Contracting (Number)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	20	Nov/2028
Assessment of damage and reconstruction needs in the underground water supply and sewerage or stormwater network completed (Yes/No)	No	Jan/2025	No	10-Sep-2025	No	10-Sep-2025	Yes	Dec/2025
Percentage of bulk water/waste water infrastructure is reconstructed to climate resilient standards (e.g. water treatment plants, waste water treatment plants, reservoirs, pumping stations) (Percentage)	0	Jan/2025	0	10-Sep-2025	0	10-Sep-2025	75	Dec/2030

Percentage of severely damaged or destroyed health, education, social and emergency response buildings reconstructed to climate resilient and EE standards (Percentage)	0	Jan/2025	0	10-Sep-2025	0	10-Sep-2025	80	Dec/2030
Percentage of severely damaged or destroyed energy network infrastructure that is reconstructed to climate resilient standards (Percentage)	10	Jan/2025	10	10-Sep-2025	10	10-Sep-2025	70	Dec/2030
Percentage of severely damaged or destroyed transport infrastructure reconstructed to climate resilient standards (Percentage)	0	Jan/2025	0	10-Sep-2025	0	10-Sep-2025	80	Dec/2030

Project Management

Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Average number of weeks from issuance of a procurement notice to signed contract for works and goods (Number)	56	Jan/2025	56	10-Sep-2025	56	10-Sep-2025	12	Nov/2025
Average number of weeks from issuance of	36	Jan/2025	36	10-Sep-2025	36	10-Sep-2025	18	Dec/2025

procurement notice to contract signing for consultancy firm services (Number)								
Average number of weeks required to issue a procurement notice from finalization of draft bidding documents due streamlined processes and digitalization in CDR (Number)	36	Jan/2025	36	10-Sep-2025	36	10-Sep-2025	2	Dec/2026
Grievances addressed by PMU in accordance with the stipulated service standards (Percentage)	0	Dec/2024	0	10-Sep-2025	0	10-Sep-2025	95	Nov/2030
Beneficiary Feedback Mechanism is in place (Yes/No)	No	Jan/2025	No	10-Sep-2025	No	10-Sep-2025	Yes	Sep/2025

7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

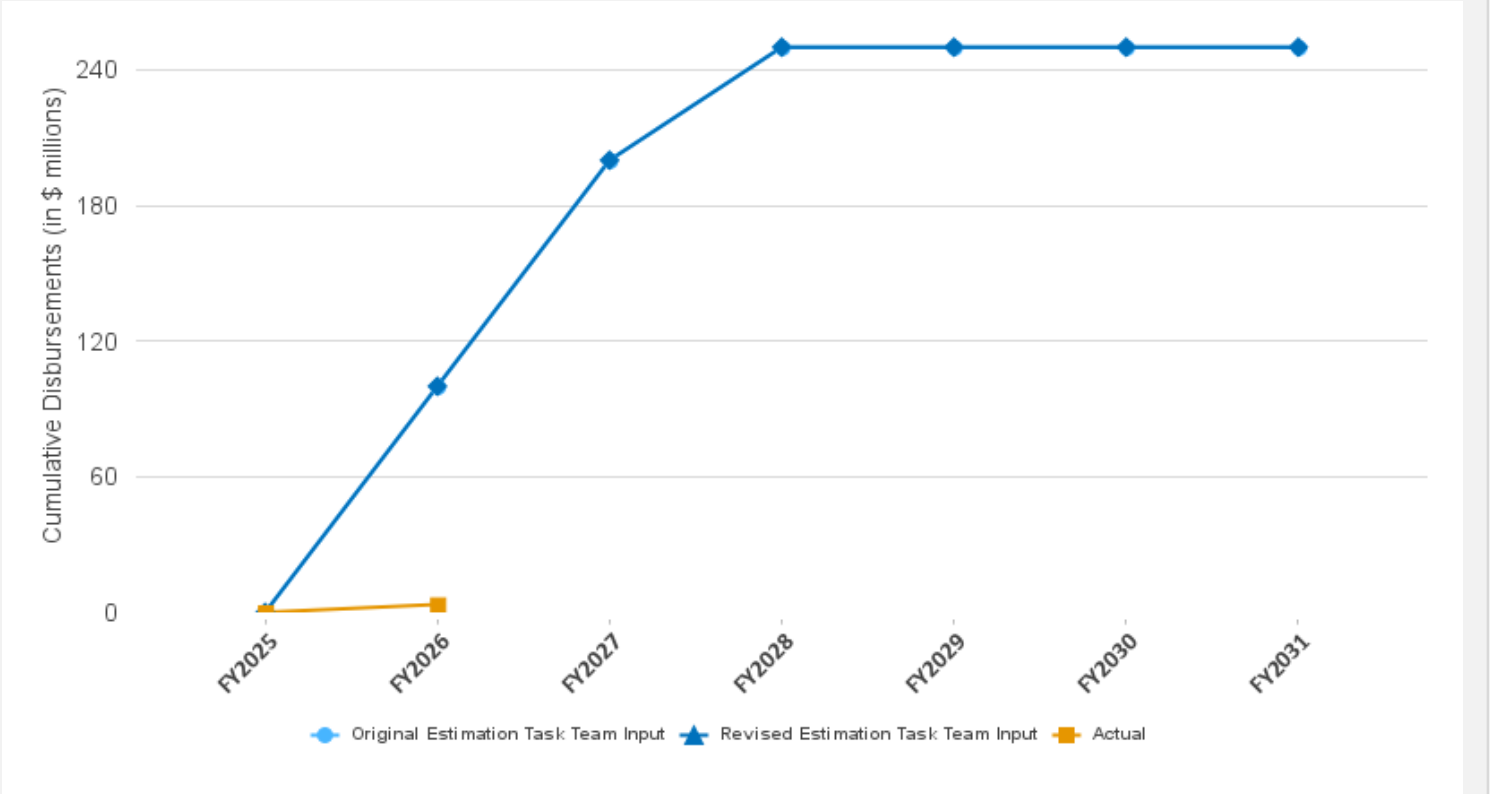

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	Historical Disbursed	% Disbursed
IBRD-98410	Effective	250.00	250.00	0.00	4.13	245.88	0.00	1.65%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IBRD-98410	Effective	24-Jun-2025	25-Aug-2025	26-Feb-2026	31-Dec-2030	31-Dec-2030

8. KEY DATES

Key Events	Planned	Actual
Approval	24-Jun-2025	24-Jun-2025
Effectiveness	26-Feb-2026	26-Feb-2026
Operation Closing/Cancellation	31-Dec-2030	

9. RESTRUCTURING HISTORY

10. ASSOCIATED OPERATION(S)

There are no associated operations
