



Local Governance and Community Resilience Project (P178699)

WESTERN AND CENTRAL AFRICA | Central African Republic | IBRD/IDA | Investment Project Financing (IPF) | FY 2024 | Seq No: 2 | Archived on 07-Jun-2024 | ISR00310

Implementing Agencies: Ministry of Economy, Planning and International Cooperation

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 05-Sept-2023)

The Project development objective is to: build state and citizen capacity for local service delivery, improve access to basic socio-economic climate adaptive infrastructure, and provide socio-economic support to the reintegration of ex-combatants.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name

Strengthening central systems underpinning decentralization and enhancing local capacity for service delivery:(Cost 18,000,000.00)

Community Resilience:(Cost 48,000,000.00)

Socio-economic reintegration of ex-combatants:(Cost 10,000,000.00)

Project management:(Cost 14,000,000.00)

Contingent Emergency Response (CERC):(Cost 0.00)

3. OVERALL RATINGS

| Name | Previous | Current |
|--------------------------------------|----------------|---------------------------|
| Progress towards achievement of PDO | ● Satisfactory | ● Moderately Satisfactory |
| Overall Implementation Progress (IP) | ● Satisfactory | ● Moderately Satisfactory |
| Overall Risk Rating | ● High | ● High |



4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

The Project was officially launched on January 23, 2024 by the Ministry of Economy, Planning and International Cooperation and the World Bank Representative.

The project has three main components: 1) Strengthening Central Systems Underpinning Decentralization and Enhancing Local Capacity for Service Delivery 2) Resilient Communities 3) Socio-economic reintegration of ex-combatants. It will cover four provinces: Lobaye, Basse-Kotto, Mbomou and Vakaga.

A number of workshops have been held and manuals and policy documents, including the grievance mechanism have been developed.

The project will include participatory climate risk assessments, and a manual for that work was tested in Bangui and Mbaiki in the end of May/early June, 2024.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

| Risk Category | Rating at Approval Approval Package - 06 Sep 2023 | Last Approved Rating ISR Seq. 01 - 05 Dec 2023 | Proposed Rating |
|--|---|--|-----------------|
| Political and Governance | ● High | ● High | ● High |
| Macroeconomic | ● High | ● High | ● High |
| Sector Strategies and Policies | ● Substantial | ● Substantial | ● Substantial |
| Technical Design of Project or Program | ● Substantial | ● Substantial | ● Substantial |
| Institutional Capacity for Implementation and Sustainability | ● Substantial | ● Substantial | ● Substantial |
| Fiduciary | ● Substantial | ● Substantial | ● Substantial |
| Environment and Social | ● Substantial | ● Substantial | ● Substantial |
| Stakeholders | ● Moderate | ● Moderate | ● Moderate |



| | | | |
|---------|--------|--------|--------|
| Other | ● High | ● High | ● High |
| Overall | ● High | ● High | ● High |



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

| Build state and citizen capacity for local service delivery | | | | | | | | |
|--|-------------------------------|------------|--|-------------|------------------|-------------|----------------|------------|
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |
| Civic registration services provided by local authorities in the targeted communities (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 30.00 | Aug/2028 |
| | Comments on achieving targets | | Percentage | | | | | |
| Increased percentage of Community members reporting improved perceptions of inclusive and accountable local governance in a multi-dimensional survey instrument (Percentage) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 20.00 | Aug/2028 |
| | Comments on achieving targets | | Percentage disaggregated by gender. | | | | | |
| Increased percentage of women reporting improved perceptions of inclusive and accountable local governance (Percentage) | 0.00 | | 0.00 | | | | 20.00 | |
| | Comments on achieving targets | | Percentage of women that report improved perceptions of inclusive and accountable local governance | | | | | |
| Improve access to basic socio-economic climate adaptive infrastructure | | | | | | | | |
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |



| | | | | | | | | |
|---|-------------------------------|----------|---|-------------|------------------|-------------|----------------|----------|
| Direct beneficiaries in project areas with improved access to climate resilient infrastructure (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 68,000.00 | Aug/2028 |
| | Comments on achieving targets | | The total population impacted upon by project component | | | | | |
| Of which women (Percentage) | 0.00 | | 0.00 | | 0.00 | | 50.00 | |
| | Comments on achieving targets | | Percentage of total number that report improved access that are women | | | | | |
| Of which youth (Percentage) | 0.00 | | 0.00 | | | | 35.00 | |
| | Comments on achieving targets | | Youth is, as per UN definition, persons between the ages of 15 and 24 years | | | | | |
| Community members reporting that the socio-economic investments reflect their needs (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 80.00 | Aug/2028 |
| | Comments on achieving targets | | Number disaggregated by gender and youth | | | | | |
| Women reporting that the socio-economic investments reflect their needs (Percentage) | 0.00 | | 0.00 | | | | 80.00 | |
| | Comments on achieving targets | | Percentage of women reporting that the infrastructure reflects their need | | | | | |
| Youth reporting that the socio-economic infrastructure reflect their needs (Percentage) | 0.00 | | 0.00 | | | | 80.00 | |
| | Comments on achieving targets | | Youth is, as per UN definition, persons between the ages of 15 and 24 years | | | | | |
| Female participants in village committees in the targeted prefectures (Percentage) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 40.00 | Aug/2028 |
| | Comments on achieving targets | | Raw number, ratio to male members. | | | | | |
| Provide socio-economic support to the reintegration of ex-combatants | | | | | | | | |
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |



| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |
|--|-------------------------------|------------|---|-------------|-------|-------------|----------|------------|
| Former combatants that have received socio-economic support to reintegrate into their communities (Number) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 2,000.00 | Aug/2028 |
| | Comments on achieving targets | | Number of ex-combatants that have received civic and vocational training. | | | | | |
| Of which women (Percentage) | 0.00 | | 0.00 | | | | 8.00 | |
| | Comments on achieving targets | | Of which women | | | | | |

6.2 Intermediate Results Indicators by Components

| Strengthening central systems underpinning decentralization and enhancing local capacity for service delivery | | | | | | | | |
|--|-------------------------------|------------|---|-------------|------------------|------|----------------|------------|
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |
| Implementation decrees, compendiums and vulgarization documents produced (Number) | 4.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 15.00 | Aug/2028 |
| | Comments on achieving targets | | No of documents developed with TA from the Project. | | | | | |
| Regional treasury agencies (including Bangui) with a connection to Simba and reporting municipal financial data (Number) | 1.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 4.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative indicator | | | | | |
| Training modules on core decentralized or deconcentrated functions | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 10.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative Indicator | | | | | |



| | | | | | | | | |
|--|-------------------------------|----------|---|-------------|--|--|--------|----------|
| produced by the enhanced training program (Number) | | | | | | | | |
| Deconcentrated or decentralized staff trained on core functions using the new modules (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 150.00 | Aug/2028 |
| | Comments on achieving targets | | Disaggregated by gender and commune | | | | | |
| Of which women (Number) | 0.00 | | 0.00 | | | | 40.00 | |
| | Comments on achieving targets | | Number of women that have received training | | | | | |
| Increase in revenues (local taxes and retroceded taxes from central government) mobilized by communes (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative Indicator | | | | | |
| Communes with a rehabilitated an operational office (town hall, or public administration offices) (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 15.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative Indicator | | | | | |
| Communes with core planning documents approved and published (LDP, annual budget, annual investment plan) (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 75.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative indicator | | | | | |
| Community leaders (e.g. CSO leaders, local associations leaders, traditional chiefs etc.) trained on their rights | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 110.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative | | | | | |



| and voice within local governance (Number) | | | | | | | | |
|---|-------------------------------|------------|---|-------------|------------------|------|----------------|------------|
| Women trained (Number) | 0.00 | | 0.00 | | | | 40.00 | |
| | Comments on achieving targets | | Number of women trained | | | | | |
| Respondents to the governance surveys who report an improved awareness of their role in the local governance and increased voice and agency. (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Aug/2028 |
| | Comments on achieving targets | | Percentage (increased proportion) | | | | | |
| Women who report an improved awareness (Percentage) | 0.00 | | 0.00 | | | | 20.00 | |
| | Comments on achieving targets | | Percentage | | | | | |
| Community Resilience | | | | | | | | |
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |
| Community Groups established and trained in participatory methods. (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 22.00 | Aug/2028 |
| | Comments on achieving targets | | Number: Quantitative Indicator, disaggregated. | | | | | |
| Women in leadership positions in the community groups established and trained by the Project (Percentage) | 0.00 | Jan/2024 | 0.00 | 22-Nov-2023 | | | 40.00 | Aug/2028 |
| | Comments on achieving targets | | Proportion of women in leadership position (as chair or co-chair) in the community committees established and trained by the project. | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 100.00 | Aug/2028 |



| | | | | | | | | |
|--|-------------------------------|----------|--|-------------|------|-------------|--------|----------|
| Local Development plans including community climate led diagnostics (Percentage) | Comments on achieving targets | | Percentage of LDPs | | | | | |
| Climate resilient infrastructure built or rehabilitated (Number) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 66.00 | Aug/2028 |
| Communes where a platform for receiving feed-back from community members on community infrastructure and local development plans have been established (Number) | Comments on achieving targets | | Number | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 22.00 | Aug/2028 |
| Grievances registered and addressed within the Projects grievance mechanism (Percentage) | Comments on achieving targets | | Measured by platforms established, that are working with collecting feedback from community members (through scorecards or other social accountability tools). | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 100.00 | Aug/2028 |
| Grievances reported by women (and percentages of grievances addressed) (Percentage) | Comments on achieving targets | | Number of complaints received and number of the complaints resolved (as a %). | | | | | |
| | 0.00 | | 0.00 | | | | 100.00 | |
| Respondents to the social cohesion survey that reports improvement in horizontal and vertical social cohesion in communes where the project is implemented. (Percentage) | Comments on achieving targets | | Number of complaints received by woment and number of the complaints resolved (as a %). | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Aug/2028 |
| Respondents to the social cohesion survey that reports improvement in horizontal and vertical social cohesion in communes where the project is implemented. (Percentage) | Comments on achieving targets | | Measured via PIU MIS and surveys | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Aug/2028 |



| | | | | | | | | |
|---|-------------------------------|------------|---|-------------|------------------|------|----------------|------------|
| Women that reports improvement in vertical and social cohesion in communes where the Project is implemented (Percentage) | 0.00 | | 0.00 | | | | 20.00 | |
| | Comments on achieving targets | | Measured via PIU MIS and surveys | | | | | |
| Beneficiaries involved in LIPW (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 22,000.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative | | | | | |
| Women involved in LIPW (Percentage) | 0.00 | | 0.00 | | | | 40.00 | |
| | Comments on achieving targets | | Percentage of beneficiaries that are woman | | | | | |
| Small-scale infrastructures created (demarcation and water points) (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 60.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative indicator | | | | | |
| Mediation platforms trained by the project (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 22.00 | Jul/2028 |
| | Comments on achieving targets | | Number of mediation groups (existing and new) trained by the project in conflict resolution | | | | | |
| Disputes related to transhumant pastoralists mediated by structures created or supported by the project in areas where the project is implemented. (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 22.00 | Jul/2028 |
| | Comments on achieving targets | | Number of disputes solved. | | | | | |
| Socio-economic reintegration of ex-combatants | | | | | | | | |
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |



| | | | | | | | | |
|--|-------------------------------|----------|--|-------------|------|-------------|----------|----------|
| Ex-combatants who complete civic education (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 2,000.00 | Dec/2026 |
| | Comments on achieving targets | | Quantitative indicator (disaggregated) | | | | | |
| Of which women (Number) | 0.00 | | 0.00 | | | | 160.00 | |
| | Comments on achieving targets | | Percentage of women amongst the ex-combatants that have received civic education | | | | | |
| Ex-combatants who complete vocational training (Number) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 2,000.00 | Dec/2026 |
| | Comments on achieving targets | | Quantitative indicator disaggregated | | | | | |
| Of which women (Number) | 0.00 | | 0.00 | | | | 160.00 | |
| | Comments on achieving targets | | Quantitative | | | | | |
| Reintegration kits distributed to ex-combatants (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 2,000.00 | Dec/2026 |
| | Comments on achieving targets | | Quantitative indicator (disaggregated) | | | | | |
| Of which women (Number) | 0.00 | | 0.00 | | | | 160.00 | |
| | Comments on achieving targets | | No of women | | | | | |
| AGRs established (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Dec/2026 |
| | Comments on achieving targets | | Quantitative indicator (disaggregated) | | | | | |
| Women that are part of AGRs (Number) | 0.00 | | 0.00 | | | | 160.00 | |
| | Comments on achieving targets | | Quantitative indicator | | | | | |
| | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 80.00 | Dec/2026 |




| | | | | | | | | |
|---|-------------------------------|------------|--|-------------|------------------|-------------|----------------|------------|
| Ex-combatants expressing that they are accepted by their communities (Percentage) | Comments on achieving targets | | Quantitative. Measured through surveys at the community level | | | | | |
| Community members that express acceptance of ex-combatants (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 80.00 | Dec/2026 |
| | Comments on achieving targets | | Measured through surveys of community members | | | | | |
| Ex-combatants report an increase in household income (Percentage) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 90.00 | Dec/2026 |
| | Comments on achieving targets | | Percentage of ex-combatants (six months after having finished the vocational training) | | | | | |
| Women reporting an increase (Number) | 0.00 | | 0.00 | | 0.00 | | 144.00 | |
| | Comments on achieving targets | | Measured through surveys | | | | | |
| Climate resilient socio-economic infrastructure rehabilitated and constructed. (Number) | 0.00 | Apr/2024 | 0.00 | 22-Nov-2023 | | | 20.00 | Dec/2026 |
| | Comments on achieving targets | | No of infrastructures rehabilitated or created in areas where Component 3 are implemented independently from Subcomponent 2.1. | | | | | |
| Project management | | | | | | | | |
| Indicator Name | Baseline | | Actual (Previous) | | Actual (Current) | | Closing Period | |
| | Value | Month/Year | Value | Date | Value | Date | Value | Month/Year |
| Number of knowledge products developed (Number) | 0.00 | Apr/2024 | 0.00 | 15-Apr-2024 | 0.00 | 15-Apr-2024 | 5.00 | Aug/2028 |
| | Comments on achieving targets | | Quantitative indicator | | | | | |



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

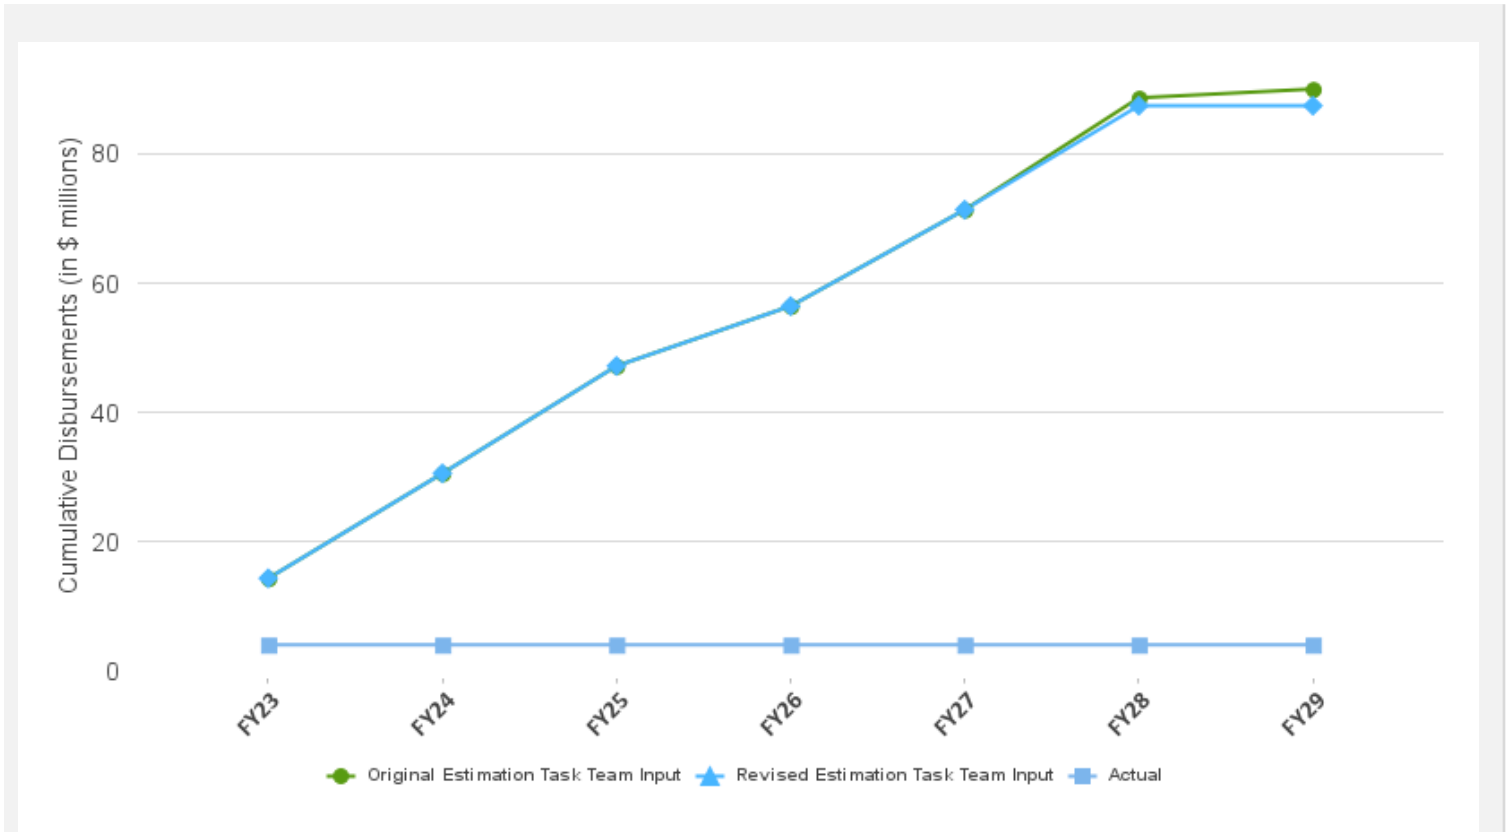

7.2 Disbursements (by loan)

| Loan/Credit/TF | Status | Original | Revised | Cancelled | Disbursed | Undisbursed | % Disbursed |
|----------------|-----------|----------|---------|-----------|-----------|-------------|-------------|
| IDA-E2240 | Effective | 90.00 | 90.00 | 0.00 | 4.43 | 85.20 | 4.92% |
| IDA-V4720 | Closed | 1.36 | 0.00 | 1.36 | 0.00 | 0.00 | 0% |

7.3 Key Dates (by loan)

| Loan/Credit/TF | Status | Approval | Signing | Effectiveness | Orig. Closing | Rev. Closing |
|----------------|-----------|--------------|--------------|---------------|---------------|--------------|
| IDA-E2240 | Effective | 06-Sept-2023 | 25-Sept-2023 | 19-Dec-2023 | 31-Aug-2028 | 31-Aug-2028 |



8. KEY DATES

| Key Events | Planned | Actual |
|--------------------------------|--------------|--------------|
| Approval | 06-Sept-2023 | 06-Sept-2023 |
| Effectiveness | 16-Mar-2023 | 16-Mar-2023 |
| Mid-Term Review No. 01 | 18-May-2026 | |
| Operation Closing/Cancellation | 31-Aug-2028 | |

9. RESTRUCTURING HISTORY

10. ASSOCIATED OPERATION(S)

There are no associated operations
