



## Guinea-Bissau Strengthening Maternal and Child Health Service Delivery (P163954)

WESTERN AND CENTRAL AFRICA | Guinea-Bissau | IBRD/IDA | Investment Project Financing (IPF) | FY 2018 | Seq No: 13 | Archived on 30-Jun-2024 | ISR01012

Implementing Agencies: Ministry of Public Health

**1. OBJECTIVE****1.1 Development Objective**

Original Development Objective (Approved as part of Approval package on 30-May-2018)

To improve coverage of essential maternal and child health services in the Recipient's territory.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

**2. COMPONENTS**

Name

1. Institutional Strengthening of MINSAP:(Cost 3,290,000.00)

2 - Health Workforce Development:(Cost 2,710,000.00)

3. Improving Essential Maternal and Child Health Services:(Cost 7,480,000.00)

4 - Community Health and Social Mobilization:(Cost 10,170,000.00)

5. Contingent Emergency Response:(Cost 0.00)

**3. OVERALL RATINGS**

Name	Previous	Current
Progress towards achievement of PDO	<span style="color: green;"> </span> Satisfactory	<span style="color: green;"> </span> Satisfactory
Overall Implementation Progress (IP)	<span style="color: green;"> </span> Satisfactory	<span style="color: green;"> </span> Satisfactory
Overall Risk Rating	<span style="color: orange;"> </span> Substantial	<span style="color: orange;"> </span> Substantial



## 4. KEY ISSUES & STATUS

### 4.1 Implementation Status and Key Decisions

The project was approved on May 31, 2018, and declared effective on October 3, 2018. It was restructured in June 2021, with the restructuring becoming effective on October 15, 2021. The project has continued to make steady progress since then. In September 2023, the government conducted the project's Mid Term Review (MTR), concluding that the project is on a sound track to achieve its objectives. As a result, the progress towards the achievement of the PDO has been upgraded to satisfactory. The supervision mission held in May 2024 confirmed that the project is on track to achieve its objectives, as evidenced by activities and indicators, and the progress towards the achievement of the PDO is kept as satisfactory. Nonetheless, some challenges remain.

## 5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 31 May 2018	Last Approved Rating ISR Seq. 012 - 17 Jan 2024	Proposed Rating
Political and Governance	High	High	High
Macroeconomic	Substantial	Substantial	Substantial
Sector Strategies and Policies	Substantial	Substantial	Substantial
Technical Design of Project or Program	Substantial	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	High	High	High
Fiduciary	Substantial	Substantial	Substantial
Environment and Social	Moderate	Moderate	Moderate
Stakeholders	Substantial	Substantial	Substantial
Other		Substantial	Substantial
Overall	Substantial	Substantial	Substantial



## 6. RESULTS

### 6.1 PDO Indicators by PDO Outcomes

To improve coverage of essential maternal and child health services in the Recipient's territory.								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Pregnant women attending at least 4 prenatal care consultations during pregnancy (Number)	23,990.00	Dec/2018	67,987.00	29-Dec-2023			103,000.00	Dec/2025
Number of deliveries in the health facilities (Number)	30,197.00	Dec/2018	92,915.00	29-Dec-2023			105,000.00	Dec/2025
Number of children (0-11 months) fully vaccinated (Number)	51,523.00	Dec/2018	125881	18-Jun-2024	125881	18-Jun-2024	105,000.00	Dec/2025
Number of children under-five with confirmed malaria who receive antimalaria treatment by CHWs (Number)	0.00	Dec/2018	2,000.00	29-Dec-2023			4,000.00	Dec/2025

### 6.2 Intermediate Results Indicators by Components

1. Institutional Strengthening of MINSAP				
Indicator Name	Baseline	Actual (Previous)	Actual (Current)	Closing Period



	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Number of administrative staff trained in the ministry of health (Number)	0.00	Dec/2018	11.00	29-Dec-2023			250.00	Dec/2025
<b>2 - Health Workforce Development</b>								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Number of primary health workers trained in RMNCH competencies (Number)	0.00	Dec/2018	2,217.00	29-Dec-2023			2,500.00	Dec/2025
Percentage of healthcare workers that provide the correct treatment for a basic case of childhood diarrhea (Percentage)	0.00	Mar/2018	0.00	31-Jan-2022			60.00	Dec/2025
Percentage of healthcare workers that apply the appropriate EmONC treatment (Percentage)	0.00	Sept/2018	0.00	31-Jan-2022			60.00	Dec/2025
<b>3. Improving Essential Maternal and Child Health Services</b>								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People who have received essential health, nutrition, and	228,000.00	Dec/2018	921,347.00	29-Dec-2023			1,200,000.00	Dec/2025



population (HNP) services (Number)								
People who have received essential health, nutrition, and population (HNP) services - Female (RMS requirement) (Number)	54,000.00		96,410.00				230,000.00	
Number of children immunized (Number)	51,523.00	Dec/2018	647,029.00	29-Dec-2023			800,000.00	Dec/2025
Number of women and children who have received basic nutrition services (Number)	190,000.00	Dec/2018	900,000.00	19-Jan-2024			1,000,000.00	Dec/2025
Number of deliveries attended by skilled health personnel (Number)	30,197.00	Dec/2018	92,915.00	29-Dec-2023			105,000.00	Dec/2025
Children 12-59 months of age attending at least one healthcare consultation (Number)	122,535.00	Dec/2018	515,507.00	29-Dec-2023			700,000.00	Dec/2025
Percentage of primary health care facilities	0.00	Sept/2018	54.55	18-Jun-2024	54.55	18-Jun-2024	50.00	Dec/2025



(type A, B, and C) with all essential drugs available on the day of the visit (Percentage)								
Number of health centers rehabilitated (Number)	0.00	Sept/2018	0.00	31-Jan-2022			11.00	Dec/2025
Number of facilities with beneficiaries reporting illegal charges from providers for essential maternal and child health services (Number)	128.00	Sept/2018	128.00	31-Jan-2022			70.00	Dec/2025


**4 - Community Health and Social Mobilization**

Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Women visited by community health workers (Number)	0.00	Sept/2018	18557	18-Jun-2024	18557	18-Jun-2024	20,000.00	Dec/2025
Satisfaction of users with basic MCH services provided (Percentage)	0.00	Apr/2018	0.00	31-Jan-2022			60.00	Dec/2025
Number of women taken care in way houses (Number)	0.00	Sept/2018	2219	10-Jun-2024	2219	10-Jun-2024	4,000.00	Dec/2025



## 7. DATA ON FINANCIAL PERFORMANCE

### 7.1 Cumulative Disbursements

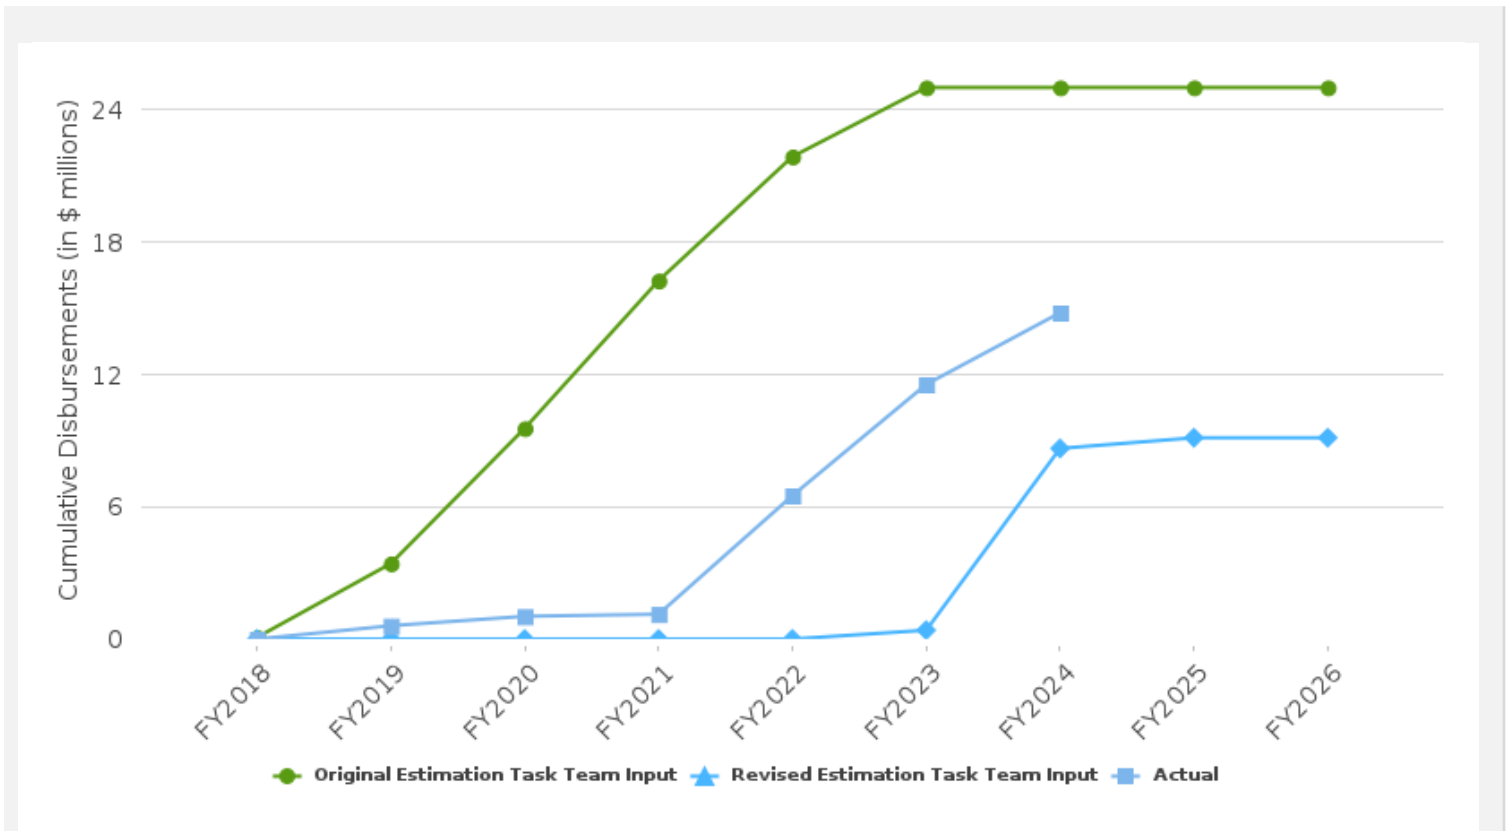

### 7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
IDA-D3280	Effective	25.00	25.00	0.00	14.79	8.22	59.15%

### 7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IDA-D3280	Effective	31-May-2018	17-Jul-2018	03-Oct-2018	31-Dec-2023	26-Dec-2025



## 8. KEY DATES

Key Events	Planned	Actual
Approval	31-May-2018	31-May-2018
Effectiveness	08-Aug-2018	03-Oct-2018
Mid-Term Review No. 01	06-Oct-2023	18-Sept-2023
Operation Closing/Cancellation	26-Dec-2025	

## 9. RESTRUCTURING HISTORY

Restructuring Level 2 Approved on 25-Jun-2021  
Restructuring Level 2 Approved on 01-Dec-2021  
Restructuring Level 2 Approved on 10-Mar-2024

## 10. ASSOCIATED OPERATION(S)

There are no associated operations
