



## Harmonizing and Improving Statistics in West Africa (P169265)

AFRICA WEST | Western Africa | Poverty and Equity Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2020 | Seq No: 3 | ARCHIVED on 22-Oct-2021 | ISR47746 |

Implementing Agencies: Ghana Statistical Service, Liberia Institute of Statistics and Geo-Information Services (LISGIS), Republic of Sierra Leone, Statistics Sierra Leone (Stats SL), Republic of Ghana, Republic of Liberia, Togo Institut National de la Statistique et des Etudes Economiques et Démographiques (INSEED), Cote d'Ivoire L'Institut national de la statistique (INS), Burkina Faso Institut National de la Statistique et de la Démographie (INSD), Republic of Cote d'Ivoire, Republic of Togo, Economic Community of West African States, Burkina Faso, Republic of Cabo Verde, African Union Commission, Cabo Verde National Institute of Statistics (INE) and the National Planning Directorate (DNP/ MF)

**Key Dates****Key Project Dates**

Bank Approval Date: 26-Mar-2020

Effectiveness Date: 13-Jul-2020

Planned Mid Term Review Date: 10-Apr-2023

Actual Mid-Term Review Date:

Original Closing Date: 31-Dec-2025

Revised Closing Date: 31-Dec-2025

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

Strengthen the statistical systems of participating countries and regional bodies in Africa to harmonize, produce, disseminate and enhance the use of core economic and social statistics.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

**Components Table**

Name
Regional component: Harmonization, Data Collection, Quality Improvement, Dissemination and Use of Core Social and Economic Statistics:(Cost \$334.21 M)
Country-Specific Component: Improving and modernizing physical and statistical infrastructure:(Cost \$27.79 M)
Project Management and Monitoring and Evaluation:(Cost \$17.00 M)

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

**Implementation Status and Key Decisions**

Detailed implementation progress:

Over the last six months, the Harmonizing and Improving Statistics in West Africa (HISWA) Project made progress despite the covid-19 pandemic continuing to affect the implementation pace and budget requirement.



Component 1: Regional Component: Harmonization, Data Collection, Quality Improvement, Dissemination and Use of Core Social and Economic Statistics.

### **1. African Union (AU):**

A virtual implementation support mission (ISM) was conducted from July 28 – 29, 2021.

**Project management:** AU Project startup activities are now on track. A Finance Officer and Procurement Specialist for the project are assigned. Systematic Tracking of Exchanges in Procurement (STEP) and Client Connection are activated. Both the project operation manual and the revised Annual Work Plan and Budget (AWPB) until December 31, 2021 were approved by the World Bank. Additionally, the draft GRM is being finalized following receipt of the World Bank's comments.

**Technical aspects:** Notwithstanding the above achievements, progress has been slow in taking forward the technical training activities.

**Recommendation:** The team recommends expediting the implementation of the planned project activities under the recently approved work plan for the next quarter. This includes the purchase of IT equipment; conducting training on National accounts, online annual meetings of Specialized Technical Groups (STGs); STG annual meetings on labor market information systems; annual STG meetings on agriculture, environment, natural resources, and climate change; and annual STG meeting on demography, migration, health, human development, social protection, and gender. The plan also covers organizing online training on the adoption of the second Strategy for the Harmonization of Statistics in Africa (SHaSA 2) in National Strategies for Development of Statistics (NSDS) through strategic planning and coordination with Regional Economic Commissions (RECs); developing statistics database and dashboard on SHaSA2 indicators.

### **2. Economic Community of West African States (ECOWAS):**

An ISM was conducted from July 1 – 2, 2021.

**Project Management:** The Regional Coordinating Unit has been formed. The evaluation for the recruitment of three staff members (Project Manager, Financial Specialist, and Procurement Specialist) is completed and already received World Bank's No Objection Notice to proceed to the interviews. The virtual launching workshop was conducted albeit incomplete because of some technical difficulties. The first Financial Interim Report has been submitted and awaiting World Bank's comments. However, the recruitment of an audit firm, which is one of the legal covenants, has been delayed. As a result, the current FM performance is rated Moderately Satisfactory. Meanwhile, the World Bank will provide technical support, including training to ECOWAS on Client Connection to assist them in submitting fund requests through the system and replenish their account. On procurement, no specific issue was raised. The World Bank mainly advised the project team on procedures to follow on STEP to complete the ongoing recruitment process.

**Technical Aspects:** The recent mission reaffirmed ECOWAS's key role in modernizing administrative data collection in the West African region. The expected leading role of ECOWAS also covers areas related to big data, poverty statistics, agricultural statistics, population statistics, and gender statistics. To that end, the mission shared presentations and brainstorm with ECOWAS staff on the latter three areas.

On Agricultural statistics, Ghana was noted to have started implementing the 50x2030 initiative to strengthen national agricultural data systems in 50 L/LMICs, and opportunities for the other project participating countries were explored. On population and housing census, IPUMS International presented the work the Minnesota Population Center (MPC) is doing in the field of harmonizing, standardizing, and anonymizing population censuses data, providing free extracts free of charge for researchers, organizing training, workshops, and knowledge exchange and capacity building activities for the NSOs and Censuses Bureau.

Performance rating on overall project management and regional coordination of the Economic Community of West African States (ECOWAS) remains unchanged. The project's Results Framework indicators will continue to be monitored by ECOWAS in coordination with project participating countries. ECOWAS had earlier decided to endorse the two indicators at the NSOs level including the Institutional Capacity Index (ICI) and Statistical Capacity Index (SCI) as part of its own M&E system of the project, but experience from the first year implementation necessitated some level of simplification before it is widely endorsed. Meetings are expected to be held over the next few months with the World Bank team to brainstorm on refining the Results Framework and provide a better explanation and understanding of the process and methodology to compute and assess these indicators.

**Recommendations:** ECOWAS will update the fields of core statistics harmonization and set up a roadmap, including poverty statistics, and consider the harmonization work implemented in the West African Economic and Monetary Union (WAEMU) countries and take all 15 countries participants into its budget consideration.

### **3. Burkina Faso:**

An ISM was conducted from July 12 – 13, 2021.

**Project management:** The procurement plan that was cleared by the World Bank is under implementation. However, progress has been slow. A number of constraints and difficulties affected the progress of the work, including among others: delay in setting up the project team, the resignation of the procurement specialist just a few weeks after taking up the position, delay in getting back proposal from some government structures implementing activities, and delays in obtaining No Objections for the implementation of some activities. The Bank team also acknowledges the workload is also heavy for the NSO.

**Technical aspects:** The main activities under implementation include the Demographic and Health Survey (DHS) and the agriculture census. The support to the improvement of administrative data in the health and education sectors has also started as well as the preparatory work for the informal sector and labor force survey. Most of these are activities are in progress albeit with some delays.

**Recommendation:** The Bank team recommended the recruitment of the procurement specialist to not lose implementation momentum and consider prioritizing and sequencing activities over time where possible to avoid overstretching the limited capacity.

### **4. Cabo Verde:**

An ISM was conducted from July 12-15, 2021.

**Project management:** The implementation of the project activities has started in May 2021 with the recruitment of the Project Manager. The procurement plan is updated and cleared by the World Bank. The General Procurement Notice (GPN) was published in the local newspaper and on United Nations Development Business (UNDB) online. A review of the project FM arrangements was undertaken with an emphasis on assessing their adequacy and follow-up on the implementation status of the agreed FM action plan. To date, the project disbursement rate was at 3.2%. An initial advance of \$500,000 was credited to the project designated account and expenditures of an amount of \$14,927 have been made to cover operating costs. The first interim financial report is shared with the World Bank for clearance and the overall performance of the project FM is



Satisfactory. The manual of procedures has been validated and the accounting software has been customized for the project bookkeeping. The recruitment of the external auditor is ongoing. An annual work plan for 2021 including disbursement revision was produced by the PIU and was approved by the World Bank. It covered all the project activities including the new activities that were subject to discussions (cadastral registry, electronic billing system, non-informal, and identification registry of informal production units). The budget associated with this work plan is estimated at US\$2.3 million corresponding to 15% of the overall project funding. Regarding the effective implementation period (September-December, 2021), the proposed budget seems to be ambitious. However, one can note that the preparation of activities is well in progress. The technical documents (Terms of References (ToR)s for the selection of firms, questionnaires, manuals) are well advanced.

**Technical aspects:** The Borrower provided clarity on the newly requested statistical activities and agreement has been reached on changes to be made on the project's activities which aim at laying the foundation for more use of administrative sources for statistics production.

**Recommendation:** Memorandum of Understanding (MOU) between UGPE and other agencies including the INE, Institute of the sea (Instituto do Mar, IMAR), and Institute of Sport and Youth (Instituto do Desporto e da Juventude, IDJ) should get initial World Bank's clearance before implementation.

#### **5. Cote d'Ivoire:**

An ISM was conducted from August 24-27, 2021.

**Project management:** An inter-ministerial decree establishing and defining the composition and the functioning of the Steering Committee and the Technical Committee of the project was signed by the Ministry of Planning, the Ministry of Budget, and the Ministry of Finance. The Steering Committee will meet by October 15. The selection process of the PIU is being finalized. The Coordinator and the Procurement Specialist have been selected while the FM and the M&E specialists have been short-listed and planned to be interviewed as soon as possible. Meanwhile, the PIU of the other World Bank governance project, "Enhancing Government Effectiveness for Improved Public Services - P164302" is assuming the day-to-day management of the project.

**Technical aspects:** The population census activities supported by the project in Cote d'Ivoire costs approximately 20 percent of the total budget of the project. The cartography was completed in January 2020. The enumeration, which was initially planned for May 2020, is now planned to be conducted from November 1st to 21st, 2021 because of the COVID-19 pandemic, the presidential elections of October 2020, and the legislative elections planned for March 2021. According to international standards, the enumeration should be completed not later than six months after the cartography. Therefore, the national institute of statistics updated the cartography in some selected regions to update the 2020 cartography data. The update of the cartography increased the initial budget of the census. Furthermore, because of the COVID-19 pandemic, the initial budget increased to account for additional costs related to social distancing and the precautionary measures needed for field operation.

The disbursement conditions linked to the population census activities are the following: (a) the beneficiary will provide proof, satisfactory to IDA, of the closing of the total census budget apart from the additional financial support of US \$ 10.8 million from the Association, (b) an evaluation of the quality of the census mapping will be carried out to certify the quality of the data necessary to carry out the enumeration phase, and (c) the beneficiary must submit to the Association a detailed timetable of the preparation activities and execution of the enumeration that can ensure the good quality of the census data. Conditions (a), (b) are fully met. The condition (c) is partially met as the Statistics Office is working to address some recommendations from the assessment mission of the cartography of the population. The team expects the NSO to address the remaining recommendations as soon as possible, and the disbursement conditions will be lifted.

**Recommendations:** The team recommends close follow-up of fulfilling the legal covenants and disbursement conditions.

#### **6. Ghana:**

An ISM was conducted from June 09 - 10, 2021.

**Project management:** The project assigned a project coordinator and financial management and procurement specialists. As part of the legal covenants, a Project Oversight Committee and a Technical Committee have also been set up. Furthermore, the Ghana Statistical Service (GSS) participated in the virtual launching of the HISWA project organized by ECOWAS on 19 April 2021.

**Technical aspects:** The main ongoing activity under the project is the 2021 population and housing census. All activities are ongoing as per the schedule and enumeration have commenced on 28th June 2021 and ended by mid-July 2021. Additional activities implemented include preparatory activities of an annual household income and expenditure survey to feed the annual national accounts. The extension of the Consumer Price Index (CPI) to the newly created regions was also supported as well as the improvement of administrative data in various Ministries, Departments, and Agencies (MDAs). Under the latter, an orientation workshop was organized for the thirteen MDAs' coordinators to strengthen the administrative data system in each of the MDA.

In September 2021, the Ghana Statistical Service released the preliminary results of the 2021 population census, which focuses on population size and sex composition, population density, and structures by region. The use of tablets for the first time at this scale in Ghana has made it possible to have these preliminary results just two months after the enumeration that started on June 28, 2021, and ended on July 11, 2021.

**Recommendations:** The GSS requested some fund reallocation between sub-components. The team recommends discussing with the client if the request can be included in the proposed project restructuring.

#### **7. Liberia:**

An ISM was conducted from June 14 - 18, 2021.

**Project management:** The project is largely on track with implementing the planned activities. The members of the Project Steering Committee (PSC) and Project Technical Committee (PTC) are selected, and the lists have been shared with the World Bank.

**Technical aspects:** The population census is facing a financing gap. In addition, there was an immediate funding gap to complete the ongoing cartographic mapping exercise, caused by the unavailability of funds that were expected to come from the United Nations Populations Fund (UNFPA), according to the initial plan in which the project finances three months of the mapping exercise and UNFPA four months. During a meeting with the Liberia Institute of Statistics & Geo-Information Services (LISGIS), UNFPA, and World Bank on June 18, 2021, all parties agreed that LISGIS will utilize funding from the project to finance the cartographic mapping exercise in order to ensure there is no further delay in the census implementation.

**Recommendations:** The team advised that the project should focus on the preparation for the population and housing census and the establishment of a GRM in anticipation of the large-scale recruitment of the Census enumerators and related staff. In addition, it is recommended that the Liberia Institute of Statistics & Geo-Information Services (LISGIS) finalize the revised annual work plan and budget.



## 8. Sierra Leone:

An ISM was conducted from May 31 – June 1, 2021.

**Project management:** After almost a year, the project implementation staff is now mostly in place. A project coordinator has been in place since November 2020 and was joined in July/August 2021 by an FM Specialist, an M&E Specialist, and an Environmental and Social Safeguards Specialist. In addition, a decision has recently been taken by the Ministry of Finance and the World Bank country office to allocate staff working for the Project Fiduciary Management Unit (PFMU) to specific projects. Under this arrangement, the project will have a dedicated Procurement Officer and Finance Officer. The overall FM performance for the project is rated as satisfactory while the FM risk rating remains Substantial. The existing FM procedures and systems at the Project Fiduciary Management Unit meet the minimum World Bank requirements for FM. As Audit Services Sierra Leone was unable to perform the external audit for the project, a private firm was selected to do the external audit, and a contract has been signed. The first external audit will cover the period from effectiveness (Sept 2020) through the end of 2021 and be done in early 2022.

Progress on safeguards issues has been slow, including establishing a GRM, Stakeholder Engagement Plan, and COVID-19 Standard Operating Procedures. Now that the Environmental and Social Safeguards Specialist is in place, the project is expected to make good progress on these issues before the end of the calendar year, with the support of the Safeguards team at the Bank. The project's social risk and E&S performance continue to be Moderate and Moderately Satisfactory respectively. The outstanding issue is the hiring of a Procurement Specialist due to some procedural issues.

**Technical aspects:** Implementation of the mid-term census continues to be a concern. During the ISM, the consensus was reached by the World Bank, Statistics Sierra Leone, and UNFPA that the planned date of mid-September was not possible, but that it was important to conduct the census before the end of the calendar year. Issues around the mid-term census were discussed at length with the Minister of Planning and Economic Development, and a timeline for conducting the main enumeration in early December 2021 was developed. Progress has been made, with the cartography fieldwork completed, and substantial progress made on the Computer-Aided Personal Interview (CAPI) application. Implementation is falling behind the timeline agreed, however, as the pilot census is still several weeks away, and serious challenges in management and coordination of this activity remain. In addition, the cartography process resulted in 30% more enumeration areas than expected, which would significantly increase the budget and the number of tablets needed to be borrowed. Given the focus on the mid-term census, very little has been accomplished with respect to the other project activities as laid forth in the Annual Work Plan.

**Recommendations:** The team recommends expediting the hiring of the Procurement Specialist.

## 9. Togo:

An ISM was conducted from May 25 - 28, 2021.

**Project management:** A virtual project launch took place on Thursday, May 27, 2021, under the effective chairmanship of Mrs. Sandra Ablamba Johnson, Minister Secretary-General at the Presidency in the presence of Mrs. Hawa Cissé Wagué, World Bank Resident Representative. All the specialists have now been recruited and officially started work in June 2021 albeit with a delay of one month. No Objection has been provided for the recruitment of the Internal Auditor. The dated covenants are almost all completed. The Project Coordination Committee meets regularly, and its meetings are documented in minutes. The client is informed about the World Bank social safeguards issues, i.e., the provisions for proper conduct in the event of incidents or accidents, and that these provisions are documented in various documents such as surveyors' manuals, insurance contracts. The social safeguards specialist asked to review these documents and to provide any additional input if necessary. The INSEED is informed of the existence of the document developed by the United Nations and World Bank on data collection in times of the COVID-19 pandemic for all consultations and surveys to be conducted under the project. The safeguards risk is rated Moderate and its performance is satisfactory.

**Technical aspects:** The activities included in the AWP 2021 have not yet started due to the delay in the implementation of urgent activities that condition the execution of the activities of the action plan. The census cartography has now started, thanks to efforts made by the World Bank to provide technical assistance to INSEED.

The SCI is rated at 66.66 points out of a total of 100 compared to a value of 60 at the start of the project. This improvement is not attributable to the project, however, and the team recommended that the project implement subcomponents that would not only maintain the SCI dimensions in focus but also those that have not changed. The ICI remained unchanged at 20 out of a total of 100. This indicator will be much more impacted by the implementation of institutional and human resource reform activities.

**Recommendations:** i) the establishment of a network of "Technical Assistants" from the structures that are supporting the fifth population and housing census (Sieme Recensement Général de la Population et de l'Habitat, RGPH-5) financially and technically in order to allow for a better exchange of information and greater efficiency; ii) drawing the attention of stakeholders to the improvement and modernization of data collection using new technologies and innovative methods for the ongoing activities to be carried out in 2021, and iii) the development of a GRM document in the next two months based on INSEED's Human Resources Division and sample documents that the World Bank will share with the Project Management Unit; iv) improved project results framework be put in place as a matter of urgency, given that the monitoring and evaluation specialist has been recruited and will be operational at the beginning of June 2021

## Risks

### Systematic Operations Risk-rating Tool



Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	☐ Moderate	☐ Low	☐ Low
Macroeconomic	☐ Moderate	☐ Moderate	☐ Moderate
Sector Strategies and Policies	☐ Moderate	☐ Moderate	☐ Moderate
Technical Design of Project or Program	☐ High	☐ Substantial	☐ Substantial
Institutional Capacity for Implementation and Sustainability	☐ Substantial	☐ Substantial	☐ Substantial
Fiduciary	☐ Substantial	☐ Moderate	☐ Moderate
Environment and Social	☐ Moderate	☐ Moderate	☐ Moderate
Stakeholders	☐ Moderate	☐ Low	☐ Low
Other	--	☐ Substantial	☐ Substantial
Overall	☐ Substantial	☐ Substantial	☐ Substantial

## Results

### PDO Indicators by Objectives / Outcomes

Strengthening statistical systems.				
▶ Modified Statistical capacity index (SCI 2.0) (disaggregated by participating countries) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	50.00	50.00	50.00	65.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	<p>A composite score assessing the capacity of a country's statistical system, based on a diagnostic framework assessing the methodology; data sources; and periodicity and timeliness. There will be no change under this PDO-level indicator because it was difficult to obtain updated SCI data from some of the project beneficiary countries including Ghana, Sierra Leone, Liberia, Burkina Faso and Cabo Verde. The update was not possible as there is some baseline calculation data missing. Due to these reasons, the project is planning to conduct a Level 2 restructuring.</p>			
☐ Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	65.00	65.00	75.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
☐ Liberia (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	50.00	50.00	50.00	65.00



Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	50.00	50.00	50.00	65.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	60.00	60.00	66.60	75.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	55.00	55.00	55.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	70.00	70.00	70.00	75.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	65.00	65.00	75.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Share of beneficiary countries (National Statistical Office) that score at least 30 out of 50 for the ICI. (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	The ICI is designed to conduct systematic functional reviews to identify and analyze an Institution's capacity across three areas: (i) staffing and human resources policies; (ii) management, incentive, and institutional arrangements; and (iii) knowledge and learning (competencies, learning plans, knowledge systems). Each area is composed of technical indicators that are measured systematically. The maximum score of each area is 50 and the overall ICI is the average the scores of the three areas. The ICI indicator			



does not apply for all beneficiary countries and not all three areas are covered by the activities of the project.  
This PDO-level indicator will be removed and some of its measurements will be moved to intermediate results indicators. This is mainly because ICI does not apply to all beneficiary countries, and some of the scores under the measurement are subjective to the score evaluator. Additionally baseline data is missing for Ghana, Liberia, Sierra Leone and Cabo Verde.

Ghana (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.00	20.00	20.00	30.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Liberia (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	30.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Sierra Leone (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	30.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Burkina Faso (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.00	20.00	20.00	30.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Togo (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.00	20.00	20.00	40.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Cote d'Ivoire (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	23.60	23.60	24.30	35.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025



Production and dissemination of harmonized statistics				
► Share of comparable core economic and social statistics indicators produced and available for open access (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	The indicators to be considered are the following: (i) Population size by region and areas of residence, (ii) Poverty indices, (iii) Inflation rates, (iv) Production volume of main staple crops, (v) Value added of SMEs and MSMEs, (vi) Gross domestic product growth and (vii) underemployment rate. Open access means available to the users on a website. Statistics are comparable when produced using similar methodologies.			
☐ Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	30.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
☐ Liberia (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
☐ Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
☐ Togo (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
☐ Cabo Verde (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025





<input type="checkbox"/> Burkina Faso (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Share of comparable core economic and social statistics datasets produced and available for open access (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	The list datasets include: (1) Anonymized cartography dataset; (2) Anonymized household poverty survey, (3) CPI dataset, (4) Anonymized agricultural census or annual survey dataset, (5) Anonymized updated business registry, (6) Input-output tables, and (7) Anonymized labor force surveys dataset. Open access means available to the users on a website or upon request. Statistics are comparable when produced using similar methodologies.			
<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Percentage, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Share of statistical products produced and published by the NSO following international standards and a predetermined release calendar (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	Core economic and social statistics include household poverty survey (Poverty indices), CPI (Inflation rate), agricultural census and annual survey data (agricultural production), economic census and annual survey data, national accounts (GDP growth rate), and labor force surveys ( underemployment rate). For each statistical output of a subset of the core economic and social statistics, a methodological manual or guideline is produced or applied based on international standards, and a release calendar is set and adopted by all countries.			
<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	28.00	28.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	14.00	14.00	14.00	43.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	14.00	14.00	14.00	43.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	28.00	28.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	28.00	28.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	28.00	45.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	28.00	28.00	70.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

Enhance the use of statistics

► Share of countries that produce and disseminate at least two analytical reports using survey, macro or administrative data. (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025



Comments:	The analytical reports are those produced using population data, households surveys data, labor force surveys, enterprise or agricultural surveys data, macroeconomic data including national account, price data. the reports include but not limited to economic updates, economic projections and shocks policy impact analysis.			
<b>► Increase in user satisfaction index (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	The user satisfaction index will be computed from user surveys. A baseline survey will be conducted the first year of the project and follow-up surveys in years three and five. This indicator will measure the change in percentage points from baseline.			
<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	21-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025



<input type="checkbox"/> Burkina Faso (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	02-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025

### Intermediate Results Indicators by Components

Harmonization, Data Collection, Quality Improvement, Dissemination and Use of Core Statistics				
▶ Manuals on reprocessing and adjustment methodologies adopted for producing and managing all core economic and social statistics (disaggregated by participating countries) (Yes/No) (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	A manual is adopted if it is used in a specific statistical survey or to construct a specific index (GDP, CPI) Idem as above at the regional level			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes



Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Regional platform built or updated that enables data access, archiving and dissemination (Yes/No) (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	Idem as above at the regional level			
<b>► Number of UNSD Minimum List gender indicators available using data collected within the past 5 years (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	78.00	78.00	78.00	132.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	7.00	7.00	7.00	12.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	18.00	18.00	18.00	24.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	17.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	3.00	3.00	3.00	18.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote d'Ivoire (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	5.00	5.00	5.00	16.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	18.00	18.00	18.00	22.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	17.00	17.00	17.00	23.00
Date	22-Jan-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025



Component 2: Country-Specific Component				
<b>► Number of analytical reports produced and disseminated using survey, macro or administrative data per country (Text, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0 for all countries	No report	No report	3 reports per country
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► NSS staff trained to produce welfare and macroeconomic statistics (disaggregated by participating countries) (number) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	Number of staff trained to use CAPI in censuses (population, enterprises, agriculture) and surveys (household, LFS, enterprises, agriculture) and in CPI data collection. Staff might be from NSO or any line ministry supported by the project.			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025





<input type="checkbox"/> Burkina Faso (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote d'Ivoire (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	15.00
Date	04-Mar-2020	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Months between end of data collection and dissemination of main report (disaggregated by participating countries) (number) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	12.00	12.00	12.00	8.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	Average number of months between the end of data collection of major surveys and the release of the main results. The surveys to be consider are household surveys, LFS, agriculture surveys and enterprises surveys			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	6.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	12.00	12.00	12.00	8.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	12.00	12.00	12.00	8.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	10.00	10.00	10.00	6.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	12.00	12.00	12.00	8.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	6.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	10.00	10.00	6.00
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<p>► Internationally accepted statistical concepts, definitions and standards are used for data compilation and validation (disaggregated by participating countries) (Yes/No) (Yes/No, Custom)</p>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	The concepts and standards are the one adopted with ECOWAS (NSNA 2008, harmonized methodology for the CPI, harmonized methodology for enterprises surveys) and FAO (AGRI surveys)			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025



<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote D'Ivoire (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<b>► Data Quality Assessment Framework developed (Yes/No) (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	An assessment of data quality is developed and applied in the country A calendar of dissemination of the main statistical products (CPI, national accounts, labor statistics, agricultural production, etc.) is developed and adopted			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	No	No	Yes	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cote d'Ivoire (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
▶ Data release calendar updated regularly (Yes/No) (Yes/No, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
Comments:	A calendar of dissemination of the main statistical products (CPI, national accounts, labor statistics, agricultural production, etc.) is developed and adopted			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	Yes	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Liberia (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Togo (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Cabo Verde (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025
<input type="checkbox"/> Burkina Faso (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025



Cote d'Ivoire (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Nov-2019	15-Jan-2021	23-Sep-2021	31-Dec-2025

## Performance-Based Conditions

### Data on Financial Performance

#### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P169265	IDA-65730	Effective	USD	30.00	30.00	0.00	0.00	31.63	0%
P169265	IDA-65740	Effective	USD	15.00	15.00	0.00	0.50	15.22	3.2%
P169265	IDA-65750	Effective	USD	54.00	54.00	0.00	4.64	54.93	7.8%
P169265	IDA-65760	Effective	USD	150.00	150.00	0.00	80.20	75.27	52%
P169265	IDA-65770	Effective	USD	15.00	15.00	0.00	1.19	13.81	7.9%
P169265	IDA-65780	Effective	USD	15.00	15.00	0.00	0.00	15.87	0%
P169265	IDA-D5810	Effective	USD	30.00	30.00	0.00	7.46	23.25	24%
P169265	IDA-D5820	Effective	USD	7.50	7.50	0.00	0.50	7.44	6.3%
P169265	IDA-D5830	Effective	USD	15.00	15.00	0.00	4.58	10.94	29%
P169265	IDA-D5840	Effective	USD	30.00	30.00	0.00	9.23	21.67	30%
P169265	IDA-D5850	Effective	USD	15.00	15.00	0.00	2.23	13.32	14%
P169265	IDA-D5880	Effective	USD	2.50	2.50	0.00	0.00	2.73	0%


#### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P169265	IDA-65730	Effective	26-Mar-2020	04-May-2020	09-Oct-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-65740	Effective	26-Mar-2020	30-Jun-2020	28-Sep-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-65750	Effective	26-Mar-2020	05-May-2020	31-Aug-2020	31-Dec-2025	31-Dec-2025



P169265	IDA-65760	Effective	26-Mar-2020	24-Apr-2020	13-Jul-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-65770	Effective	26-Mar-2020	29-Apr-2020	02-Dec-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-65780	Effective	26-Mar-2020	18-May-2020	11-Aug-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5810	Effective	26-Mar-2020	04-May-2020	09-Oct-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5820	Effective	26-Mar-2020	19-May-2020	13-Aug-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5830	Effective	26-Mar-2020	29-Apr-2020	02-Dec-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5840	Effective	26-Mar-2020	03-Apr-2020	10-Sep-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5850	Effective	26-Mar-2020	18-May-2020	11-Aug-2020	31-Dec-2025	31-Dec-2025
P169265	IDA-D5880	Effective	26-Mar-2020	11-Sep-2020	25-Nov-2020	31-Dec-2025	31-Dec-2025

**Cumulative Disbursements**

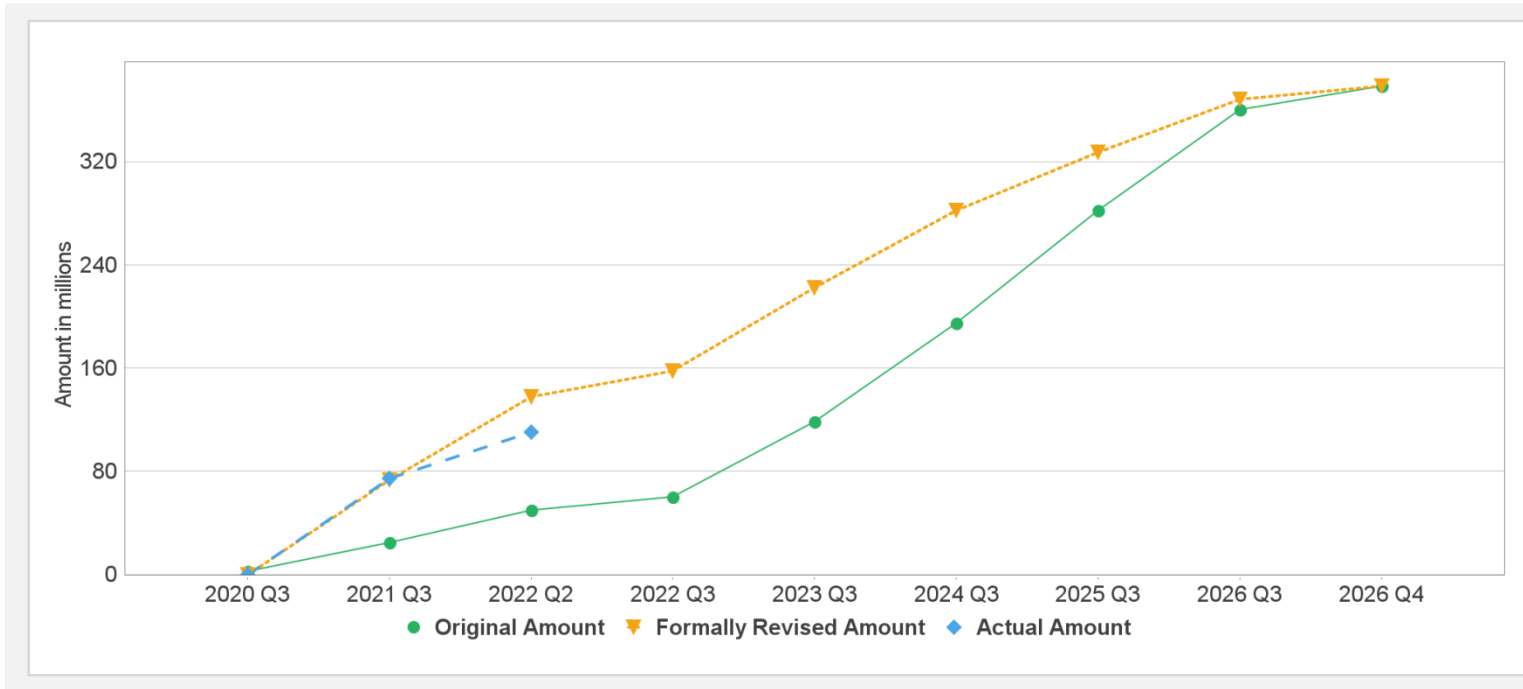

**PBC Disbursement**

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC



---

### **Restructuring History**

There has been no restructuring to date.

### **Related Project(s)**

There are no related projects.

---
