



## Central African Republic - LONDO Project (P152512)

AFRICA WEST | Central African Republic | Social Sustainability & Inclusion Global Practice |  
IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 11 | ARCHIVED on 28-Jan-2021 | ISR45333 |

Implementing Agencies: Ministry of Economy, Planning, and Cooperation, LONDO+ Project Implementation Unit

### Key Dates

#### Key Project Dates

Bank Approval Date: 30-Jul-2015

Effectiveness Date: 29-Sep-2015

Planned Mid Term Review Date: 15-Nov-2017

Actual Mid-Term Review Date: 15-Dec-2017

Original Closing Date: 31-Dec-2018

Revised Closing Date: 30-Jul-2024

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To provide temporary employment to vulnerable people throughout the entire territory of the country.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

To provide temporary employment to vulnerable people and to facilitate access to basic services throughout the entire territory of the Recipient, and to provide a response in the case of an eligible crisis or emergency.

### Components Table

Name

Local Governance:(Cost \$7.50 M)

Public Infrastructure:(Cost \$29.60 M)

Socio-Economic Integration:(Cost \$29.80 M)

Project Management:(Cost \$6.65 M)

Contingency (3%): to be allocated to Components 1, 2, and 3:(Cost \$1.45 M)

CERC

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> High

### Implementation Status and Key Decisions

#### Overproduction of non-surgical masks:

Project reports received by the task team revealed a total of 7 million surplus masks produced without any clearance from the World Bank.



The government went ahead to request World Bank support to cover the deficit, as the situation has caused animosity and strife between the Government, the PIU and the disgruntled sewing workshops who are waiting for final payments of the masks they produced. The World Bank responded to the Government in a letter dated November 12, 2020 stating that it would not take responsibility for the surplus production and that the Government should instead cover the deficit. In addition, the task team has asked the PIU to commission an audit in order to understand how the large surplus masks were erroneously produced.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	High	High	High
Macroeconomic	Substantial	Substantial	Substantial
Sector Strategies and Policies	Moderate	Moderate	Moderate
Technical Design of Project or Program	Substantial	Substantial	Moderate
Institutional Capacity for Implementation and Sustainability	High	High	Moderate
Fiduciary	High	High	High
Environment and Social	Moderate	Moderate	Moderate
Stakeholders	Substantial	Substantial	Moderate
Other	--	--	--
Overall	High	High	High

## Results

### PDO Indicators by Objectives / Outcomes

Improve access				
▶ Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	41,349.00	41,349.00	148,749.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024
□ Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	38.00	38.00	40.00
-------	------	-------	-------	-------

Expand public services				
▶ Benefitting districts (sous-prefectures) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	70.00	70.00	124.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024

Promote resilience				
▶ Worked days (men-days) (Days, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1,499,194.00	1,499,194.00	6,975,895.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024

#### Overall Comments

The project has been suspended because of the pandemic, therefore no change in the figures of June 24, 2020.

#### Intermediate Results Indicators by Components

Local Governance				
▶ Rapid development assessments (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	94.00	94.00	149.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024
▶ Grievances registered related to delivery of project benefits addressed (%) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024



Public Infrastructure				
<b>► Road maintenance (Kilometers, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,296.04	2,296.04	4,663.78
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► New or rehabilitated community infrastructures (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	180.00
Date	01-Jul-2019	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► Infrastructures built via the chantier-école method (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	23.00
Date	01-Jun-2019	24-Jun-2020	24-Jun-2020	30-Jun-2024
Socio-Economic Integration				
<b>► Distribution of stipends (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	318.00	318.00	792.00
Date	01-Jan-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► Local private firms or NGOs contracted to train beneficiaries on community works (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	01-Jul-2019	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► Direct beneficiaries of LIPW (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	38,000.00	38,000.00	129,250.00



Date	01-Jul-2015	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► Direct beneficiaries of chantiers-écoles (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1,499.00
Date	01-Jul-2019	24-Jun-2020	24-Jun-2020	30-Jun-2024
<b>► Number of sewing workshops contracted to organize and train the mask makers (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	57.00	57.00	360.00
Date	20-May-2020	24-Jun-2020	24-Jun-2020	30-Jun-2021
<b>► Direct beneficiaries remunerated to produce the non-medical masks (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3,349.00	3,349.00	18,000.00
Date	20-May-2020	24-Jun-2020	24-Jun-2020	30-Jun-2021
<b>► Number of non-medical masks manufactured by the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	544,203.00	544,203.00	10,000,000.00
Date	20-May-2020	24-Jun-2020	24-Jun-2020	31-Dec-2020

#### Overall Comments

The project has been suspended because of the pandemic, therefore no change in the figure of June 24, 2020.

#### Performance-Based Conditions

#### Data on Financial Performance

#### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
---------	----------------	--------	----------	----------	---------	-----------	-----------	-------------	-------------




P152512	IDA-D0800	Effective	USD	20.00	20.00	0.00	19.93	0.00	<div style="width: 100%; height: 10px; background-color: green;"></div>	100%
P152512	IDA-D4810	Effective	USD	100.00	75.00	25.00	30.46	45.84	<div style="width: 45.84%; height: 10px; background-color: #76b82a;"></div>	40%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P152512	IDA-D0800	Effective	30-Jul-2015	26-Aug-2015	29-Sep-2015	31-Dec-2018	30-Jul-2024
P152512	IDA-D4810	Effective	30-May-2019	27-Jun-2019	24-Sep-2019	30-Jul-2024	30-Jul-2024

**Cumulative Disbursements**

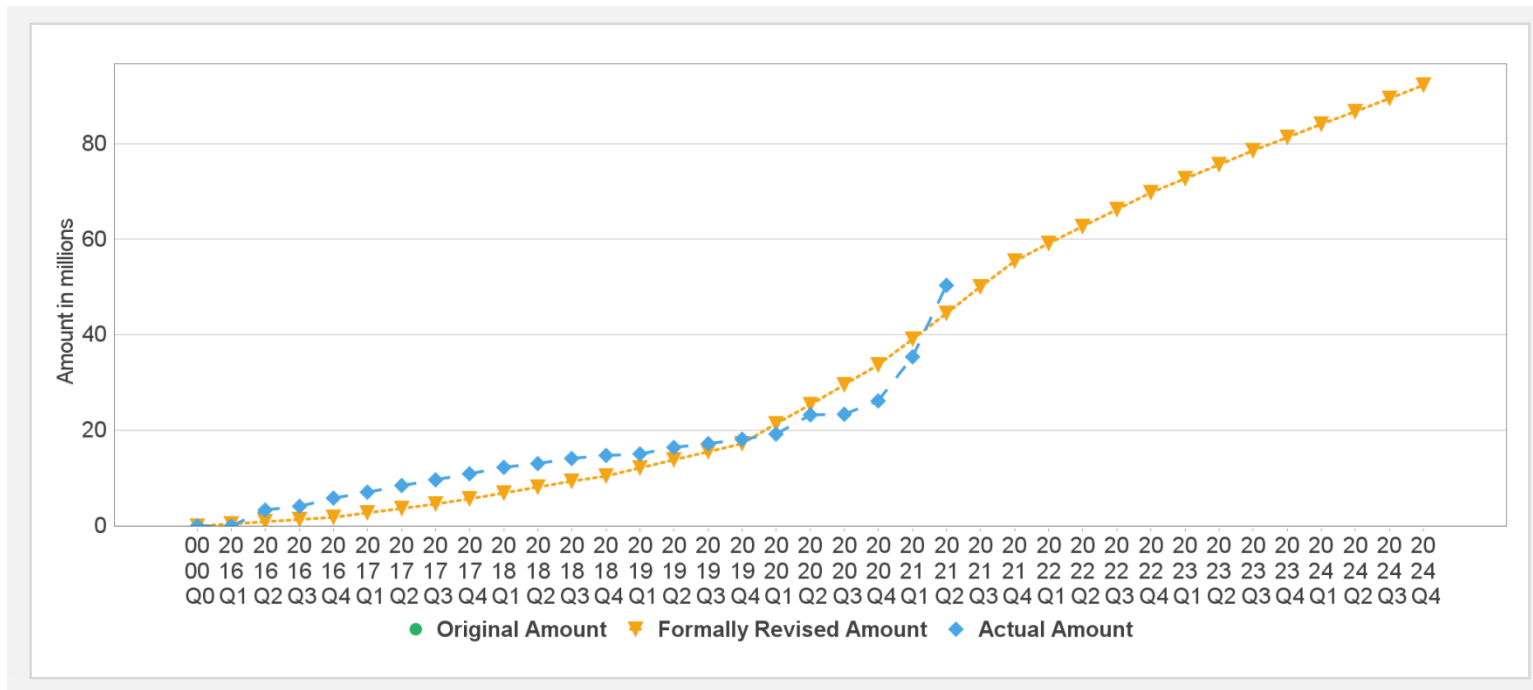

**PBC Disbursement**

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC

**Restructuring History**

Level 2 Approved on 03-Dec-2018 ,Level Approved on 08-Jun-2020

**Related Project(s)**



---

P166943-CAR: LONDO "Stand Up" Project

---
