



Governance of Extractives for Local Development & COVID-19 response Project (P164271)

AFRICA WEST | Niger | Governance Global Practice |
IBRD/IDA | Investment Project Financing | FY 2021 | Seq No: 2 | ARCHIVED on 29-Jun-2021 | ISR46750 |

Implementing Agencies: Republic of Niger, Ministry of Planing

Key Dates**Key Project Dates**

Bank Approval Date: 03-Aug-2020

Effectiveness Date: 31-Mar-2021

Planned Mid Term Review Date: 16-Jan-2023

Actual Mid-Term Review Date:

Original Closing Date: 31-Jul-2025

Revised Closing Date: 31-Jul-2025

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to strengthen local governments' capacity and extractive sector management for service delivery in the targeted regions.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name
Strengthening Local Government Capacity:(Cost \$59.00 M)
Improving extractive sector's management:(Cost \$37.00 M)
Project management:(Cost \$4.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> Substantial

Implementation Status and Key Decisions

The Governance of Extractives for Local Development & COVID-19 Response Project was approved for the amount of US\$100 million by the Board of Directors of the World Bank on August 3, 2020. The project was signed by the Government of Niger on August 14, 2020 and became effective on March 31, 2021.

The Project's development objective is to strengthen local governments' capacity and extractive sector management for service delivery in the targeted regions of Agadez, Diffa, Tillabéry and Zinder which are the main extractive regions; and also, currently facing fragility.

The project through a combination of Performance Based Conditions (PBCs) and Technical Assistance (TA) aims to support government reforms notably, the TA will finance, inter alia, expertise to improve the legal framework, strategies and processes, software and training manuals as well as conflict monitoring and harmonizing early warning mechanisms. Meanwhile, PBCs will provide incentives for the implementation of policies, laws and regulations related to state deployment, COVID-19 coordination mechanism and extractive sector management.



The year 2020 was a challenging year for project implementation. The COVID-19 pandemic and preparation for national elections contributed to significant delays in recruitment of Project Implementation Unit (PIU) staff and project preparation activities, including key preparatory studies that aim to inform project technical assistance. Despite these delays, the establishment of the Steering Committee and PIU were secured by end of March 2021 and key studies are close to finalization and will inform the call for proposals for TA on Decentralization and Geology data and Artisanal Mining pilot. For 2020, four (4) Performance based conditions were due to be achieved, namely:

- i. PBC 1.1 on the Local Government Code and Civil service texts on HRM: the adoption in 2020 of texts and decrees in CY 2020 (US\$6 million). All of the decrees have been drafted in 2020, however, because of the national elections, these are not yet adopted.
- ii. PBC 2.1 on the Inter-ministerial decision on modalities for allocation and execution of extractive revenues (US\$4 million) is being drafted.
- iii. PBC 5.1 and 5.2 on the Effective central-local coordination mechanism for COVID-19 emergency response (US\$12 million). This PBC has been achieved and is pending verification.
- iv. PBC 6.1 on Inspection Manuals of the Ministries of Education, Health and Hydraulics for CY 2020 (US\$0.5 million) is pending submission to the World Bank.

The project's progress towards achievement of the PDO and its overall project implementation progress are rated as Moderately Satisfactory

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	High	High	Substantial
Macroeconomic	High	High	High
Sector Strategies and Policies	Moderate	Moderate	Moderate
Technical Design of Project or Program	Substantial	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	High	High	High
Fiduciary	Substantial	Substantial	Substantial
Environment and Social	Substantial	Substantial	Substantial
Stakeholders	Substantial	Substantial	Substantial
Other	High	High	High
Overall	High	High	Substantial

Results

PDO Indicators by Objectives / Outcomes

Strengthen Local Government Capacity				
► Increased access to water, primary education and health services in the targeted regions (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Unsatisfactory: 30.6 percent of population	Unsatisfactory: 30.6 percent of population	Unsatisfactory: 30.6 percent of population	Improved: 40 percent of population with



	with access to drinkable water point, 31.3 students per teacher, 52.52 percent of population with integrated health center within 5km	with access to drinkable water point, 31.3 students per teacher, 52.52 percent of population with integrated health center within 5km	with access to drinkable water point, 31.3 students per teacher, 52.52 percent of population with integrated health center within 5km	access to drinkable water point, 25 students per teacher, 60 percent of population with integrated health center within 5km
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	01-Jan-2024
Comments:	This indicator measures the access to service in the four targeted regions for primary education, health and water and disaggregated in sub-indicators.			
<input type="checkbox"/> For Water: population with access to drinkable water point (Text, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	30.6 percent	30.6 percent	30.6 percent	40 percent
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	31-Mar-2025
<input type="checkbox"/> For Education: reduced student per teacher ratio (Text, Custom Breakdown, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	31.30	31.30	31.30	25.00
Date	01-Sep-2016	03-Nov-2020	30-Apr-2021	30-Jun-2025
<input type="checkbox"/> For Health: population with integrated health centers within 5 km (Text, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	52.52 percent	52.52 percent	52.52 percent	60 percent
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	31-Mar-2025
<input checked="" type="checkbox"/> Improved municipalities budget execution rate in the targeted regions (Percentage, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	38.00	38.00	38.00	50.00
Date	31-Oct-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	This indicator is the average of the annual budget execution rate of municipalities of the targeted regions			
<input checked="" type="checkbox"/> Increased extractives revenues transferred to LG (Percentage, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	54.00	54.00	54.00	70.00
Date	29-Nov-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Transfers of the 15 percent extractive sector taxes to LG include (i) the 2009-2017 arrears plan execution expected in 2018-2022 and (ii) the annual 15 percent following 2017 (i.e. 2018 and onwards).			



Improve extractive sector's management				
▶ Increased requests for mining exploration permits (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	59.00	59.00	59.00	139.00
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	30-Jun-2025
Comments:	Number of mining exploration permits' request registered (cumulative)			
▶ Increased artisanal miners under valid mining permit and trained on environmental and social good practices (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5,000.00
Date	01-Jan-2020	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Number of artisanal miners who benefited from at least 4 days training on both social and environmental safeguards and active under a valid authorization for mining exploitation			
□ of which women (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2,000.00
Date	01-Jul-2020	03-Nov-2020	30-Apr-2021	30-Jun-2025

Intermediate Results Indicators by Components

Strengthening Local Government Capacities				
▶ Public officials trained on LG's PFM & HRM, conflict mediation & Citizen Engagement (Number, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,000.00
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Number of public officials who benefited from a training from the CFGCT on HRM or PFM or citizen engagement or conflict mediation			
□ Of which percentage are women (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00



► National report on drivers of conflict produced, incl. perceptions (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4.00
Date	29-Nov-2019	03-Nov-2020	30-Apr-2021	31-Mar-2025
Comments:	Report published by the CNESS on drivers of conflict			
► Municipality's own tax recovery rate (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	30.00	0.00	0.00	60.00
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Average of the own-source tax recovery rate of the municipalities in the targeted regions			
► Beneficiaries' satisfaction (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Average satisfaction rate (satisfied and very satisfied) of the beneficiaries of trainings programs for both components: decentralization and extractives.			
<input type="checkbox"/> Women beneficiaries' satisfaction (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
► Citizens in the targeted regions who are aware of their municipality's annual investment projects plan and think it corresponds to their priorities (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	30-Jun-2025
Comments:	This indicator aims to measure the level of engagement of citizens in their commune as well as their satisfaction of their commune' spending			
<input type="checkbox"/> Women in the targeted regions who are aware of their municipality's annual investment projects plan and think it corresponds to their priorities (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00



► Inter-ministerial decision on modalities for allocation and execution of extractive revenues adopted (Yes/No, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	15-Jun-2020	03-Nov-2020	30-Apr-2021	31-Dec-2020
Comments:	Adoption of interministerial decision on modalities for the allocation & execution of the extractive revenue transferred to LG			
► Increased spending of targeted municipalities in targeted sectors (Percentage, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	200.00
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	This indicator measures the percentage increase of total annual spending of all municipalities in the targeted regions in the targeted sectors (primary education, health, water) compared to 2019 baseline.			
► Effective central-local COVID-19 emergency response coordination mechanism (Text, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	no coordination between local level and central level	no coordination between local level and central level	Regional coordination centers have been created to implement coordination mechanisms between local level and central level	COVID-19 response coordination mechanism are effective with regular reporting from regional crisis management cells
Date	11-Mar-2020	03-Nov-2020	30-Apr-2021	30-Sep-2020
Comments:	The indicator measures the effective coordination mechanism of the COVID-19 emergency response with the creation of regional COVID-19 crisis management cells, the production of report to the central level			
► Increased impact of Inspection missions in targeted social sectors (Number, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	300.00
Date	01-Jun-2020	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	The indicator measures the number of local public structures (from front-line service delivery providers to local public administration) in the targeted sectors (primary education, health, water) which implemented >70 percent of inspections recommendations.			
Improving extractive sector management				
► Geographical coverage of geological knowledge (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	12.86	12.86	12.86	17.86
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	30-Jun-2025
Comments:	The indicator seeks to increase the geological knowledge throughout the country, with geological mapping at 1/200,000			
► Adoption of mine closure strategy (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	15-Dec-2022
Comments:	This indicator measures the adoption of the GoN mine closure strategy along with its implementation road map			
► Adoption of Local content strategy for extractives (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	31-Dec-2023
Comments:	This indicator measures the adoption of the GoN Local content strategy for the extractives sector			
► Increased women leadership in targeted ASM sites (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	30-Sep-2019	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	Women leadership in ASM management is the increase of women in decision-making roles in ASM sites, within the ASM value chain in this ASM site, as well as business around the ASM site.			
► EITI compliance to new standard (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Jan-2020	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	This indicator reflects the government's commitment to make the extractive sector transparent by making key information on mining and oil management accessible to the public			
► Perceptions of extractive firms on legal system and geo-data management as encouraging investment (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00



Date	01-Jun-2020	03-Nov-2020	30-Apr-2021	28-Jun-2024
Comments:	The indicator will measure the perceptions of extractive firms on Niger's legal system and geo-data management, and whether it encourage private sector investment or do not deter it.			
► Increased impact of mining sites' inspection (Number, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	150.00
Date	01-Jun-2020	03-Nov-2020	30-Apr-2021	31-Dec-2024
Comments:	This indicator measures the number of mining permit holders who have been subject to inspection mission and implemented >70 percent of recommendations.			
► Increased formalization of artisanal and small scale mining sites (Number, Custom, PBC)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	168.00	168.00	168.00	568.00
Date	31-Dec-2019	03-Nov-2020	30-Apr-2021	31-May-2025
Comments:	The indicator measures the number of artisanal and small scale mining permits registered by the ministry of mines in compliance with the mining code.			

Project Management				
► Grievances received and addressed timely by the project (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	30-Jun-2020	03-Nov-2020	30-Apr-2021	27-Dec-2024
Comments:	This indicator measures the percentage of grievances and received and processed by the PIU within the delay set in the PIM.			

Performance-Based Conditions

► PBC 1 PBC 1. Operational municipalities & decentralized services with adequately trained staff (Text, Output, 21,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	Legal framework for LG HRM incomplete, municipalities staffing inadequate, training at scale not rolled up yet	Text are currently being finalized and will be sent to the parliament for approval by December.	Text are currently being finalized and will be sent to the parliament for approval by June 30, 2021.	Legal framework for LG HRM is adopted; and Staff is trained and certified and at post.



Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 1.1 PBR 1.1 (i) the application decrees of the Local Civil Service Law and (ii) revised manual for payroll process have been adopted in a manner satisfactory to the Association in CY20 (Yes/No, Output, 6,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	No	No	No	Yes
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 1.2 Public officials trained on LG's PFM & HRM, conflict mediation & Citizen Engagement (Number, Intermediate Outcome, 15,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

►PBC 2 PBC 2: Effective mechanism for extractive revenue transfer to LG (Text, Output, 8,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	limited transfer and opacity on allocation	limited transfer and opacity on allocation	limited transfer and opacity on allocation	increased transfer of extractive revenue to LG
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 2.1 Inter-ministerial decision on modalities for allocation and execution of extractive revenues adopted (Yes/No, Intermediate Outcome, 4,000,000.00, 4%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	No	No	No	--
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 2.2 Increased extractives revenues transferred to LG (Percentage, Outcome, 4,000,000.00, 4%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	54.00	54.00	54.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

►PBC 3 Improved municipalities budget execution rate in the targeted regions (Percentage, Intermediate Outcome, 3,000,000.00, 3%)				
------------------------------------------------------------------------------------------------------------------------------------------	--	--	--	--



	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	38.00	38.00	38.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

► PBC 4 PBC 4: Improved LG capacity for better service delivery in the targeted sectors (Text, Outcome, 4,000,000.00, 0.00%)

	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	limited capacity of LG to improve service delivery	limited capacity of LG to improve service delivery	limited capacity of LG to improve service delivery	Increased capacity of LG to improve service delivery
Date	--	03-Nov-2020	03-Nov-2020	--

□ PBC 4.1 Increased spending of targeted municipalities in targeted sectors (Percentage, Intermediate Outcome, 2,000,000.00, 2%)

	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

□ PBC 4.2 For Education: reduced student per teacher ratio (Text, Outcome, 2,000,000.00, 0.00%)

	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	31.30	31.30	31.30	--
Date	--	03-Nov-2020	30-Apr-2021	--

► PBC 5 Effective central-local COVID-19 emergency response coordination mechanism (Text, Output, 12,000,000.00, 0.00%)

	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	no coordination between local level and central level	no coordination between local level and central level	Regional coordination centers have been created to foster coordination between local level and central level	--
Date	--	03-Nov-2020	30-Apr-2021	--

□ PBC 5.1 PBR 5.1 8 regional COVID-19 crisis management cells established in accordance with ministerial decision 052/PM of March 20,2020 and operational in a manner satisfactory to the Association in CY20 (Number, Output, 10,000,000.00, 0.00%)

	Baseline	Actual (Previous)	Actual (Current)	December 2024
--	----------	-------------------	------------------	---------------



Value	0.00	0.00	8.00	8.00
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 5.2 PBR 5.2 The 8 regional COVID-19 crisis management cells have provided to the Recipient's central COVID-19 crisis management cell cumulatively 80 weekly reports to central level since establishment (Percentage, Intermediate Outcome, 2,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	80.00	80.00
Date	--	03-Nov-2020	30-Apr-2021	--

<input checked="" type="checkbox"/> PBC 6 PBC 6: Increased impact of inspection missions and coordination with LG in targeted sectors (Text, Intermediate Outcome, 4,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	limited missions with no impact	limited missions with no impact	limited missions with no impact	increased inspection of services and active monitoring of recommendations
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 6.1 PBR 6.1 The Recipient has prepared and adopted Inspection Manuals satisfactory to the Association in CY20 (Text, Intermediate Outcome, 500,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	Inspections Manuals not yet adopted	Not yet adopted	Not yet adopted	Inspection Manuals adopted
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 6.2 PBR 6.2 At least 200 Public Entities have been inspected annually using the Inspection Manual by end of each CY in (i) CY21, (ii) CY22, (iii) CY23 (Number, Intermediate Outcome, 1,500,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	600.00
Date	--	03-Nov-2020	30-Apr-2021	--
<input type="checkbox"/> PBC 6.3 Increased impact of Inspection missions in targeted social sectors (Number, Outcome, 2,000,000.00, 2%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	--
Date	--	03-Nov-2020	30-Apr-2021	--



► PBC 7 PBC 7: Increased impact of inspection missions of mining sites (Text, Intermediate Outcome, 5,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	limited inspection, limited follow up	limited inspection, limited follow up	limited inspection, limited follow up	increase mining sites inspection and active monitoring
Date	--	03-Nov-2020	30-Apr-2021	--
□ PBC 7.1 PBR 7.1 At least 70 mining license holders have been subject to annual inspection using the Extractive Sites Inspection Manual in CY22, CY23, CY24 (Number, Intermediate Outcome, 3,000,000.00, 0.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	210.00
Date	--	03-Nov-2020	30-Apr-2021	--
□ PBC 7.2 Increased impact of mining sites' inspection (Number, Intermediate Outcome, 2,000,000.00, 2%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	0.00	0.00	0.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

► PBC 8 Increased formalization of artisanal and small scale mining sites (Number, Intermediate Outcome, 5,000,000.00, 5.00%)				
	Baseline	Actual (Previous)	Actual (Current)	December 2024
Value	168.00	168.00	168.00	--
Date	--	03-Nov-2020	30-Apr-2021	--

Data on Financial Performance

Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P164271	IDA-67480	Effective	USD	50.00	50.00	0.00	0.00	54.32	0%
P164271	IDA-D6970	Effective	USD	50.00	50.00	0.00	1.85	50.75	3.5%



Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P164271	IDA-67480	Effective	03-Aug-2020	14-Aug-2020	31-Mar-2021	31-Jul-2025	31-Jul-2025
P164271	IDA-D6970	Effective	03-Aug-2020	14-Aug-2020	31-Mar-2021	31-Jul-2025	31-Jul-2025

Cumulative Disbursements

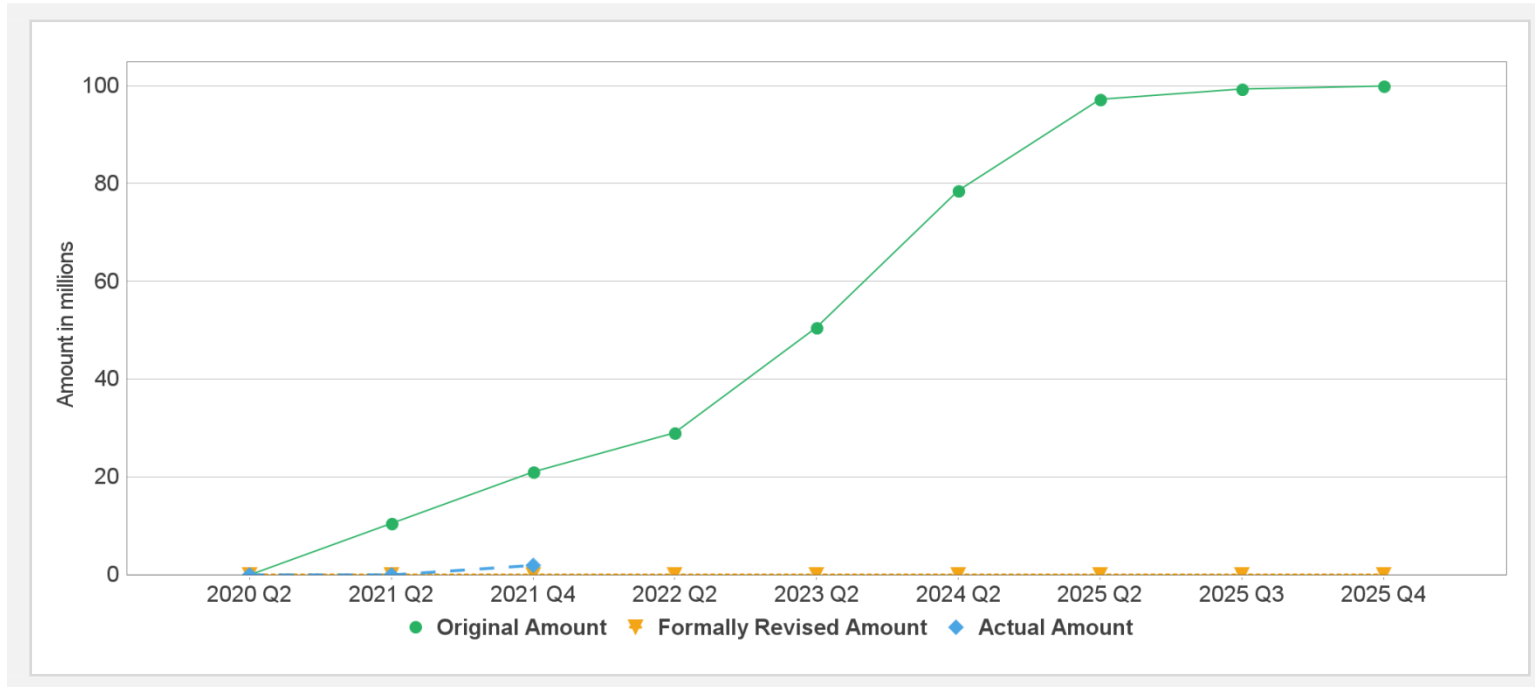

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
