



Tejaswini: Socioeconomic Empowerment of Adolescent Girls & Young Women (P150576)

SOUTH ASIA | India | Social Protection & Jobs Global Practice |
IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 9 | ARCHIVED on 23-Sep-2021 | ISR47743 |

Implementing Agencies: Republic of India, Department of Women and Child Development and Social Security

Key Dates**Key Project Dates**

Bank Approval Date: 21-Jun-2016

Effectiveness Date: 17-Apr-2017

Planned Mid Term Review Date: 28-Feb-2020

Actual Mid-Term Review Date: 17-Jun-2020

Original Closing Date: 31-Aug-2021

Revised Closing Date: 31-Aug-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To improve completion of market-driven skills training and secondary education for adolescent girls and young women in select districts of Jharkhand.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Expanding social, educational, and economic opportunities:(Cost \$50.00 M)

Intensive service delivery:(Cost \$16.00 M)

State capacity building and implementation support:(Cost \$7.10 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Unsatisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Unsatisfactory
Overall Risk Rating	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

The Jharkhand Tejaswini: Socioeconomic Empowerment of Adolescent Girls and Young Women Project was approved by the World Bank Board of Executive Directors on June 21, 2016 and became effective on April 17, 2017. The first year of the project was planned as a preparatory phase, as a result none of the PDO indicators had first year targets. The project faced significant delays in the first couple of years and thereby failed to achieve physical and financial targets for the first three years. In later part of the fourth year the Project implementation started to significantly pick up with the saturation of the community services component in all Project Districts. However, the implementation of project activities pertaining to institutional services (skills training & education) continues to be a major concern for two reasons – first COVID – 19 related restrictions on field implementation of skills training and education services, and second lack of readiness of the Project towards launching the training and education services immediately upon State Government lifting the COVID – 19 related restrictions.



Given the time lost due to COVID - 19 related restrictions, both Department of Economic Affairs and World Bank Management agreed to a one-year extension to the closing date of the Project, from August 31, 2021 to August 31, 2022. The Bank Task Team in consultation with the Jharkhand Women Development Society (JWDS) at the Department of Women, Child Development & Social Security (DWCDSS) has developed a detailed plan of action for expediting project implementation. The Bank Task Team has been and will continue to provide all necessary technical and hand-holding support to the JWDS in expediting project implementation and sustaining the momentum gained using the plan of action towards achieving the project development objectives.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	☐ Moderate	☐ Moderate	☐ Moderate
Macroeconomic	☐ Moderate	☐ Moderate	☐ Moderate
Sector Strategies and Policies	☐ Moderate	☐ Moderate	☐ Moderate
Technical Design of Project or Program	☐ Substantial	☐ Moderate	☐ Moderate
Institutional Capacity for Implementation and Sustainability	☐ Substantial	☐ Moderate	☐ Moderate
Fiduciary	☐ Substantial	☐ Substantial	☐ Substantial
Environment and Social	☐ Low	☐ Low	☐ Low
Stakeholders	☐ Moderate	☐ Moderate	☐ Moderate
Other	--	--	--
Overall	☐ Substantial	☐ Moderate	☐ Moderate

Results

PDO Indicators by Objectives / Outcomes

Project Development Objective Indicators				
▶ Number of project beneficiaries (ages 16-24) who complete market-driven skills training (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	130,000.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
▶ Number of project beneficiaries (ages 14-20) who receive a secondary education certificate through bridge education or NFE (Number, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	23,000.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
► Share of project beneficiaries having completed market-driven skills training who are in employment or continued education after completion of training course (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	30-Apr-2021	30-Apr-2021	30-Jun-2021	31-Aug-2022
► Share of project beneficiaries having completed education who are either in training, employment or continued education after completion of education track (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
Date	30-Apr-2021	30-Apr-2021	30-Jun-2021	31-Aug-2022
► Share of project beneficiaries who complete life skills education (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	66.00	68.50	90.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022

Intermediate Results Indicators by Components

Expanding social, educational, and economic opportunities, and Intensive service delivery				
► Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1,091,536.00	1,092,585.00	1,000,000.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
□ Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00



▶ Number of operational clubs for adolescent girls and young women in select districts (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12,839.00	12,839.00	11,000.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
▶ Share of vulnerable and marginalized people (SC, ST) of the total project beneficiaries (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	40.82	43.74	38.00
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
▶ Share of project beneficiaries that feel the project is responsive to their needs (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	99.60	99.60	80.00
Date	30-Jun-2015	17-Jun-2020	30-Jun-2021	31-Aug-2022

State capacity building and implementation support				
▶ State strategy and plan for convergent action on the empowerment of adolescent girls and young women developed and adopted (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
▶ Project MIS established and producing periodic reports. (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	30-Jun-2015	30-Apr-2021	30-Jun-2021	31-Aug-2022
Comments:	MIS deployed, beneficiary data entry underway.			

Performance-Based Conditions

Data on Financial Performance




Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P150576	IDA-58680	Effective	USD	63.00	50.00	13.00	14.00	36.00	28%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P150576	IDA-58680	Effective	21-Jun-2016	23-Feb-2017	17-Apr-2017	31-Aug-2021	31-Aug-2022

Cumulative Disbursements

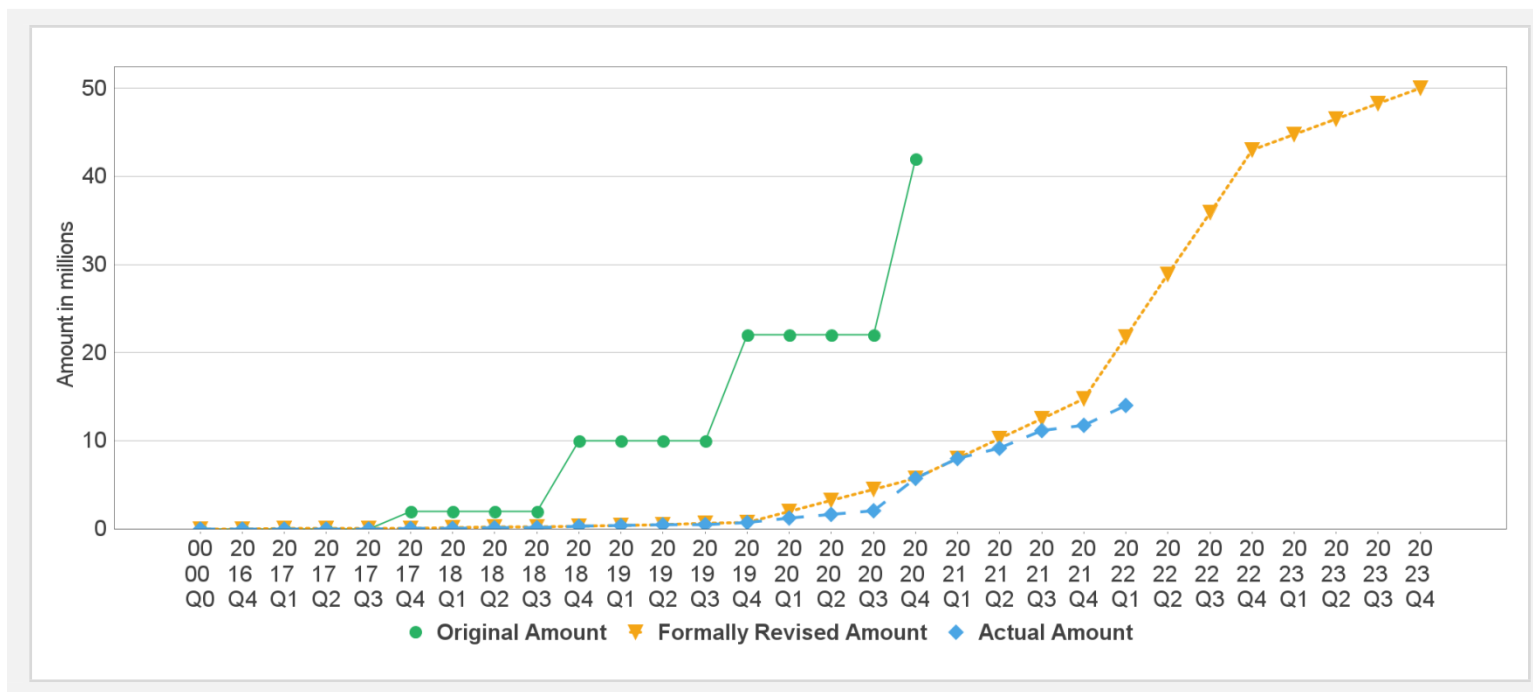

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

Level 2 Approved on 16-Oct-2020 ,Level 2 Approved on 14-Jun-2021

Related Project(s)



There are no related projects.
