



Cambodia Higher Education Improvement Project (P162971)

EAST ASIA AND PACIFIC | Cambodia | Education Global Practice |
IBRD/IDA | Investment Project Financing | FY 2018 | Seq No: 1 | ARCHIVED on 27-Aug-2018 | ISR33454 |

Implementing Agencies: KINGDOM OF CAMBODIA, Ministry of Education, Youth and Sport

Key Dates

Key Project Dates

Bank Approval Date: 26-Apr-2018

Effectiveness Date: --

Planned Mid Term Review Date: 12-Oct-2020

Actual Mid-Term Review Date: --

Original Closing Date: 30-Jun-2024

Revised Closing Date: 30-Jun-2024

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The PDO of HEIP is to improve the quality and relevance of higher education and research mainly in STEM and agriculture at targeted higher education institutions, and to improve governance in the sector.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Improving Teaching and Learning Capacity:(Cost \$63.70 M)

Component 2: Improving Research in STEM and Agriculture:(Cost \$15.80 M)

Component 3: Strengthen Sectoral Governance and Project Management:(Cost \$13.00 M)

Component 4: Contingent Emergency Response

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Moderate

Implementation Status and Key Decisions

Though project is not yet effective, Ministry of Education, Youth and Sport (MoEYS) has developed annual implementation plans and appointed focal officials in charge of component activities. Various operations manuals are ready to guide the implementing agencies.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	--	● Substantial
Macroeconomic	● Moderate	--	● Moderate
Sector Strategies and Policies	● Moderate	--	● Moderate
Technical Design of Project or Program	● Moderate	--	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	--	● Substantial
Fiduciary	● Substantial	--	● Substantial
Environment and Social	● Low	--	● Low
Stakeholders	● Moderate	--	● Moderate
Other	--	--	--
Overall	● Moderate	--	● Moderate

Results

PDO Indicators by Objectives / Outcomes

Improve the quality and relevance of higher education and research at targeted HEIs				
▶ Students benefiting from direct interventions to enhance learning (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	16,356.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▲ Students benefiting from direct interventions to enhance learning - Female (Number, Corporate Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5,070.00
▶ Number of HE partnership programs evaluated as modest or higher by expert panels (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	the revised curriculum and other improved outputs under the HE Partnership Program will be evaluated by multi-dimensional evaluation panel (led by Cambodian chair and includes international experts). The evaluation process will be based on a four-tier scoring.			



▶Number of research projects in collaboratin with industry completed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	35.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	Collaboration includes (i) documented connection between the development of a research project with industry; (ii) membership of industry employees on research teams; or (iii) industrial funding for additional research activities.			
▲Number of research projects in collaboratin with industry completed, led by female faculty (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024

Improve governance in the higher education sector				
▶Number of HEIs that complete accreditation process (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024

Overall Comments

As the project is not yet effective, there has been no information to report on PDO indicators yet.

Intermediate Results Indicators by Components

Component 1: Improving Teaching and Learning Capacity				
▶Signed agreements for higher education partnership programs (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	17.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▶Faculty members who receive advanced degree (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00



Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▲Number of female faculty members who receive advanced degree (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▶Number of classroom built (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▶number of laboratories constructed or rehabilitated (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	55.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▶Number of dormitories built (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
▲Share of female students living in newly constructed dormitories under the project (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
▶Number of HEIs that produce consolidated FM reports (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	Consolidated FM reports based on HEIP FM guidelines for HEIs.			
▶Number of target HEIs that complete tracer studies (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00



Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	HEIs that complete annual tracer studies are counted one.			
►Number of HEIs that collect, record and report on the grievances from students (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024

Component 2: Improving Research in STEM and Agriculture				
►Number of submitted articles to peer-reviewed international journals (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	24.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	Journal submission document means the PDF version of the submitted article through an online system or an email from the journal's editor with submitted article.			

Component 3: Strengthen Sectoral Governance and Project Management				
►Draft legislation on HEI autonomy submitted to Council of Ministers (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
►Human resource development master plan approved (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
►Number of HEIs that input data into HEMIS (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	5.00	5.00	5.00	40.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	HEIs must input data through the system.			



► Number of IQA units that submit report with recommendatins to BoD (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20.00
Date	01-Jul-2018	08-Aug-2018	08-Aug-2018	30-Jun-2024
Comments:	HEIs that submit are counted once. The report must follow the MoEYS IQA guidelines.			

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P162971	IDA-62210	Not Effective	USD	90.00	90.00	0.00	0.00	86.51	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P162971	IDA-62210	Not Effective	26-Apr-2018	12-Jul-2018	--	30-Jun-2024	30-Jun-2024

Cumulative Disbursements

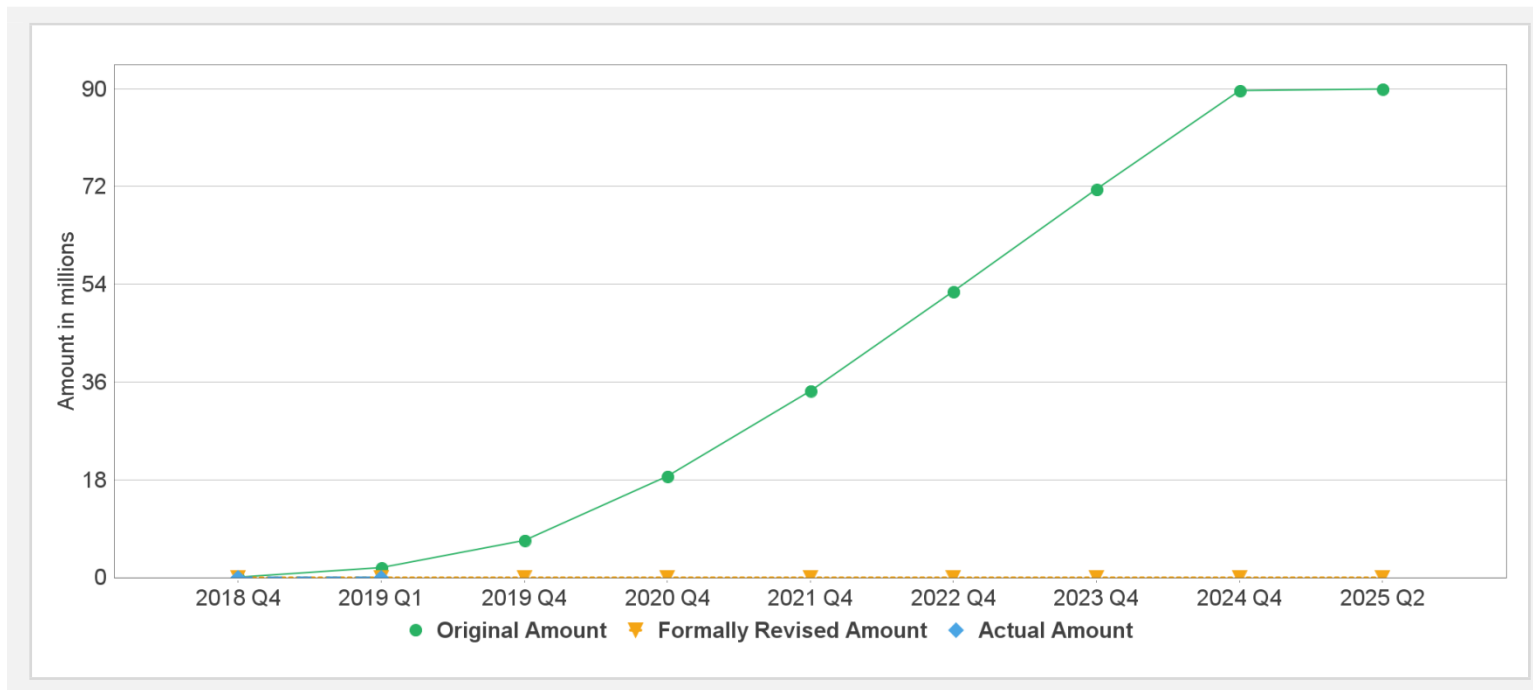



Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
