



## West Africa Food System Resilience Program (FSRP) Phase 2 (P178132)

WESTERN AND CENTRAL AFRICA | Western and Central Africa | Agriculture and Food Global Practice | IBRD/IDA | Investment Project Financing | FY 2023 | Seq No: 3 | ARCHIVED on 24-Jul-2023 | ISR56791 |

Implementing Agencies: Ministry of Agricultural Development - Chad, Ministry of Agriculture and Forestry - Sierra Leone, Ministry of Food and Agriculture - Ghana, Republic of Chad, Republic of Ghana, Republic of Sierra Leone

**Key Dates****Key Project Dates**

Bank Approval Date: 29-Jul-2022

Effectiveness Date: 04-Nov-2022

Planned Mid Term Review Date: 28-May-2025

Actual Mid-Term Review Date:

Original Closing Date: 30-Sep-2028

Revised Closing Date: 30-Sep-2028

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

To increase preparedness against food insecurity and improve the resilience of food systems in participating countries.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

**Components Table**

Name
Digital Advisory Services for Agriculture and Food Crisis Prevention and Management:(Cost \$45.20 M)
Sustainability and Adaptive Capacity of the Food System's Productive Base:(Cost \$200.41 M)
Regional Food Market Integration and Trade:(Cost \$66.69 M)
Contingent Emergency Response (CERC):(Cost \$25.00 M)
Project Management:(Cost \$27.70 M)

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

**Implementation Status and Key Decisions**

**Sierra Leone:** The Financing Agreement was signed on August 22, 2022, and the project became effective on November 4. On November 11, the Contingency Emergency Response Component (CERC) was activated to support cash transfers, school feeding programs and critical agriculture inputs. In order to replenish the resources allocated to the CERC and scale-up critical food security interventions, a US\$50M Additional Financing was approved for Sierra Leone on December 15, 2022 and became effective on March 17, 2023. As part of the CERC, the project is currently providing school feeding for 114,823 children in 588 pre-primary and primary schools in three crisis-affected districts to enhance nutritional levels of the children from at-risk households, as well as vulnerable children (e.g., learners with disabilities). The project has also started providing unconditional cash transfers to a target of between 15,000-20,000 people and providing cash-for-work for the rehabilitation of 8,500 hectares of inland valley swamps.



**Chad:** The Financing Agreement was signed on October 16, 2022 and the project became effective on February 13, 2023. The team has finalized the Annual Work Plan and Budget. Next steps are to set up a Grievance Mechanism, put in place key project staff, update safeguards documents, update the accounting system, and launch project activities.

**Ghana:** The project received parliamentary approval on May 2, 2023, and the Financing Agreement was signed on 26 May 2023. The project became effective on May 30 2023. Activities are ramping up rapidly.

The next Implementation Support Mission will take place from October 23-27, 2023, in Niamey, Niger and will be hosted by CILSS. The following wrap up mission will take place from April 22 – 26, 2024 and will be hosted by Sierra Leone.

### MPA Program Development Objective

To increase preparedness against food insecurity and improve the resilience of food systems in participating countries.

### Multiphase Programmatic Approach (MPA) Status

**Phase 1 (Togo, Mali, Burkina Faso):** In January, 2023 a restructuring of Phase 1 of the MPA was undertaken to allow for the procurement of agricultural inputs for increased food production against a backdrop of increasing levels of food insecurity in the region. Following that, Togo undertook a large-scale procurement and distribution of fertilizers through an e-voucher scheme. Mali and Burkina Faso are working towards procurement of seeds and other inputs for the upcoming cropping season. All the three countries are undertaking feasibility studies to validate identified investments in value-chain infrastructure. All countries and regional organizations are progressing on activities and making progress towards its objectives.

**Phase 2 (Chad, Sierra Leone, Ghana):** Phase 2 was declared effective on November 4, 2022 and overall, the project has made progress in rolling out startup activities. For Sierra Leone the Contingency Emergency Response Component (CERC) was activated on November 11 in response to a widespread food insecurity crisis, and Additional Financing for US\$50M was approved on December 15, 2022 and became effective on March 17, 2023. Following the effectiveness, FSRP-SL has initiated start-up activities across all its components with greater emphasis on the emergency interventions under the CERC. Chad is accelerating compliance with dated covenants as well as other activities at the start of the project in order to ensure a rapid take-off of the implementation activities. For Ghana, the project received parliamentary approval on May 2, 2023, and the Financing Agreement was signed on May 26, 2023. The project was declared effective on May 30 2023 and is rapidly ramping up activities.

**Phase 3:** A third phase of the FSRP is being prepared and is expected to be approved by the World Bank Board of Directors in November, 2023.

**Progress on Learning Agenda:** Learning is an integral part of FSRP. The FSRP Phase1 developed a Learning Agenda with five mechanisms to generate and disseminate knowledge and learning. The program has created public policy notes on: i) regional risk management architecture, ii) the conflict-climate nexus, iii) mechanisms for the delivery of digital climate information, and iv), a scorecard methodology allowing to monitor countries' performance in implementing regional trade regulations to facilitate the region's intraregional food trade. It has also developed a guide for a rigorous impact evaluation methodology to measure changes in food insecurity in areas targeted by FSRP, and to assess the impact of program's interventions on key food security and other development indicators in the region. It is currently working with the World Bank's Development Impact Evaluation group to operationalize the IE in countries. The impact evaluation will help learning to be further promoted throughout the lifetime of the MPA.



## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	☐ Substantial	☐ Substantial	☐ Substantial
Macroeconomic	☐ Substantial	☐ Substantial	☐ Substantial
Sector Strategies and Policies	☐ Moderate	☐ Moderate	☐ Moderate
Technical Design of Project or Program	☐ Moderate	☐ Moderate	☐ Moderate
Institutional Capacity for Implementation and Sustainability	☐ Substantial	☐ Substantial	☐ Substantial
Fiduciary	☐ Substantial	☐ Substantial	☐ Substantial
Environment and Social	☐ Substantial	☐ Substantial	☐ Substantial
Stakeholders	☐ Substantial	☐ Substantial	☐ Substantial
Other	☐ High	☐ High	☐ High
Overall	☐ Substantial	☐ Substantial	☐ Substantial

## Results

### PDO Indicators by Objectives / Outcomes

Increase Preparedness Against Food Insecurity				
▶ Intra-regionally traded production in selected value chains (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.00	0.00	0.00	30.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Share of intra-regionally traded production in selected value chains			
▶ Reduction of food insecure people in program targeted areas (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator measures the reduction of food insecure people in the targeted areas. The food insecure people are those in phase 3 and 5 based on the Integrated Food Insecurity Phase Classification (IPC).			



<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► Program beneficiaries (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	114,823.00	2,045,200.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator will measure the number of beneficiaries in project target areas which are provided with agricultural assets or services as a result of project activities. Agriculture assets or services in the context of this indicator refer to infrastructure, goods and services that are provided as a result of project activities. Services include, for example, early earning advice, agriculture advices or trainings. The values of this indicator will be measures as total and also broken down by gender and country.			
<input type="checkbox"/> Of which women (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	51.00	40.00
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1,080,000.00
Date	29-Sep-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	600,000.00
Date	29-Sep-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	114,823.00	881,900.00
Date	29-Sep-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► People receiving emergency support from the project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	114,823.00	516,700.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	08-Nov-2024

<b>Improve Resilience of Food Systems in Participating countries</b>				
<b>► Food system actors accessing hydro and agrometeorological advisory services (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	406,200.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator measures the number of Food system actors who are benefiting from the FSRP support for accessing hydro and agrometeorological advisory services			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	211,200.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	75,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	200,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Of which women (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00
<b>► Land area under sustainable landscape management practices (Hectare(Ha), Corporate)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	11,850.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	The indicator measures, in hectares, the land area for which new and/or improved sustainable landscape management practices have been introduced. Land is the terrestrial biologically productive system comprising soil, vegetation, and the associated ecological and hydrological processes; Adoption refers to change of practice or change in the use of a technology promoted or introduced by the project; Sustainable landscape management (SLM) practices refers to a combination of at least two technologies and approaches to increase land quality and restore degraded lands for example, agronomic, vegetative, structural, and management measures that, applied as a combination, increase the connectivity between protected areas, forest land, rangeland, and agriculture land.			
<input type="checkbox"/> Ghana (Hectare(Ha), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,850.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	28-Sep-2028
<input type="checkbox"/> Chad (Hectare(Ha), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	28-Sep-2028
<input type="checkbox"/> Sierra Leone (Hectare(Ha), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	28-Sep-2028
<b>► Producers adopting climate-smart agricultural technologies and services (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	480,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator measures the total number of the Program beneficiaries who have adopted technologies/practices that can lead to improve resilience to climate variability, increase productivity and/or mitigation and also for advisory services under the Project support			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	240,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	260,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Of which are women (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	40.00

**Intermediate Results Indicators by Components**

Digital Advisory Services for agriculture and food crisis prevention and management				
▶ Satisfaction of farmers have access to usable weather, climate and ag-advisory services (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Percentage of beneficiaries who express satisfaction with the weather, climate and ag-advisory services provided in the project areas based on formal surveys. It is expected that a survey to measure this indicator will be carried out twice throughout the project. The sample size should be representative of the total number of beneficiaries.			



<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► Improved access to local climate information services with digital information platforms (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator informs on the on the delivery of climate information services to the Project's beneficiaries through digital information platforms provided by the Project.			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target





Value	No	No	No	Yes
Date	29-Sep-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► Agreements involving co-production of agro-hydro-meteorological services between the public and private sectors (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Number of agreements and contracts involving co-production of agro-hydro-meteorological services between the public and private sectors			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

**Sustainability and Adaptive Capacity of the Food System's Productive Base**

**► Technologies made available to farmers by the consortium of NCoS, CGIAR and other international research institutes (Number, Custom)**

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	74.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Number of technologies developed by the consortium of NCoS, CGIAR and other international research institutes and made available to farmers by the extension system			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	15.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Percentage of nutrition sensitive technologies (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
<b>► Sub-projects selected from the integrated landscape management plans with climate-resilient measures implemented (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Share of sub-projects selected from the integrated landscape management plans with climate-resilient measures implemented out of the total sub-projects			
<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028



<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► Spatial information system established and operational for designing and planning climate-resilient land management practices (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	Existence of an operational spatial information system for designing and planning climate-resilient land management practices			
<input type="checkbox"/> Ghana (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

<b>Regional Food Market Integration and Trade</b>				
<b>► Private-sector actors involved in regional agriculture trade that are supported by the Project (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	300.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator measures the number of private-sector led initiatives involved in regional agriculture products, inputs and output trade that are supported by the Program.			



<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	180.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<b>► Women farmers reached with assets or services to improve commercialization in selected value chains (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	102,300.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
Comments:	This indicator measures the number of farmers reached with assets or services to improve the commercialization of agricultural products as a result of project activities. It is to note that while the word "farmer" includes for the purposes of this indicator livestock, herders and fishermen and primary agro-processors.			
<input type="checkbox"/> Ghana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100,000.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

### Project Management

#### ► Beneficiaries satisfied with the Project's interventions (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

Comments: Percentage of beneficiaries who express satisfaction with the services provided in the project areas based on formal surveys. It is expected that a survey to measure this indicator will be carried out twice throughout the project. The sample size should be representative of the total number of beneficiaries.

#### Ghana (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

#### Chad (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

#### Sierra Leone (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

#### ► Grievances registered and addressed by the Program (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	90.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028

Comments: This indicator measures the percentage of grievances relayed through the GM system that are adequately addressed.



<input type="checkbox"/> Ghana (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	90.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Chad (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	90.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Sierra Leone (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	90.00
Date	31-Aug-2022	17-Oct-2022	30-Jun-2023	30-Jun-2023

Contingency Emergency Response Component (CERC), Sierra Leone				
▶ People benefiting from unconditional cash transfer (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> People benefiting from unconditional cash transfer - Female (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> People benefiting from unconditional cash transfer - individuals with disabilities (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	15,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
▶ People benefiting from food/cash for public works program (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	8,700.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	31-Jul-2024
<input type="checkbox"/> People benefiting from food/cash for public works program - Female (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	4,000.00
Date	01-Nov-2022	01-Nov-2022	01-Nov-2022	29-Sep-2028
<b>► School pupils receiving project-supported meals (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	113,907.00	114,823.00	120,000.00
Date	01-Nov-2022	17-Feb-2023	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> School pupils receiving project-supported meals - Female (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	50,000.00	59,479.00	60,000.00
Date	01-Nov-2022	17-Feb-2023	30-Jun-2023	29-Sep-2028
<b>► Farmers reached with agricultural assets or services (Number, Corporate)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	258,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
<input type="checkbox"/> Farmers reached with agricultural assets or services - Female (Number, Corporate Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100,000.00
<input type="checkbox"/> Number of producers supported in crop and livestock production (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10,500.00
<b>► Quantity of inputs distributed to beneficiary farmers (Metric ton, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	7,500.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
☐ Rice seed (Metric ton, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
☐ Fertilizer (Metric ton, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
☐ Vegetable and legume seed (Metric ton, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	500.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
▶ Households using better cropping and farm management practices (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30,000.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028
▶ Beneficiary households with increased minimum dietary diversity scores (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	70.00
Date	01-Nov-2022	01-Nov-2022	30-Jun-2023	29-Sep-2028

**Performance-Based Conditions**

**Data on Financial Performance**

**Disbursements (by loan)**






Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P178132	IDA-71950	Effective	USD	150.00	150.00	0.00	0.00	150.00	0%
P178132	IDA-E1150	Effective	USD	105.00	105.00	0.00	2.89	100.84	2.8%
P178132	IDA-E1160	Effective	USD	60.00	60.00	0.00	17.22	41.99	29%
P178132	IDA-E1430	Effective	USD	50.00	50.00	0.00	0.00	52.25	0%

**Key Dates (by loan)**

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P178132	IDA-71950	Effective	29-Jul-2022	22-May-2023	05-Jun-2023	30-Sep-2028	30-Sep-2028
P178132	IDA-E1150	Effective	29-Jul-2022	16-Oct-2022	13-Feb-2023	30-Sep-2028	30-Sep-2028
P178132	IDA-E1160	Effective	29-Jul-2022	22-Aug-2022	04-Nov-2022	30-Sep-2028	30-Sep-2028
P178132	IDA-E1430	Effective	15-Dec-2022	19-Dec-2022	17-Mar-2023	30-Sep-2028	30-Sep-2028

**Cumulative Disbursements**

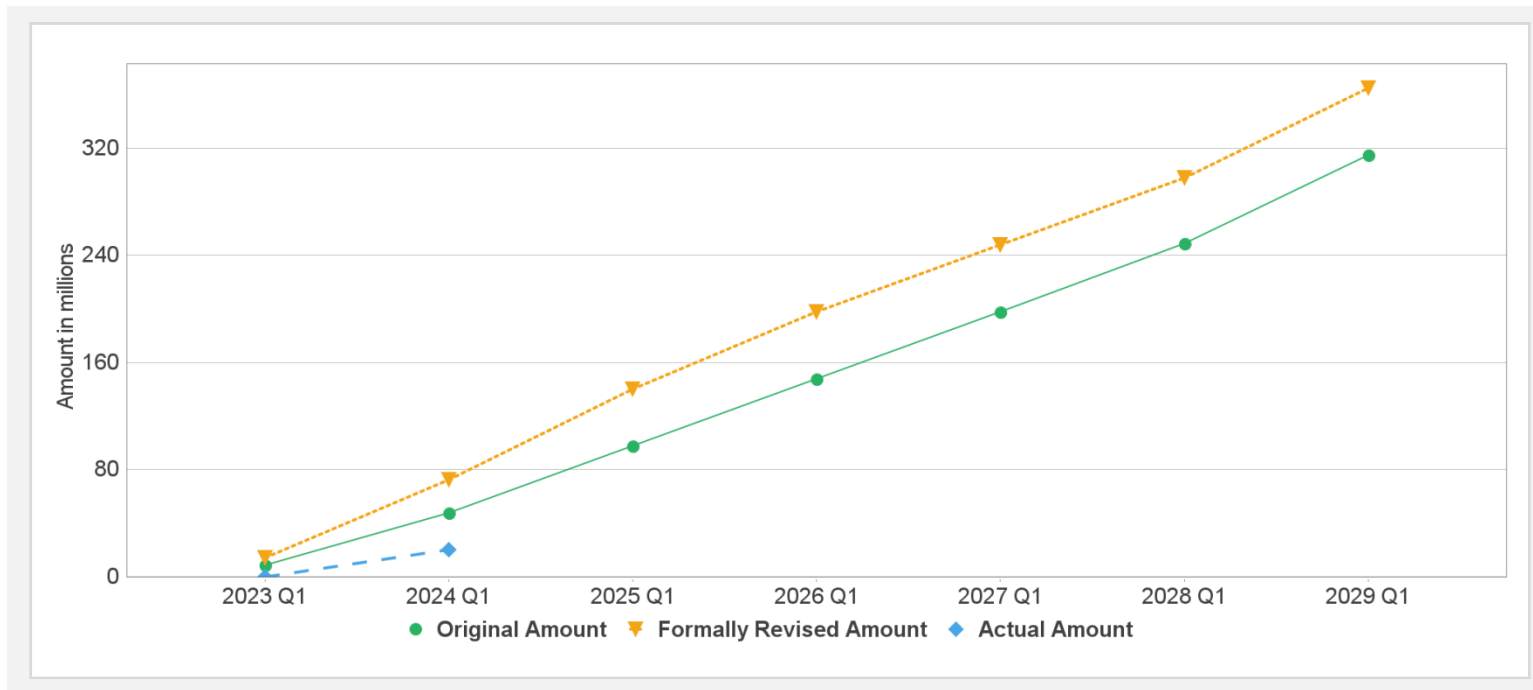



---

### Restructuring History

There has been no restructuring to date.

### Related Project(s)

P180211-Additional Financing to Sierra Leone Food Systems Resilience Program, Phase 2 ,P181054-GAFSP for Sierra Leone FSRP ,P181088-Additional Financing to the Food System Resilience Program, Phase 2 Sierra Leone

---
