



Agricultural Productivity Program for Southern Africa - Angola & Lesotho (P164486)

Eastern and Southern Africa | Eastern and Southern Africa | Agriculture and Food Global Practice | IBRD/IDA | Investment Project Financing | FY 2019 | Seq No: 8 | ARCHIVED on 17-Jun-2022 | ISR51894 |

Implementing Agencies: Angola Ministry of Agriculture, Angola Ministry of Finance, CCARDESA, Lesotho Ministry of Finance, Lesotho Ministry of Agriculture and Food Security

Key Dates**Key Project Dates**

Bank Approval Date: 18-Dec-2018

Effectiveness Date: 30-Apr-2019

Planned Mid Term Review Date: 31-Oct-2022

Actual Mid-Term Review Date:

Original Closing Date: 31-Jan-2025

Revised Closing Date: 31-Jan-2025

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To increase the availability of improved agricultural technologies in participating countries in the Southern Africa Development Community (SADC) region.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Technology Generation and Dissemination:(Cost \$16.66 M)

Strengthening the Institutional and Enabling Environment for Technology Adoption:(Cost \$17.75 M)

Contingency Emergency Response Component

Project management, monitoring and evaluation, and regional coordination:(Cost \$15.59 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

This is an interim Implementation Status and Results Report and will be updated after completion of the mission currently underway.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Macroeconomic	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Sector Strategies and Policies	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Technical Design of Project or Program	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Institutional Capacity for Implementation and Sustainability	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Fiduciary	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial
Environment and Social	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Stakeholders	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate
Other	--	--	--
Overall	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate	<input type="checkbox"/> Moderate

Results

PDO Indicators by Objectives / Outcomes

Technology generation and dissemination				
▶ Number of technologies that are being made available to farmers and other end users (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.00	8.00	50.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
▶ Number of technologies that are being made available to farmers and other end users (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13.00	13.00	100.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
□ Number of nutrition-sensitive technologies made available to farmers and other end users (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20.00



<input type="checkbox"/> Number of improved seed varieties (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13.00	13.00	30.00
<input type="checkbox"/> Number of improved agronomic, pest and disease management and water management practices (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	20.00
<input type="checkbox"/> Number of improved post-harvest storage, labor saving and processing technologies (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00

Lead Farmers aware and adopt new technologies				
▶ Percentage of Lead Farmers in targeted areas who are aware of an improved technology promoted by the Project (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	28-Mar-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
Comments:	No field activities could be conducted due to COVID-19 related travel restrictions in all countries.			
▶ Percentage of Lead Farmers in targeted areas who are aware and adopt an improved technology promoted by the Project (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
Comments:	No field activities could be conducted due to COVID-19 related travel restrictions in all countries.			
<input type="checkbox"/> Percentage of female Lead Farmers in targeted areas who are aware and adopt improved technologies (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
<input type="checkbox"/> Percentage of Lead Farmers aware of nutrition-sensitive technologies promoted by the project (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	0.00	0.00	50.00
-------	------	------	------	-------

Technologies available across participating countries

► Number of technologies generated or promoted by the Project in one participating country that are released in another participating country (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13.00	13.00	30.00
Date	28-Mar-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025

► Number of technologies generated or promoted by the Project in one participating country that are released in another participating country (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13.00	13.00	25.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025

☐ Number of nutrition-sensitive technologies generated in one country and released in another country (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00

☐ Number of improved seed varieties (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00

☐ Number of improved agronomic, pest and disease, and water management practices (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00

☐ Number of improved post-harvest storage, labor saving and processing technologies (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00

Project beneficiaries

► Direct Project beneficiaries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
--	----------	-------------------	------------------	------------



Value	0.00	0.00	0.00	50,000.00
Date	28-Mar-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
Comments:	No field activities could be conducted due to COVID-19 related travel restrictions in all countries.			
<input type="checkbox"/> of which female (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00
► Beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50,000.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
Comments:	No field activities could be conducted due to COVID-19 related travel restrictions in all countries.			
<input type="checkbox"/> of which female (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10,000.00
► Farmers reached with agricultural assets or services (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50,000.00
Date	20-Jun-2018	18-Jun-2021	18-Jun-2021	31-Jan-2025
Comments:	No field activities could be conducted due to COVID-19 related travel restrictions in all countries.			
<input type="checkbox"/> Farmers reached with agricultural assets or services - Female (Number, Corporate Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00

Intermediate Results Indicators by Components

Technology Generation and Dissemination

► Number of collaborative research and development sub-projects under implementation (Number, Custom)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.00	8.00	50.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Technology generation (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	6.00	6.00	25.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Technology dissemination (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	25.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
► Number of improved technologies formally recommended by the national research centers and subsequently promoted by the extension and advisory services (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	25.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Number of improved varieties (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
<input type="checkbox"/> Improved agronomic, pest and disease, and water management practices (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
<input type="checkbox"/> Improved post-harvest storage, labor saving and processing technologies (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
► Number of technologies generated (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00



Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Percent of beneficiaries (gender disaggregated) reporting satisfaction with technologies generated under APPSA (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Number of improved varieties newly released (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Number of improved agronomic, pest and disease, and water management practices developed and formally recommended to the national extension and advisory services (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Number of improved post-harvest storage, labor saving and processing technologies developed and formally recommended to the national extension and advisory services (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	10.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
► Percentage of collaborative R&D Projects completed (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
Comments:	8 collaborative R&D subprojects are under implementation.			
<input type="checkbox"/> Technology generation (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	100.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025



<input type="checkbox"/> Technology dissemination (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025

Strengthening the Institutional and Enabling Environment for Technology Adoption

► Actions taken to encourage women scientists' increased access or participation to either employment in ag research or scholarships (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	None	Not yet due	Not yet due	List of actions taken to promote/encourage women's participation
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025

► Number of clients (RCoL staff) days of training (disaggregated by gender and type of training) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2,000.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025

Comments: No field activities could be conducted due to COVID-19 related travel restrictions in all countries.

Number of funded scholarship holder that have successfully completed long term training (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	15.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025

Of which female (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025

► Number of research centers rehabilitated or equipped (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	3.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025



Project management, monitoring and evaluation, and regional coordination				
▶ Regionally harmonized quality assurance of science (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Lack of harmonized R&D	Not yet due	Not yet due	Regionally harmonized R&D between 2 or more countries
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
Comments:	Terms of reference developed to launch country policies alignment with SADC regional policies			
▶ Participating country alignment with the SADC Regional Policies (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	2.00
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
Comments:	Process initiated for country realignment of policies with SADC regional policies.			
▶ Common M&E system being used by APPSA participating institutions (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	20-Jun-2018	30-Nov-2021	30-Nov-2021	31-Jan-2025
<input type="checkbox"/> Undertake citizen engagement mechanisms e.g. interactive voice response (IVR), online feedback platforms etc. (Yes/No, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes

Performance-Based Conditions

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P164486	IBRD-89170	Effective	USD	25.00	25.00	0.00	5.14	19.86	21%




P164486	IDA-63580	Effective	USD	20.00	20.00	0.00	4.29	15.32	<div style="width: 22%; background-color: green;"></div>	22%
P164486	IDA-D4150	Effective	USD	5.00	5.00	0.00	2.73	2.22	<div style="width: 55%; background-color: green;"></div>	55%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P164486	IBRD-89170	Effective	18-Dec-2018	12-Apr-2019	28-Jan-2020	31-Jan-2025	31-Jan-2025
P164486	IDA-63580	Effective	18-Dec-2018	12-Apr-2019	12-Jun-2019	31-Jan-2025	31-Jan-2025
P164486	IDA-D4150	Effective	18-Dec-2018	30-Jan-2019	30-Apr-2019	31-Jan-2025	31-Jan-2025

Cumulative Disbursements

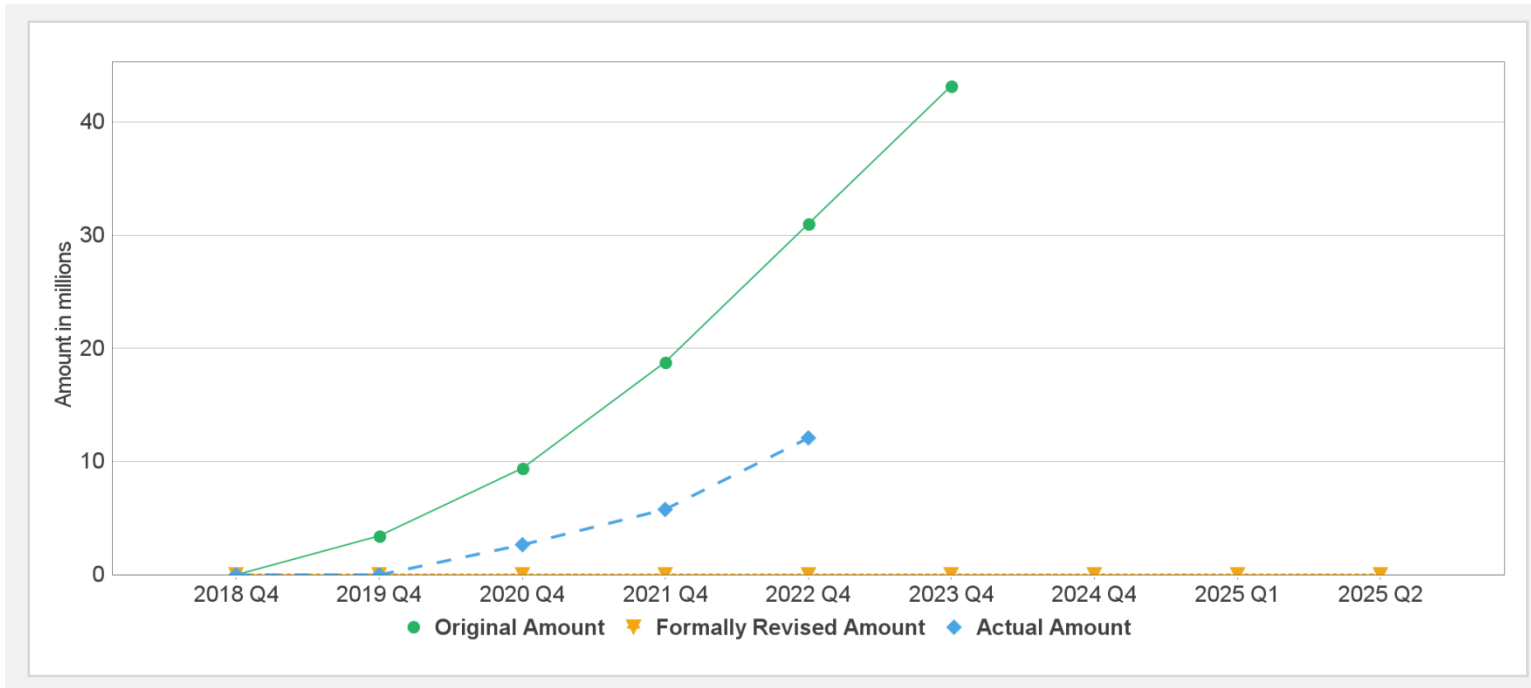

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
