



## Support to Nutrition Sensitive Agriculture and Capacity Development of Small and Marginal Farmers (P155081)

AFRICA WEST | Cote d'Ivoire | Agriculture and Food Global Practice |  
 Recipient Executed Activities | Investment Project Financing | FY 2018 | Seq No: 3 | ARCHIVED on 23-Dec-2020 | ISR45003 |

Implementing Agencies: Republic of Cote d'Ivoire, Helen Keller International, Ministry of Agriculture and Rural Development

**Key Dates****Key Project Dates**

Bank Approval Date: 18-Oct-2017

Effectiveness Date: 05-Apr-2019

Original Closing Date: 22-Feb-2022

Revised Closing Date: 22-Feb-2022

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

Improve access to nutrient-rich food of plant and animal origins by poor households in selected areas in Côte d'Ivoire.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory

**Implementation Status and Key Decisions**

Achievement of the development objectives is measured by the following indicators that focus mainly on production and consumption targets: (i) increase in consumption of at least 4 groups of nutrient rich food by 60%; (ii) increase by 30% of the number of beneficiaries who consume Orange-Fleshed Sweet Potatoes; (iii) increase by 200% of the production of nutrient rich crops at the end of the project. Data are currently being collected by the PIU to monitor progress towards the PDO. The baseline data has been collected and was used to inform the benchmark situation of the result framework.

There is indeed good indication that the activities implemented are progressing toward the PDO. Production of nutrient rich food started during the first months of the cropping season and ANADER is supporting producers to adopt Good Agricultural Practices since August 2020. At the end of December, they will complete their first training cycle. The production of chicken has been launched. Capacity improvement activities and nutrition education are also expanding. The institutional partners have been trained on the Essential Hygiene Actions and Essential Nutrition Actions. This training is expected to be deployed at the community level in December.

Progress toward development objectives and implementation progress are rated both as Moderately Satisfactory. Overall disbursement is estimated at 26.3 %. A new Fund Request of 140 878 914 F CFA has been submitted and once approved will increase the disbursement rate to 35%.

**Risks****Overall Risk Rating**



Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	☐ Moderate	☐ Moderate

## 5. Results

### Project Development Objective Indicators

#### ► Percentage of targeted 2400 beneficiaries ☐☐ HH that report improved consumption of nutrient-rich food other than OFSP (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	8.10	--	--	60.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

#### ► Percentage of targeted 2400 beneficiaries consuming OFSP (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	20.90	0.00	0.00	30.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	30-Sep-2021

#### ► Percentage of increase in volume of production of nutrient-rich foods per beneficiary woman (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	200.00
Date	28-May-2015	25-Jun-2020	04-Dec-2020	22-Feb-2022

### Intermediate Results Indicators

#### ► Number of hectares cultivated under improved irrigation techniques to produce nutrient-rich crops (directly on the VMFs and in beneficiaries' home gardens) (Hectare(Ha), Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	250.00
Date	04-Sep-2019	25-Jun-2020	04-Dec-2020	22-Feb-2022

#### ► Percentage of beneficiaries adopting improved agricultural practices for the production of nutrient-rich high-value crops and animal-source foods (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	45.40	--	--	60.00



Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022
------	-------------	-------------	-------------	-------------

► Percentage of women adopting essential nutrition, hygiene actions and water saving practices (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	8.00	--	--	60.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

► Percentage of targeted women with improved knowledge of essential nutrition, hygiene actions and water saving practices (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	45.30	--	--	60.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

► Percentage of targeted women having access to improved water availability to produce nutrient rich crops (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	42.33	0.00	0.00	60.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

► Percentage of targeted women with improved physical access to market, storage and processing facilities (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	51.00	0.00	0.00	50.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

► Number of research reports completed (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	1.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022

► Number of knowledge and experience sharing workshops organized (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	4.00
Date	30-Nov-2020	25-Jun-2020	04-Dec-2020	22-Feb-2022



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P155081	TF-A8132	Effective	USD	2.73	2.73	0.00	0.72	2.01	26%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P155081	TF-A8132	Effective	17-Oct-2018	14-Mar-2019	05-Apr-2019	22-Feb-2022	22-Feb-2022

Cumulative Disbursements

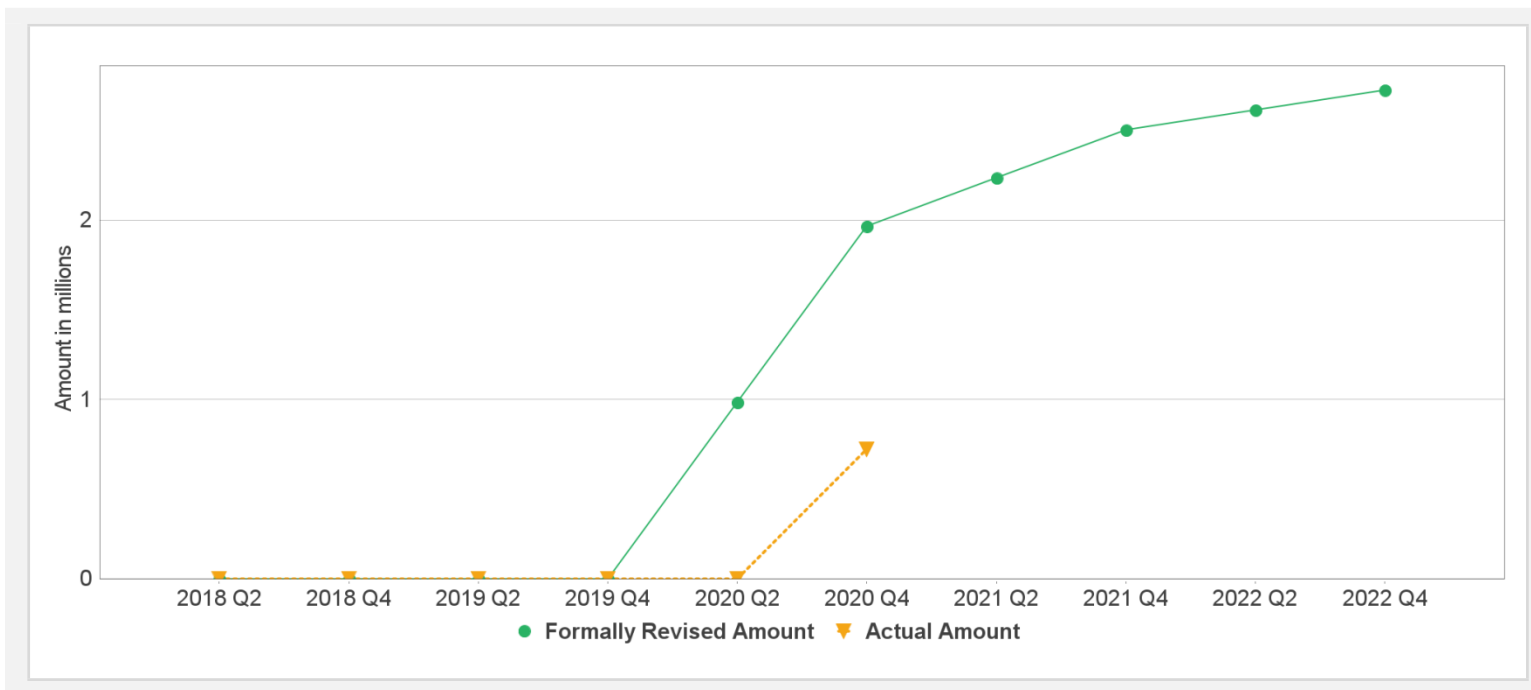

Restructuring History

Level 2 Approved on 03-Dec-2019

Related Project(s)

There are no related projects.

