



West Africa Unique Identification for Regional Integration and Inclusion (WURI) Program (P161329)

AFRICA | Western Africa | Social Protection & Labor Global Practice |
IBRD/IDA | Investment Project Financing | FY 2018 | Seq No: 1 | ARCHIVED on 07-Mar-2019 | ISR35549 |

Implementing Agencies: Office of the Prime Minister (Primature), ECOWAS Commission, Organisation National de l'Identification (ONI), Republic of Cote d'Ivoire, Republic of Guinea

Key Dates

Key Project Dates

Bank Approval Date: 05-Jun-2018

Effectiveness Date: 09-Nov-2018

Planned Mid Term Review Date: --

Actual Mid-Term Review Date: --

Original Closing Date: 03-Jul-2024

Revised Closing Date: 03-Jul-2024

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Program Development Objective (Pr.DO) is to increase the number of persons in participating countries who have government-recognized proof of unique identity that facilitates access to services. The Project Development Objective (PDO) for Phase 1 of the Project is to increase the number of persons in Côte d'Ivoire and Guinea who have government-recognized proof of unique identity that facilitates access to services.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Strengthening the legal and institutional enabling environment:(Cost \$9.60 M)

Component 2: Establishing robust and inclusive foundational ID systems:(Cost \$100.85 M)

Component 3: Facilitating access to services through IDs:(Cost \$11.65 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Moderately Satisfactory
Overall Implementation Progress (IP)	--	● Moderately Satisfactory
Overall Risk Rating	--	● High

Implementation Status and Key Decisions

Overall implementing progress is moderately satisfactory in this initialization phase. We should expect disbursement to slowly pick up, as stakeholder capacity is being progressively built up to implement this complex agenda.

Multiphase Programmatic Approach (MPA) Status



The project is effective in both countries benefiting from the credit/grants - Cote d'Ivoire and Guinea - and in the ECOWAS Commission.

Current activities are focused on (i) building the capacity of counterpart agencies to develop the technical architecture of the Foundational Identification Platform (fID); and (ii) on setting up project implementation units. The project annual work and implementation plans for 2019 are under preparation, and will detail activities to be financed and conducted in 2019. Implementation progress is rated moderately satisfactory in this initialization phase, as implementation units in Cote d'Ivoire, Guinea and ECOWAS are being set up and equipped to carry forward the work.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	--	● Substantial
Macroeconomic	● Moderate	--	● Moderate
Sector Strategies and Policies	● High	--	● High
Technical Design of Project or Program	● High	--	● High
Institutional Capacity for Implementation and Sustainability	● High	--	● High
Fiduciary	● Substantial	--	● Substantial
Environment and Social	● Substantial	--	● Substantial
Stakeholders	● High	--	● High
Other	● High	--	● High
Overall	● High	--	● High

Results

PDO Indicators by Objectives / Outcomes

Legal robustness				
► Legal Robustness: Development of foundational ID system enabling legal and institutional frameworks in keeping with regional standards and international good practices. (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Technical robustness



►Development of fID system which generates UNIs, in keeping with international practices (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Inclusion and Coverage				
►Number of direct project beneficiaries who have received a UNI (of which women) (Number (Thousand), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	35,000.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Access to Services				
►National or regional functional public and private services linked to the Foundational ID system (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Intermediate Results Indicators by Components

Robustness Data Quality				
►Percentage of individuals in fID system whose biometric and demographic data meet international stds (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	100.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Robustness Sustainability				
►Percentage of newborns assigned UNIs during birth registration. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	80.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023



Robustness Legal				
▶law for fID system created, establishing the system's inclusivity for all persons in territory, UNI, (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Stakeholder Engagement				
▶Percentage of grievances responded to and/or resolved within the stipulated service standards for re (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	90.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023
▲Citizen Engagement: Annual consultations held with beneficiaries and ID stakeholders and government to act on feedback received during consultations. - Disaggregated by marginalized group categories: (Yes/No, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes

Access to Services				
▶Access to Services: Number of digital authentications made by functional users (by sector or service) per month on behalf of their beneficiaries or clients (of which % on behalf of women). (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,600.00
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Implementation Readiness				
▶The FID system is operational and ready for rollout (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	02-Jul-2018	--	10-Jan-2019	03-Jul-2023

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P161329	IDA-62390	Effective	USD	67.40	67.40	0.00	0.89	61.41	1.4%
P161329	IDA-62400	Effective	USD	24.85	24.85	0.00	0.75	22.94	3.2%
P161329	IDA-D3210	Not Effective	USD	5.00	5.00	0.00	0.00	4.97	0%
P161329	IDA-D3260	Effective	USD	24.85	24.85	0.00	0.00	23.69	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P161329	IDA-62390	Effective	05-Jun-2018	13-Jul-2018	09-Nov-2018	03-Jul-2024	03-Jul-2024
P161329	IDA-62400	Effective	05-Jun-2018	27-Jun-2018	20-Dec-2018	03-Jul-2024	03-Jul-2024
P161329	IDA-D3210	Not Effective	05-Jun-2018	--	--	03-Jul-2024	03-Jul-2024
P161329	IDA-D3260	Effective	05-Jun-2018	27-Jun-2018	20-Dec-2018	03-Jul-2024	03-Jul-2024

Cumulative Disbursements

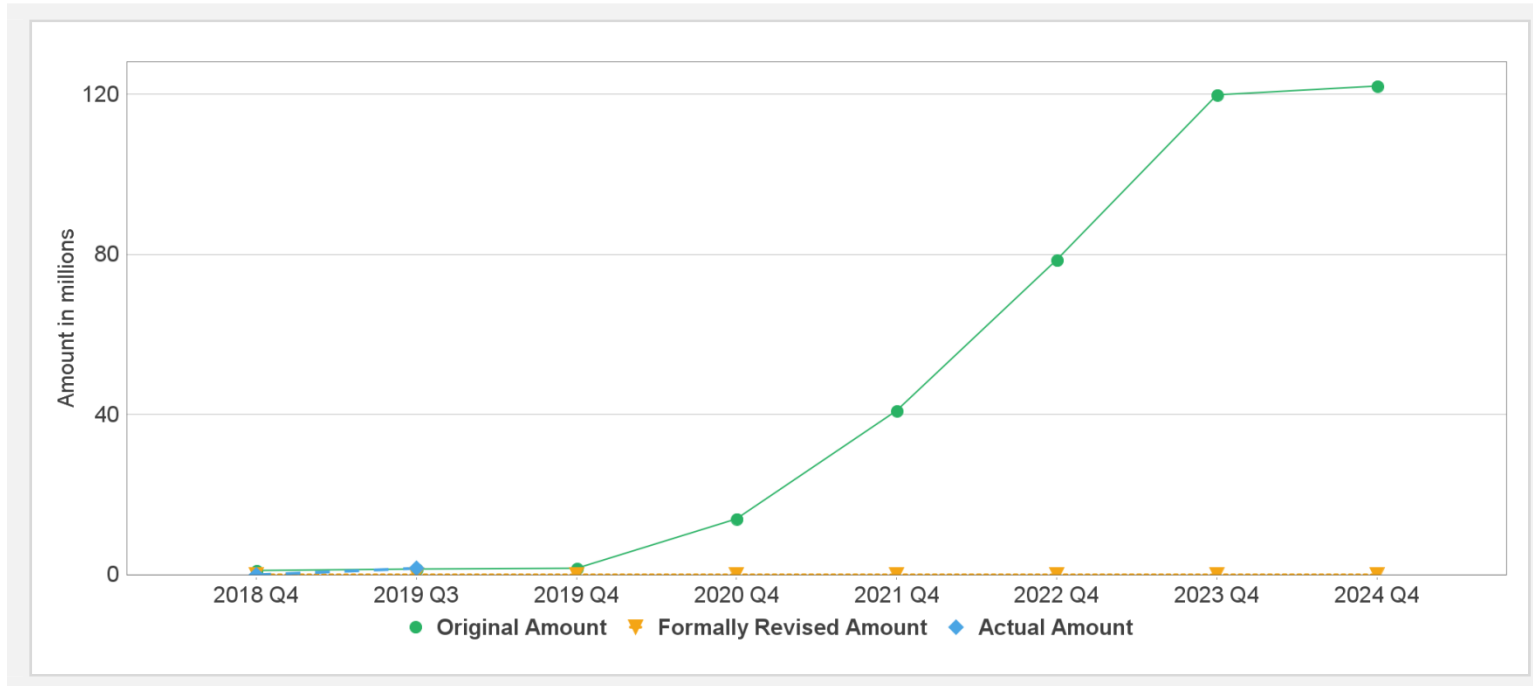



Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
