



REGIONAL PROGRAM TO HARMONIZE AND MODERNIZE LIVING CONDITIONS SURVEYS (P153702)

AFRICA | Western Africa | Poverty and Equity Global Practice |
IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 8 | ARCHIVED on 30-Jun-2020 | ISR42384 |

Implementing Agencies: West African Economic and Monetary Union, West African Economic and Monetary Union

Key Dates**Key Project Dates**

Bank Approval Date: 06-Apr-2016

Effectiveness Date: 08-Jul-2016

Planned Mid Term Review Date: 02-Dec-2019

Actual Mid-Term Review Date: 25-Nov-2019

Original Closing Date: 31-Dec-2021

Revised Closing Date: 31-Dec-2021

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The PDO is to support the WAEMU Commission at strengthening the capacity of its member countries to conduct living conditions surveys that meet harmonized, regional standards and to make the collected micro-data publicly accessible.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components Table

Name

Capacity building and survey harmonization and modernization through data collection and dissemination:(Cost \$36.30 M)

Quality control and coordination:(Cost \$4.20 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Satisfactory	<input type="checkbox"/> Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Substantial

Implementation Status and Key Decisions

The overall objective of the project is to support the WAEMU Commission to reinforce the capacity of its member eight countries to carry out Living Conditions surveys conforming to regional harmonized norms and to make the micro-data accessible to the public. After harmonizing the technical instruments, the first harmonized survey has been implemented successfully in all eight countries. Harmonized and comparable micro-data have been produced for the eight countries. Poverty numbers based on the harmonized methodology have also been produced and validated by the World Bank team and the Steering Committee of the project.

Anonymized micro-data are supposed to be disseminated in July 2020, one year after the end of data collection. When this is done, they will allow rich analytical work at the country level, and at the sub-regional level, for example the specific issues of the Sahelian countries. In addition, the project is having positive externalities as several non-beneficiary countries have adopted the same type of survey, including among others Burundi, Chad, Guinea, Republic of Comoros, Republic of Congo, Gabon, Sao-Tome and Principe, etc. Many of these countries have also benefited from capacity building events organized by the project.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	Substantial	Substantial	Substantial
Macroeconomic	Low	Low	Low
Sector Strategies and Policies	Substantial	Substantial	Substantial
Technical Design of Project or Program	Moderate	Moderate	Moderate
Institutional Capacity for Implementation and Sustainability	High	High	Moderate
Fiduciary	Substantial	Substantial	Substantial
Environment and Social	Low	Low	Low
Stakeholders	Low	Low	Low
Other	--	Substantial	High
Overall	Substantial	Substantial	Substantial

Results

PDO Indicators by Objectives / Outcomes

Build Capacity through Survey Harmonization, Data Collection and Dissemination



► WAEMU member countries which completed the collection of harmonized living conditions surveys that made the anonymized micro-data available to the public through the WAEMU website (*) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	25.00	85.00
Date	17-Apr-2016	15-May-2019	18-Jun-2020	15-Apr-2021
► WAEMU member countries that completed a 2nd living conditions survey according to harmonized, regional standards (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	7.00
Date	17-Apr-2016	15-May-2019	18-Jun-2020	15-Oct-2021

Enforce the Use of the harmonize Survey				
► Adoption by the WAEMU's Council of Minister of a ruling committing all member countries to apply WAEMU living conditions survey standards with respect to methodology, contents and periodicity (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	17-Apr-2016	15-May-2019	15-May-2019	15-Oct-2021

Overall Comments

As for the first indicator, it is relevant to note that the micro-data have been produced. The anonymization process is planned for July 2020, and then the data can be released.

Intermediate Results Indicators by Components

Capacity building and survey harmonization and modernization through data collection and dissemination				
► Draft standardized questionnaires, disaggregated by gender are reviewed by data users (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	14-Apr-2017	21-Sep-2018	18-Jun-2020	15-Apr-2021
► Standardized living conditions survey instruments and manuals(**)developed, and jointly adopted by the NSIs of all eight WAEMU member states (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	No	Yes	Yes	Yes
Date	14-Apr-2017	21-Sep-2018	18-Jun-2020	15-Apr-2021
► Regional capacity building events (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.00	11.00	8.00
Date	14-Apr-2017	08-Feb-2019	18-Jun-2020	15-Apr-2021
► A statistical abstract with selected official welfare statistics for WAEMU countries and the region are published by the WAEMU Commission (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	14-Apr-2017	15-May-2019	18-Jun-2020	15-Apr-2021
► WAEMU member countries that archive their harmonized living conditions surveys (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8.00
Date	14-Apr-2017	11-Dec-2019	18-Jun-2020	15-Apr-2021
Quality control and coordination				
► Living conditions surveys that have been subject to review by peers and by independent external parties (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	12.00
Date	14-Apr-2017	04-Nov-2019	18-Jun-2020	15-Apr-2021

Performance-Based Conditions**Data on Financial Performance****Disbursements (by loan)**

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
---------	----------------	--------	----------	----------	---------	-----------	-----------	-------------	-------------




P153702	IDA-D1120	Effective	USD	40.50	40.50	0.00	23.18	17.95	<div style="width: 56%; height: 15px; background-color: #4CAF50;"></div>	56%
---------	-----------	-----------	-----	-------	-------	------	-------	-------	--	-----

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P153702	IDA-D1120	Effective	06-Apr-2016	17-Apr-2016	08-Jul-2016	31-Dec-2021	31-Dec-2021

Cumulative Disbursements

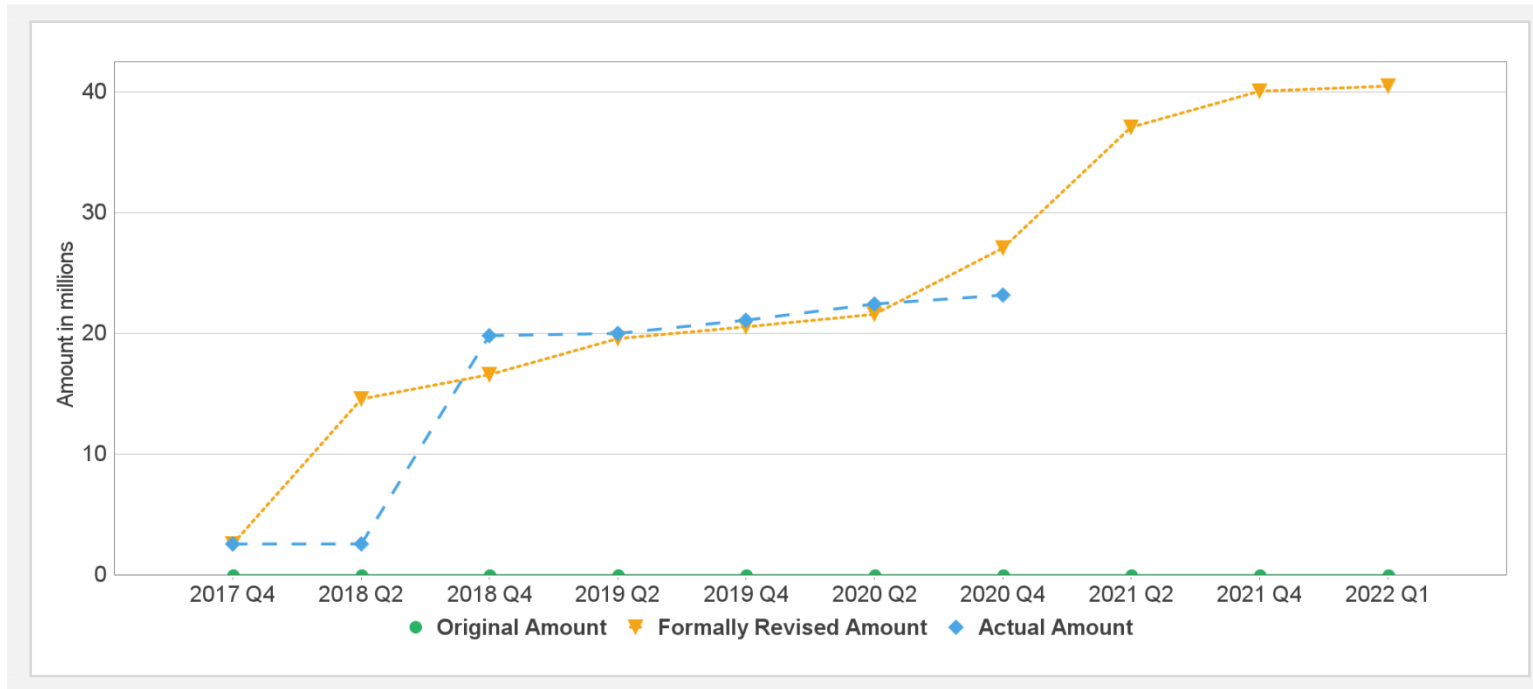

PBC Disbursement

PBC ID	PBC Type	Description	Coc	PBC Amount	Achievement Status	Disbursed amount in Coc	Disbursement % for PBC
--------	----------	-------------	-----	------------	--------------------	-------------------------	------------------------

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
