



Second Lao Environment & Social Project (former Protected Area and Wildlife Project) (P128393)

EAST ASIA AND PACIFIC | Lao People's Democratic Republic | Environment, Natural Resources & the Blue Economy Global Practice | IBRD/IDA | Investment Project Financing | FY 2014 | Seq No: 15 | ARCHIVED on 28-Dec-2020 | ISR44479 |

Implementing Agencies: Lao People's Democratic Republic, Environment Protection Fund

Key Dates**Key Project Dates**

Bank Approval Date: 02-Apr-2014

Effectiveness Date: 04-Jul-2014

Planned Mid Term Review Date: 31-Dec-2017

Actual Mid-Term Review Date: 20-Mar-2017

Original Closing Date: 30-Jun-2021

Revised Closing Date: 30-Jun-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen the management systems for national protected areas conservation and for enforcement of wildlife laws

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

The objective of the Project is to help strengthen selected environmental protection management systems, specifically for protected areas conservation, enforcement of wildlife laws and environmental assessment management.

Components Table

Name

Institution Development and Capacity Building:(Cost \$17.40 M)

Management of Wildlife and Protected Areas:(Cost \$17.60 M)

Project Administration and EPF Capacity Building:(Cost \$6.83 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> Substantial	<input type="checkbox"/> Moderate

Implementation Status and Key Decisions

Implementation progress is largely on track with tangible results becoming apparent in protected areas management, enforcement of wildlife laws, and environmental management, assessment, and planning. The project demonstrates positive progress despite facing difficulties in implementing activities due to COVID-19 outbreak and travel restriction which results in slow disbursement over the past six months. The 36 active subprojects have helped improved, to varying degrees, the functional capacity of numerous government agencies that support environmental management in



Laos. Some notable steps in the government's monitoring and enforcement role over the past six months include the good progress on the development of the Strategic Environmental Assessment (SEA) of the National Green Growth Strategy being advanced, SEA of the National Power Development Plan, the 5-year Provincial Sector Strategic Plans, admirable progress on the implementation of field activities of protected area management subprojects on both biodiversity monitoring/research and law enforcement, and the National University of Laos subprojects in exceeding expectations. However, areas that are lagging include subprojects aimed at strengthening capacity for wildlife law enforcement, where improvement is still needed in interagency cooperation and the investigation, reporting, and prosecution of illegal activities. An area that needs to be accelerated involves the disbursement livelihood development grants to 47 villages within the national parks, and issuance of the Environmental Compliance Certificate (ECC) to mining projects by some Provincial Offices for Natural Resources and Environment. Even with recent approval of a one-year closing date extension, some subprojects still need to improve their performance and pace of implementation to ensure completion of activities and outputs.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	☐ Moderate	☐ Moderate
Macroeconomic	--	☐ High	☐ Substantial
Sector Strategies and Policies	--	☐ Substantial	☐ Moderate
Technical Design of Project or Program	--	☐ Substantial	☐ Moderate
Institutional Capacity for Implementation and Sustainability	--	☐ Substantial	☐ Moderate
Fiduciary	--	☐ Substantial	☐ Moderate
Environment and Social	--	☐ Moderate	☐ Moderate
Stakeholders	--	☐ Moderate	☐ Moderate
Other	--	--	☐ Moderate
Overall	--	☐ Substantial	☐ Moderate

Results

PDO Indicators by Objectives / Outcomes

Strengthen capacity on protected area management				
► Increased score on Protected Area Management Effectiveness Tracking Tool (METT) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	19.40	22.00	10.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	The indicator exceeds the end target. The whole portfolio of LENS2 protected areas (11 protected areas via 10 sub-projects) is now at full implementation stage and showing incremental increases. All PA subprojects except the NEPL NPA subproject (approved in December 2018) have contributed to the actual increase in the METT score.			



A METT consultant, who has been on board since early 2020, assessed and provided the scores. The score increase from 17 to 22 over the year.

Strengthen systems for wildlife law enforcement

► Wildlife trafficking cases involving CITES 1 listed species that are referred to the national and/or provincial public prosecutor office (cumulative) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	24.00	32.00	75.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022

Comments:

As of November 2020, 32 wildlife trafficking cases (increased from 24 to 32 over the year) involving CITES 1 listed species have been referred to the public prosecutor office (provincial or national). And, 88 wildlife trafficking cases (involving CITES1 and non-CITES 1 listed species) have been opened for investigation. It is expected that some cases opened for investigation in 2020 will be referred to the public prosecutor in 2021.

□ Number of wildlife trafficking cases involving CITES1 and non-CITES listed species opened for investigation (cumulative) (Number, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	88.00	88.00	250.00

Strengthen capacity on environmental and natural resource management

► 5-year provincial or sectoral development plans that include environmental planning, monitoring, assessment, or management components supported by MONRE or MPI (cumulative) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.00	2.00	20.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022

Comments:

ISP has been integrated into the provincial 5-year social-economic development plan of Xayabouly and Khammouane. The government is in the process of finalizing sectoral and provincial 5-year social-economic development plans which are expected to be completed at the end of the year, but not later than March 2021.

****Note: there was a mistake in recording an achievement during the May 2020 mission. Hence, the number has gone down from 9 to 2.*

□ Plans supported by MONRE departments on environmental monitoring arrangements (cumulative) (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8.00
Date	30-Dec-2017	31-Dec-2018	13-Nov-2020	30-Jun-2022

□ Plans supported by MONRE departments on ISP and/or SEA (cumulative) (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
--	----------	-------------------	------------------	------------



Value	0.00	2.00	2.00	7.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Plans supported by MPI or NIER on GG M&E (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	7.00	0.00	5.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
► Up-to-date reports published on relevant government websites including (i) compliance monitoring for Category 2 projects, (ii) state of air and noise quality, (iii) national pollution inventory (cum.) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	99.00	99.00	87.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	As of November 2019, 18 reports on noise and air quality have been published on nreri.gov.la. As of May 2020, MONRE has also disclosed 81 project compliance monitoring reports (environmental impact category 2 projects) on both MONRE and EPF websites (laoepf.org.la). As of November 2020, the reports have been uploaded to MONRE relevant department's website: www.dpcm.monre.gov.la/io MONRE has also made extra effort to disclose EIA of investment projects for public comments on dnepp-monre.gov.la			
<input type="checkbox"/> Compliance monitoring reports for hydropower projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	39.00	39.00	40.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Compliance monitoring reports for mining projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	38.00	38.00	24.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Compliance monitoring reports for road projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4.00	4.00	7.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> State of air and noise quality report published on the MONRE website (cumulative) (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	18.00	18.00	7.00
Date	30-Dec-2017	29-Nov-2019	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> National pollution inventory report published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	30-Dec-2017	30-Apr-2019	13-Nov-2020	30-Jun-2022

Strengthen institutional capacity				
▶ Score of functional capacity of EPF and key institutions implementing subprojects (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	43.90	43.00	31.00
Date	31-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>Progress toward achieving the functional capacity indicator target (average of the scores for the participating agencies or institutions) exceeds the end of target, June 2022. EPF continues to support each SDA in their self-assessment and pre-post test tool start being used by SDAs (to measure quality of training delivered and provide quantitative data for self-assessment).</p> <p>*** There was a misunderstanding in reporting the achievement because of the unit of measurement in the May 2020 mission. The achievement has gone down from 43.9 to 43.</p>			
<input type="checkbox"/> Score of functional capacity of Environment Protection Fund (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	22.00	67.00	68.50	52.00
Date	31-Dec-2015	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Score of functional capacity of Department of Public Relation of the Prime Minister Office (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	33.00	33.00	34.00
Date	31-Dec-2015	31-Dec-2018	31-Dec-2018	30-Jun-2022
<input type="checkbox"/> Average of score of functional capacity of Faculties (NUOL FFS, FSS, FNS, FES and FEB) (number) (annual) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	38.40	31.00	28.00
Date	31-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022



Average of score of functional capacity of Protected Area Management Units (NEPL, WMPA and 7 PAFOs) (number) (annual) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	29.10	29.10	31.00
Date	31-Dec-2016	15-May-2020	15-May-2020	30-Jun-2022
Score of functional capacity of MAF DOF Protected Area Management Division (number) (annual) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	56.00	56.00	22.00
Date	31-Dec-2014	15-May-2020	15-May-2020	30-Jun-2022
Score of functional capacity of National Academy of Public Administration (NAPA) (annual) (Number) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	40.00	40.00	13.00
Date	30-Dec-2016	15-May-2020	15-May-2020	30-Jun-2022

Intermediate Results Indicators by Components

Protected area management system and biodiversity conservation				
► Score tracking the development and management of a NPA system (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	70.00	80.00	90.00
Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>This indicator is on track (EOP target is: 90) The NPA Optimization Report has been prepared (15 points); NPA Master Plan has been developed (21 points). All of 24 NPA fact sheets have been updated with village profile data and infrastructure data (24 points). Seven NPA Management Guidelines have been approved by MAF in February 2019 (7 points); three Decrees on National Park approved (10 points) by MAF. They are 1. Decree on Nakai-Nam Theun National Park establishment dated 15 February 2020; 2. Decree on Nam Et-Phou Loeuy National Park dated 15 February 2019); and 3. Decree on the establishment of Hin Nam No National Park dated May 2020. Also, a draft Decree on National Park is being prepared. SDA received Data on infrastructure projects in NPAs from CDE.</p>			
► Village organizations that meet the terms of Conservation Agreements, and as a result, receive grants for implementing their action plans (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	124.00	148.00	190.00



Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	This indicator is on track (EOP target: 190) As of November 2020, 148 community conservation agreements have been signed. NE-PL and NNT sub-project have started to implement activities related to this specific indicator. They are expected to disburse village livelihood development funds to all villages in Q1 2021.			
□ Village organizations with at least 40% female participation (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	79.00	117.00	160.00
Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022
▶ Area within selected PAs where the status of selected wildlife population and threats are measured (annual) (Hectare(Ha), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	242,000.00	370,960.00	431,856.00	634,000.00
Date	30-Dec-2016	29-Nov-2019	13-Nov-2020	30-Jun-2022
Comments:	This indicator is reported annually. As of November, the total area within selected PAs where the status of selected wildlife population and threats are measured is 431,856 ha			
▶ Area within selected PAs where the gross forest loss rate is measured (Hectare(Ha), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	305,000.00	1,195,145.00	1,244,501.00	1,250,000.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	As of November 2020, 1,244,501 hectares of 9 PAs and 2 NPAs have been measured			
▶ Wildlife crime cases detected by law enforcement officers of SDAs supported by the project (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	188.00	3,188.00	4,313.00	3,100.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	The IR indicator exceeds the end target. As of November 2020, 4,313 cases have been reported by wildlife law enforcement agencies (DOFI and POFIs, Customs and Environmental Police).			
Environmental management and pollution control				
▶ Category 1 and Category 2 projects that are under design, construction or operation that have a valid Environmental Compliance Certificate (ECC) (cum.) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	19.00	54.00	62.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>The IR Indicator is on track:</p> <p>However, Issuance of ECC for hydropower and road projects are unlikely to meet their targets due to the government having a moratorium on hydropower project with a capacity less than 15kw. In addition, PONREs are facing difficulties forcing the road rehabilitation projects to carry out an Initial Environmental Examination (IEE) as mandated in the EIA decree. Moreover, there are far fewer new projects than planned.</p> <p>As of November 2020, the total number of Category 1 and 2 projects with valid ECC is 739. Category 1 hydropower, mining and road projects with ECC is 73, 272, and 53 respectively. Category 2 hydropower, mining and road projects with ECC is 156, 131 and 54 respectively.</p> <p>**There was a mistake in the number of achievement reported during the May 2020 mission. The team recommended EPF to do a data cleansing which they already completed. Hence, a number of figures reported have been corrected.</p> <p>***The total number of project provided to EPF by the department of planning and the total number of project provided by subproject delivery agencies is slightly difference. This issue has been raised and shall be fixed by the next reporting period.</p>			
<input type="checkbox"/> Category 1 hydropower projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	35.00	79.00	62.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Category 1 mining projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	111.00	84.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Category 1 road projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	57.00	46.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Category 2 hydropower projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	62.00	100.00	85.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Category 2 mining projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	10.00	17.00	49.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
□ Category 2 road and railway projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12.00	26.00	50.00
Date	30-Dec-2016	15-May-2020	13-Nov-2020	30-Jun-2022
▶ Score tracking the development of national, provincial or sectoral guiding documents and planning tools that integrate environment into development planning (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	60.00	60.00	90.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>The IR indicator is on track:</p> <p>Substantial progress has been made: the National Green Growth Strategy has been developed and endorsed by Government on Nov. 2018 and finally promulgated by PM Office later in January 2019. The SEA guidelines has been developed and approved by MONRE Minister later in December 2018. The ISP Decree was completed in early 2019.</p> <p>The ENR M&E guidelines was completed, approved in July 2017 (Departmental Decision) and printed in April 2018.</p> <p>During the reporting period, ISP has been integrated into the 5-year social-economic development plan of Xayabouly and Khammouane. Consequently, the score increase from 55 to 60.</p> <p>MPI and MEM are in the early stage of SEAs development.</p>			
▶ Score tracking the design and adoption of pollution management instruments (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	30.00	30.00	80.00
Date	30-Dec-2017	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>The IR indicator is on track even though the it's still 30 points behind the annual target.</p> <p>Some progress have been made during the year, the Decision on National Environmental Standard has been approved (promulgated in February 2017). The Pollution Prevention and Control Regulation has been reviewed by a vice minister of MONRE. It is expected to be submitted to the MONRE minister for approval and signature after which it will gain another 30 points. National Pollution Control planning documents [Vision to 2030, 10-Year Strategy (2016-2025), and 5-Year Action Plan (2016-2020)] are at advanced stage. However, it's unlikely that the 10-Year strategy will be completed by the sub-project closing date because it has to be reviewed by the National Assembly which will prolong the process of getting it approved.</p>			
Institutional capacity enhancement and sustainable financing development				
▶ Staff of SDA and SDA partner institutions that received formal short courses or participate in study tours under the project (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	10,815.00	12,935.00	3,000.00
Date	30-Dec-2015	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	The indicator is on track: the annual target has been exceeded (3,000)			
<input type="checkbox"/> Female staff (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,657.00	3,074.00	600.00
Date	30-Dec-2015	15-May-2020	13-Nov-2020	30-Jun-2022
<input checked="" type="checkbox"/> Financing mobilized by EPF each year from (a) public sources and (b) private sources (annual) (Amount(USD), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	800,000.00	620,000.00	1,216,061.00	1,600,000.00
Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022
Comments:	<p>The annual target for 2020 is unlikely to be achieved.</p> <p>As of November 2020, US\$ 965,212 have been collected from the private sector and US\$ 250,849 earned from interest and lending revenue from project credits (non-World Bank supported)</p> <p>However, EPFO has raised \$400,000 which they will receive from the Implementation of the Governance Forest Landscape and Livelihood Project supported by GIZ. The fund will be used for project administration. Moreover, it is also expected that after completion of the EPF accreditation process for GCF small grant, about \$10M grant fund can be made available starting 2022.</p>			
<input type="checkbox"/> Funds from public sources (annual) (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	350,000.00	110,000.00	250,849.00	700,000.00
Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022
<input type="checkbox"/> Funds from private sources (annual) (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	450,000.00	510,000.00	965,212.00	900,000.00
Date	30-Dec-2014	15-May-2020	13-Nov-2020	30-Jun-2022

Overall Comments

EPFO M&E team provided training to subproject delivery agencies in July. One of the purposes was to do data cleansing. This resulted in having an accurate reporting.

Performance-Based Conditions



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P128393	IDA-53830	Effective	USD	12.50	12.50	0.00	11.50	0.00	100%
P128393	IDA-56200	Effective	USD	15.00	15.00	0.00	11.75	3.14	79%
P128393	IDA-H9150	Effective	USD	4.50	4.50	0.00	4.23	0.00	100%
P128393	TF-16619	Effective	USD	6.83	6.83	0.00	5.64	1.19	83%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P128393	IDA-53830	Effective	02-Apr-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2022
P128393	IDA-56200	Effective	29-Apr-2015	04-Jun-2015	01-Oct-2015	30-Jun-2021	30-Jun-2022
P128393	IDA-H9150	Effective	02-Apr-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2022
P128393	TF-16619	Effective	14-May-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2022

Cumulative Disbursements

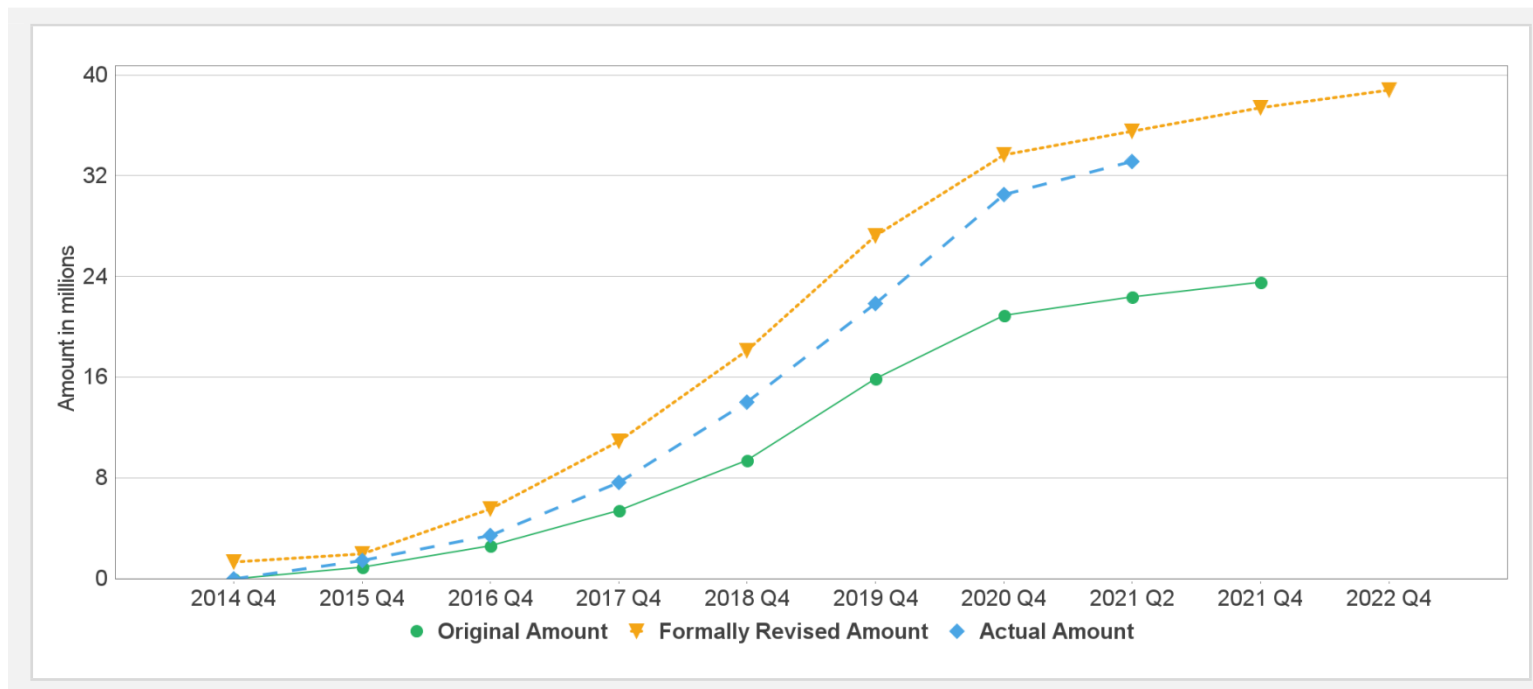



Restructuring History

Level 2 Approved on 08-Feb-2018 ,Level 2 Approved on 28-Aug-2020

Related Project(s)

P128392-Second Lao Environment & Social Project (formaly Protected Area and Wildlife) ,P152066-Second Lao Environment and Social Project (Additional Financing to the Protected Area and Wildlife Project)
