



DRC Reinsertion and Reintegration Project (P152903)

AFRICA | Congo, Democratic Republic of | Social, Urban, Rural and Resilience Global Practice Global Practice | IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 6 | ARCHIVED on 06-Dec-2018 | ISR32735 |

Implementing Agencies: UEPN-DDR, Democratic Republic of Congo, Represented by the Ministry of Finance

Key Dates

Key Project Dates

Bank Approval Date: 15-May-2015

Effectiveness Date: 27-Jan-2016

Planned Mid Term Review Date: 09-Apr-2018

Actual Mid-Term Review Date: 09-Apr-2018

Original Closing Date: 31-Dec-2019

Revised Closing Date: 31-Dec-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective (PDO) is to support the socio-economic reintegration of demobilized ex-combatants.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Reinsertion:(Cost \$5.35 M)

Component 2: Reintegration:(Cost \$8.64 M)

Component 3: Support to Demobilized Ex-combatants' Households:(Cost \$3.24 M)

Component 4: Support to Vulnerable Groups:(Cost \$1.17 M)

Component 5: Project Management, Sensitization, Monitoring and Evaluation:(Cost \$3.10 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Moderately Unsatisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Unsatisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions

- Demobilization: The project has demobilized a total of 4,700 ex-combatants (4,607 males and 93 females) since its official launch on February 26, 2016 (2,038 from the Reintegration Preparation Center (RPC) in Kitona and 2,662 from the RPC in Kamina).
- Reinsertion: 3,786 ex-combatants finished their training cycle and have been reintegrated back into their communities, while 649 are still in the RPCs (298 (294 in Kamina and 351 in Kitona) and waiting to be reintegrated. The general and vocational trainings ended in February 2018 in Kamina and in October 2017 in Kitona.



3. Reintegration: 3,786 ex-combatants have been successfully reintegrated into their communities. Reintegration activities implemented by three Implementing Partners (IPs) namely CARITAS, INPP and FAO, started in October 2016. The IPs are continuing their outreach and support services for their designated demobilized caseloads allocated based on their vocational specialty. Distribution of reintegration kits is also progressing.
4. Support to Demobilized Ex-Combatants' Households: In the months of November and December 2017, UEPNDDR contracted 8 out of 10 NGOs in earmarked Reintegration zones to provide vocational training to demobilized dependents. Activities in this component include the identification, orientation – vocational training selection, training and distribution of kits. To date 2750 dependents have been identified and received vocational training and technical support, while 1170 have received their start-up kits to begin or reinforce their income generating activities in different sectors (restaurant, bakery, soap making, flour milling, fish selling, butchery).
5. Psychosocial Support: Living Peace Institute – LPI delivered training to 50 outreach officers of UEPNDDR and its partners, whose main objective was to promote awareness of the psychosocial and mental health needs of the Project beneficiaries in order to support the meaningful implementation of psychosocial support by the project staff working most closely with beneficiaries.
6. Mid-term review (MTR): an MTR of the Project was undertaken in April-May 2018, to take stock of the Project's achievements and challenges, and to plan the way forward.
7. Overall, implementation delays, mostly due to operational challenges/constraints (including security), are likely to impact the ability of the Project to meet its objectives/targets.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● High	● High	● High
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● Substantial	● Substantial	● Substantial
Technical Design of Project or Program	● Substantial	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Substantial	● Substantial	● Substantial
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Substantial	● Substantial	● High
Other	● High	● High	● High
Overall	● Substantial	● Substantial	● Substantial

Results

PDO Indicators by Objectives / Outcomes

PDO: To support the socio-economic reintegration of demobilized ex-combatants.				
▶ 1. Direct project beneficiaries (disaggregated by gender) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	4,693.00	4,700.00	4,800.00



Date	31-Oct-2015	29-May-2018	30-Sep-2018	30-Jun-2019
►2. Adult individual beneficiaries participating in an economic activity 6 months after training completion (disaggregated by gender, individual or economic association, agrarian/non-agrarian) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	25.70	16.30	25.70	70.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019
►3. Beneficiaries able to meet their monthly household food consumption needs after 6 months at the reintegration location (disaggregated by gender, individual or economic assoc., agrarian/non-agrarian (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	16.30	82.00	82.00	70.00
Date	31-May-2016	29-May-2018	30-Sep-2018	30-Jun-2019
►4. Demobilized beneficiaries feel socially accepted by their communities after 6 months at the reintegration location (disaggregated by gender, individual or economic association, agrarian/non-agrarian (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	82.00	82.00	82.00	45.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-May-2019

Intermediate Results Indicators by Components

Component 1: Reinsertion				
►1a. Demobilized adults completed reinsertion phase (disaggregated by gender) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3,782.00	4,700.00	4,560.00
Date	31-Oct-2015	29-May-2018	30-Sep-2018	30-May-2019

Component 2: Reintegration				
►Indicator 1b: Economic associations established by individual beneficiaries (disaggregated by gender, agrarian/non-agrarian) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	87.00	87.00	300.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019
►1c. Beneficiaries satisfied with reintegration support (disaggregated by gender, individual or economic association, agrarian/non-agrarian) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	6.90	6.90	6.90	65.00
Date	31-Oct-2015	29-May-2018	30-Sep-2018	30-Jun-2019
►1d. Beneficiaries consuming at least 2 meals a day after 6 months at the reintegration location (disaggregated by gender, individual or economic association, agrarian/non-agrarian) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	27.50	27.50	27.50	70.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019

Component 3: Support to Demobilized Ex-combatants' Households

►2a. Ex-combatant spouse or nominated household member report perceiving demobilized as socially reintegrated in the community (disaggregated by gender, agrarian/non-agrarian) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	90.60	90.60	90.60	70.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019
►2b. Ex-combatant spouse or nominated household member participating in community activities (disaggregated by gender, agrarian/non-agrarian) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	73.20	73.20	73.20	60.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019

Component 4: Support to Vulnerable Groups

►3a. Psycho-social support provided to those identified as traumatized through screening (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Oct-2015	29-May-2018	30-Sep-2018	30-Jun-2019
►3b. Individual beneficiaries who received psycho-social support reporting improved mental health (disaggregated by gender, individual or economic association, agrarian/non-agrarian) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	65.00
Date	31-Oct-2015	29-May-2018	30-Sep-2018	30-Jun-2019
►3c. Women ex-combatants report they were treated the same or better than male ex-combatants by the project. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	73.90	73.90	73.90	65.00
Date	31-Aug-2016	29-May-2018	30-Sep-2018	30-Jun-2019

Overall Comments

The psychosocial support activities have not begun for the project, however, training on psycho-social support to sensitize UEPNDDR staff and implementing partners has been conducted.

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P152903	IDA-D0600	Effective	USD	15.00	15.00	0.00	14.18	1.00	93%
P152903	TF-A0087	Closed	USD	6.50	6.44	0.06	6.44	0.00	100%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P152903	IDA-D0600	Effective	15-May-2015	09-Jul-2015	27-Jan-2016	31-Dec-2019	31-Dec-2019
P152903	TF-A0087	Closed	15-May-2015	09-Jul-2015	27-Jan-2016	30-Jun-2016	30-Jun-2017

Cumulative Disbursements

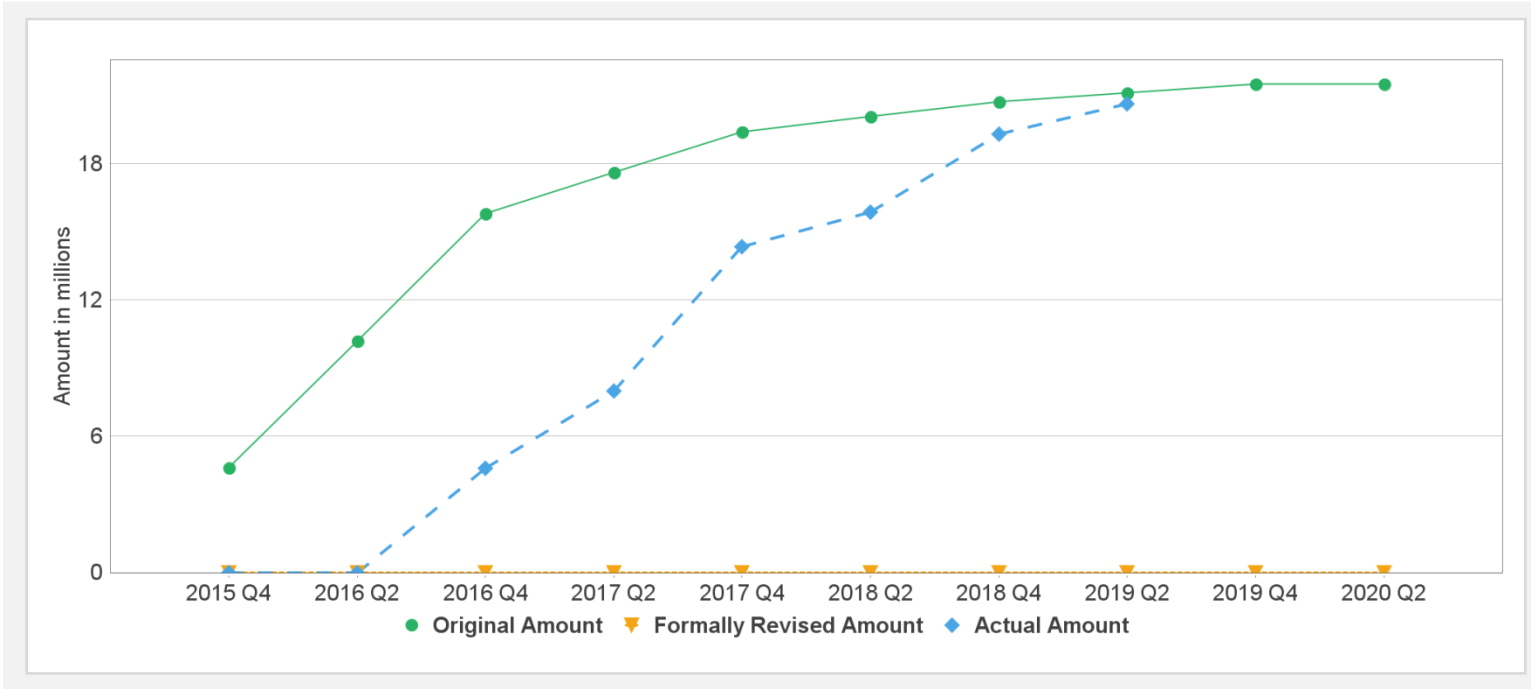

Restructuring History

Level 2 Approved on 25-Jun-2016 ,Level 2 Approved on 02-Sep-2016 ,Level 2 Approved on 12-Dec-2016

Related Project(s)

There are no related projects.
