



Renovation of General Education Project (P150058)

EAST ASIA AND PACIFIC | Vietnam | Education Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 4 | ARCHIVED on 06-Jun-2017 | ISR27011 |

Implementing Agencies: Ministry of Education and Training, SOCIALIST REPUBLIC OF VIETNAM

Key Dates

Key Project Dates

Bank Approval Date:30-Jun-2015

Effectiveness Date:08-Aug-2016

Planned Mid Term Review Date:11-Jun-2018

Actual Mid-Term Review Date:--

Original Closing Date:31-Dec-2020

Revised Closing Date:31-Dec-2020

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to raise student learning outcomes by: (i) revising and implementing the curriculum following a competency-based approach; and (ii) improving the effectiveness of instruction by creating and disseminating textbooks aligned with the revised curriculum.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Curriculum Development:(Cost \$17.50 M)

Development and Dissemination of Aligned Textbooks:(Cost \$21.60 M)

Learning Assessment and Analysis for Continuous Improvement of Curriculum and Policy:(Cost \$35.40 M)

Project Management:(Cost \$2.50 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial



Implementation Status and Key Decisions

The Annual Work Plan for 2017, including key dates, training and event plans, has been finalized, and received the requisite No Objection from the World Bank Task Team. Revision of the General and Subject Specific Curricula is currently underway, which entails revising the curricula based on Learning Outcome Standards for all subject and grades. The target date for the revised General Curriculum's official approval is Q3 2017. The revision of the subject-specific curricula will culminate in the adoption by the Ministry of Education and Training in Q1/Q2 2018.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	● Substantial	● Substantial
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● Low	● Low	● Low
Technical Design of Project or Program	● High	● High	● High
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Substantial	● Substantial	● Substantial
Environment and Social	● Low	● Low	● Low
Stakeholders	● Substantial	● Substantial	● Substantial



Other	● Low	● Low	● Low
Overall	● Substantial	● Substantial	● Substantial

Results

Project Development Objective Indicators

► Student learning gains (Text) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Partially derived from 2011 and 2014 Exams and 1st iteration of the Project's NLSA.	--	Detailed review of existing exam data underway as part of baseline construction.	A gain of at least 0.12 standard deviation in Math and Vietnamese test scores.
Date	30-Jun-2016	15-Dec-2016	26-Apr-2017	30-Dec-2020

► Teacher preparedness for new curriculum (Percentage) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	25.00
Date	10-Nov-2015	--	26-Apr-2017	30-Dec-2020

► Equitable access to learning materials (Text) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Ratio of available textbooks in math and reading to enrolled students in primary schools in disadvantaged areas.	--	Data review and collection underway to establish baseline	1.1 times baseline rate
Date	10-Nov-2015	15-Dec-2016	26-Apr-2017	30-Dec-2020

Overall Comments



Intermediate Results Indicators

► Core Technical Committee Qualifications (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Committee seated	--	Evaluation in process	12.00
Date	10-Nov-2015	--	26-Apr-2017	30-Dec-2020

► Online Training System Readiness (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No system currently exists	--	No system currently exists	50% of teacher have had at least some training
Date	10-Nov-2015	19-Dec-2016	26-Apr-2017	30-Dec-2020

► Curriculum Champions (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8,000.00
Date	10-Nov-2015	19-Dec-2016	26-Apr-2017	30-Dec-2020

► Textbook Production (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No new textbooks have been approved	--	No textbooks have been approved.	72 = 1 per grade per academic subject
Date	10-Nov-2015	--	26-Apr-2017	30-Dec-2020



► Curriculum Piloting (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No pilot available until the revisions are made	--	Pilots to be developed subsequent to revision of curricular learning goals	30 classrooms per grade + 30 classroom control monitored
Date	15-Dec-2015	--	26-Apr-2017	30-Dec-2020

► Expanded National Large-Scale Assessment System (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Current system measures learning of high school leavers only	--	Key Exam developers identified	Exams administered at 5th, 9th, and 11th grades for nationally-representative sample
Date	10-Nov-2015	19-Dec-2016	26-Apr-2017	30-Dec-2020

► Direct project beneficiaries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	5,000,000.00
Date	10-Nov-2015	19-Dec-2016	26-Apr-2017	30-Dec-2020

▲ Female beneficiaries (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	50.00

Overall Comments



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P150058	IDA-56910	Effective	XDR	55.40	55.40	0.00	1.26	54.14	2%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P150058	IDA-56910	Effective	30-Jun-2015	08-Apr-2016	08-Aug-2016	31-Dec-2020	31-Dec-2020

Cumulative Disbursements

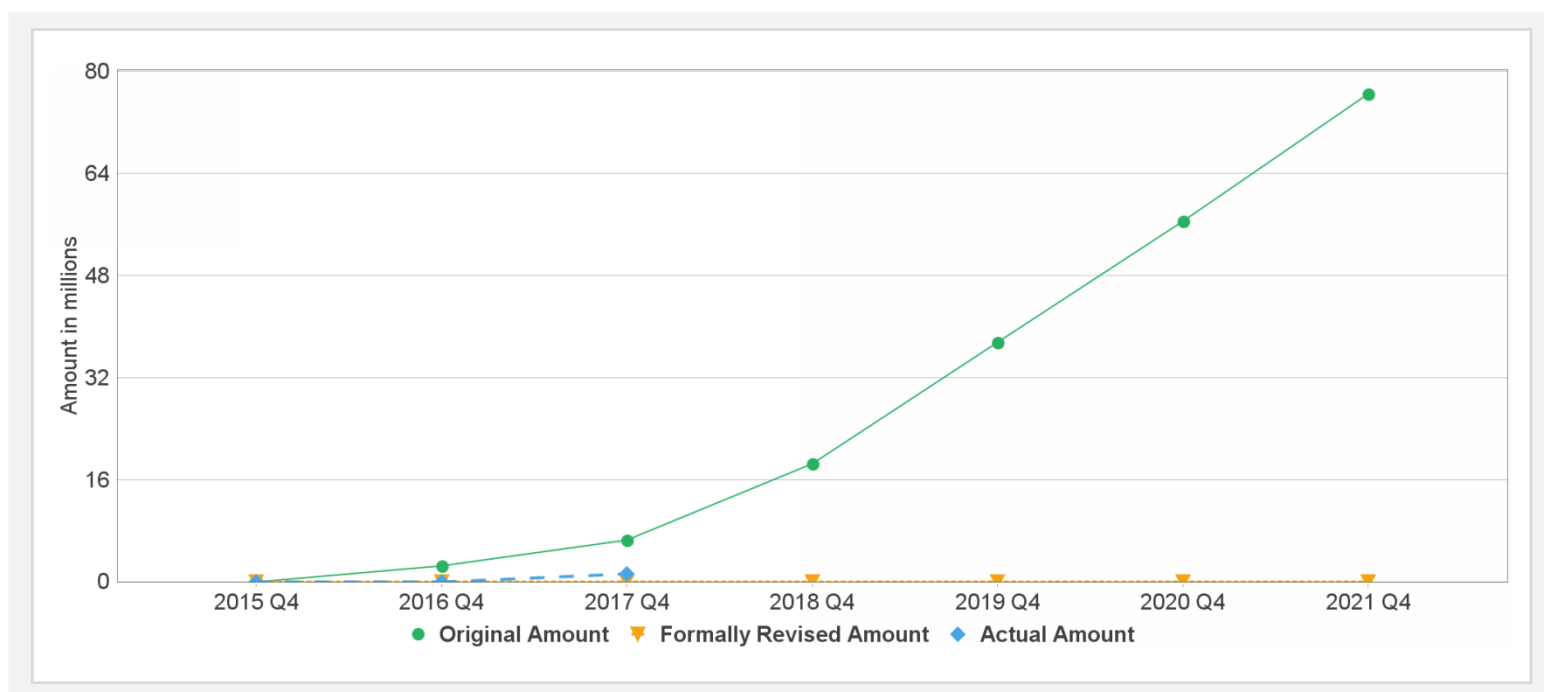

Restructuring History

There has been no restructuring to date.



Related Project(s)

There are no related projects.
