



Education Sector - Ebola Recovery and Reconstruction Project (P154880)

AFRICA | Liberia | Education Global Practice |
 Recipient Executed Activities | Investment Project Financing | FY 2015 | Seq No: 1 | ARCHIVED on 16-Dec-2016 | ISR26143 |

Implementing Agencies: Ministry of Education

Key Dates

Key Project Dates

Bank Approval Date:06-Sep-2015

Effectiveness Date:06-Oct-2015

Original Closing Date:31-Dec-2016

Revised Closing Date:31-Dec-2016

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective (PDO) is to support the implementation of key elements of the Liberian education sector's short-term Ebola response plan to minimize the impact of the epidemic on school-age children by safely reopening schools, motivating students and teachers to return to the classroom, and enhancing the quality of learning.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Moderately Satisfactory
Overall Implementation Progress (IP)	--	● Moderately Satisfactory

Implementation Status and Key Decisions

The project has made significant progress in the implementation of project activities: 1) Under Component 1 Health and Hygiene, deworming medicine has been distributed to 1,290,397 school-aged children under the project; 2) Under Component 2 Information Dissemination, a campaign was developed and launched via radio and television stations to promote the protocols related to school reopening following the Ebola Virus Disease; and 3) Under Component 3 Support to Students, Families, and Schools, the distribution of learning and teaching materials (procured under the Global Partnership for Education Grant for Basic Education Project) was divided into two phases. The first phase has been completed.



Due to the extended rainy season and difficult road conditions, the second phase distribution is ongoing but has been delayed. Consequently, the training of teachers on the materials distributed has also been delayed.

Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	--	● Moderate

Comments

There are risks associated with not completing all project activities by the current closing date. To mitigate the risks, the World Bank is currently processing a two-month extension of the project. In addition, the task team has assigned an operations specialist based in Monrovia to the project to provide support and track project implementation progress.

Results

Project Development Objective Indicators

►Percentage of students enrolled in public schools (out of 2014 enrollment) one year after official reopening date (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	124.00	90.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016

Comments

The indicator value is calculated by dividing the public school enrollment figure estimate in 2015-16 by the public school enrollment figure estimate in 2012-2013.

►Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	1290397.00	600000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016



Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	54.00	50.00

Overall Comments

Intermediate Results Indicators

Radio broadcasts aired (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	Y	Y
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016

Number of teachers who completed curriculum refresher training (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	10000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Jun-2016

Number of students who received deworming medicines (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	1290397.00	600000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016



▶Number of reader's aid distributed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	118289.00	200000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016

▶Number of sets of books distributed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	23996.00	45000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016


▶Number of charts distributed (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	62800.00	75000.00
Date	01-Oct-2015	--	01-Nov-2016	30-Dec-2016

Overall Comments

Data on Financial Performance

Disbursements (by loan)


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P154880	TF-A1017	Effective	USD	1.00	1.00	0.00	0.73	0.27	 73%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P154880	TF-A1017	Effective	30-Sep-2015	06-Oct-2015	06-Oct-2015	31-Dec-2016	31-Dec-2016



Cumulative Disbursements

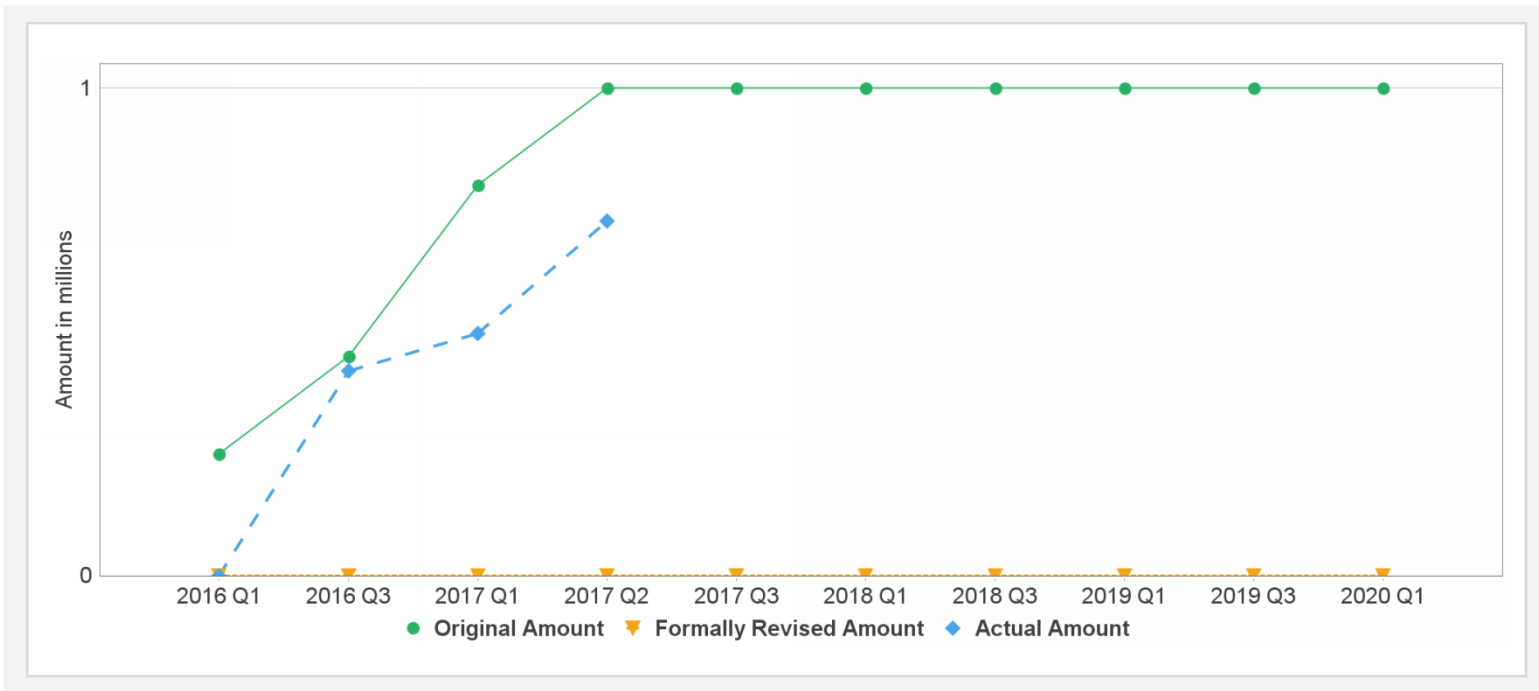

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
