



Second State Statistical System Development Project (P092429)

EUROPE AND CENTRAL ASIA | Russian Federation | Poverty and Equity Global Practice |
IBRD/IDA | Investment Project Financing | FY 2007 | Seq No: 15 | ARCHIVED on 01-Feb-2018 | ISR31185 |

Implementing Agencies: Federal State Statistical Service (ROSSTAT), Russian Federation

Key Dates

Key Project Dates

Bank Approval Date:28-Jun-2007

Effectiveness Date:22-Apr-2008

Planned Mid Term Review Date:26-Oct-2010

Actual Mid-Term Review Date:03-Feb-2011

Original Closing Date:25-Aug-2012

Revised Closing Date:31-Dec-2018

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The main objective of the project to assist the government of the Russian Federation to produce reliable, timely and accurate economic, financial, socio-demographic and other data for policy formulation and decision making in line with international good practice and frameworks.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component A. Modernization of economic statistics methodology:(Cost \$6.99 M)

Component B. Development of the modern design and technology for statistical data collection, processing and dissemination:(Cost \$79.43 M)

Component C. Enhancement of social statistics:(Cost \$4.26 M)

Component D. Human resource development:(Cost \$7.95 M)

Component E. Project management:(Cost \$7.37 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Moderate	● Moderate



Implementation Status and Key Decisions

All project activities that have been completed and those under implementation contribute to strengthening of multidimensional capacity of the Russian Federal State Statistical Service (Rosstat). In line with Project Development Objectives the project results already allow for solving a wider range of methodology issues based on the international standards and modern information technologies with a higher degree of automation used for data collection. Statistical data collected by Rosstat and other data producers serve not only the internal decision making cycle in the country, but are officially used by the international statistical organizations. These achievements are therefore, seen as a recognition of compliance with international standards and a proof of data reliability. The Second State Statistical System Development Project (STASYS 2) continues to support fulfillment of the Russia Federation's responsibilities in international data and information exchange process, increasing harmonization of national statistical system with the best international practices.

Currently, project implementation is proceeding smoothly and according to the schedule. Overall, the activities included in the last project extension for 2016-2018 have helped to continue scaling up the results already achieved and to further strengthen the Project Development Objectives. The main outputs include:

- a) advancement of system of national accounts of the Russian Federation. It includes: (i) higher quality of macroeconomic estimates, such as GDP/GRP, introduction of standard statistical units, and centralization of the regional estimates calculation; (ii) switching to 2008 SNA standards, in particular, treatment of expenditures on military equipment as fixed capital formation, and treatment of research and development as capital formation, estimation of fixed capital formation within gross value added, etc. In the transition to the 2008 SNA, the most significant changes in the final use have affected the capital formation sphere. The evaluation of the fixed capital consumption on the basis of the assets market values has been introduced into the calculation practices; (iii) introduction of the environmental and economic accounting into the practices of the national accounting in Russia; compilation of balance sheets with the account for the environmental assets.
- b) improvement of social statistics: a methodology was developed for conducting comprehensive and specific surveys of the living conditions of the population and for poverty monitoring; the analysis was carried out and the methodology and techniques for the compilation of microdata and the data of household budget survey and providing access to survey microdata and aggregated data for external users have been improved.
- c) modernization of Rosstat Computing and Information System (CIS), which made possible to improve the system for data collection and processing, introduce elements of multidimensional data analysis using integrated data warehouses with the purpose of creating statistical queries and carrying out analytical data processing (including arbitrary queries), and also to establish an efficient integrated system for protecting statistical information resources from unauthorized access. The transition from a decentralized to a centralized IT infrastructure is being done, which provides for more efficient management and use of the IT systems and ensures solution for more complicated problems under restricted budget financing through optimization of the resource uses.

Overall, project PDO and IP ratings remain Satisfactory.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Moderate	● Moderate
Macroeconomic	--	● Moderate	● Moderate
Sector Strategies and Policies	--	● Moderate	● Moderate
Technical Design of Project or Program	--	● Low	● Low
Institutional Capacity for Implementation and Sustainability	--	● Low	● Low
Fiduciary	--	● Low	● Low
Environment and Social	--	● Low	● Low



Stakeholders	--	● Low	● Low
Other	--	--	--
Overall	--	● Moderate	● Moderate

Results

Project Development Objective Indicators

► Regular analysis of users' satisfaction (Index of users' trust to official statistical data) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 - no user satisfaction surveys	Survey was scheduled for 2017 with a target value of 1.04. There is no data for 2016.	1.02	1.04 and sustained annual regularity or once in two years.
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

► Data quality assessment for National Accounts Statistics (NAS) (as per DQAF for National Accounts Statistics as detailed in the IMF 2012 Guidelines) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 - no self-assessments done. First time in 2010 -1.	Survey was scheduled for 2018 with a target value of 1.12.	- (No data available yet. Survey will be conducted later in 2018)	1.12
Date	30-Dec-2010	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

No data available yet. Survey will be conducted later in 2018

► Share of statistical information provided by Rosstat to the users according to established time schedule (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2006 - 97.8%	100%	100%	Not less than 100%
Date	28-Jun-2007	25-Sep-2017	04-Jan-2018	31-Dec-2018



Comments

The target value has been reached in 2008

Overall Comments

Intermediate Results Indicators

► The Statistical Council is established (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No Statistical Council	Statistical Council is functioning with minutes of meetings available.	Yes	Statistical Council is established
Date	28-Jun-2007	25-Sep-2017	04-Jan-2018	31-Dec-2018

Comments

The target has been reached in 2009. Since then, the Statistical Council is fully operational.

► Share of official statistical reporting forms that could be submitted to NSO electronically (as % of 2015) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	80.00	85.00	90.00	100.00
Date	01-May-2015	28-Jun-2017	04-Jan-2018	31-Dec-2018



► Degree of implementation of 2008 SNA into Russian statistical practices (% of works fulfilled in accordance with "Action Plan to implement OECD recommendations for developing the SNA in Russian Federa (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	70.00	75.00	85.00
Date	01-May-2015	28-Jun-2017	04-Jan-2018	31-Dec-2018

► Regional Statistical Offices employees dealing with receiving and processing primary statistical data (as % of 2015) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	100.00	90.00	80.00	70.00
Date	01-May-2015	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

TSB (Territorial Statistical Bodies) is the equivalent for Regional Statistical Offices.

► Number of methodological guidelines prepared for implementation for compiling satellite accounts in the social sphere recommended by OECD (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	2.00
Date	01-May-2015	28-Jun-2017	04-Jan-2018	31-Dec-2018

► Dynamics of Rosstat staff training (number of trained staff) (persons) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	8 764	1,793.00	1,713.00	The level of satisfaction of Rosstat training needs in 2013
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments



The end target "The level of satisfaction of Rosstat training needs in 2013" refers to the level of planned needs satisfied by the actual training provided during the year.

Starting in 2010, the end target was achieved.

Number of trained staff. Monitoring covers number of Rosstat staffers planned for training at the beginning of the fiscal/calendar year and the actual amount trained.

► Dynamics of state budget expenditures for training purposes (thousand rubles) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Unstable dynamics of budget allocations for training purposes	9.76	9,18	Prevailing of state budget financing of Rosstat training during the entire project period
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

► Total number of classifications used throughout the SSS that are compatible with the equivalent international classifications (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 - 7	12.00	12.00	12.00
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

► Mastering of international standards (filling out the statistical questionnaires of International Organizations with harmonized indicators) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	85%	End target value reached in 2010 and maintained till 2014.	End target value reached in 2010 and maintained till 2014.	90%.
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

Starting 2014 this indicator was substituted with another one due to changes in the set of questionnaires received from the international organizations. The previously established end target was achieved in full.



► Number of sample surveys in different economic and social fields that are conducted on a census basis (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	54.00	59 (target value - 56)	55.00	61.00
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	27-Dec-2013

Comments

New wording reflects more accurately and strictly the indicator.

The actual end target value (61) was reached in 2013. Since 2013 there are no activities in support of the indicator. We are just monitoring it.

► Reduction in respondent (enterprise) burden (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	100%	+	+	+
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

The symbols (+/-) reflect the positive and negative dynamics in respondent's burden. The dynamic is traced based on the reduction of statistical forms mandatory for reporting, introduction of electronic methods and reduction in number of questions in the questionnaires.



► Number of new surveys and/or modules of data collection (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.00	3.00	Not less than 10
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2013

Comments

New wording (old: Number of new methods of data collection).

Indicator calculated based on new statistical forms developed and introduced.

The end target value (13) was achieved in 2013.

► Number of MDG indicators produced by the SSS (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	33 out of 48	34.00	34.00	34 out of 48
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

The number of MDGs relevant to Russia has been reflected in so-called "MDG+ List" and equal to 34. The end target value has been achieved in full.

► Compliance with the ICLS household income and expenditure methodology (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Partial	In full	In full	In full
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

Compliance with the International Conference of Labor Statistics (ICLS) for household income and expenditure methodology.

Documentation that confirms compliance with ICLS methodology is available.



► Availability of data on skilled labor, demand for skilled labor (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Non available	Survey was conducted in 2016. Data will be available shortly.	Survey is conducted every two years. The next one is scheduled for 2018.	Available starting from 2010
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

The survey was conducted for the 1st time in 2010 with data available.

► Number of Rosstat website visits per annum (thousands) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 -500K	2,905.00	Data will be available shortly	Positive (increasing) dynamics of Rosstat web site visits though out the project up to 1000K.
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

Rosstat website visits in thousands per annum.

► Availability of data collected through remote/distanced methods (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	65.00	60.00
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

The end target (60%) was achieved in 2013 (61%).



► Computer equipment of Rosstat staff (MODERN computer equipment) (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 - 1 PC for 1 employee	1 for 1	x	1 for 1
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

Modern computers procured and installed by the project in 2014. The status of the equipment is assessed every two years.

► Availability of HBS and LFS microdata bases for users in open access (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Pilot (open access to sample HBS microdata for 2003 and 2004)	Yes. The LFS micro data sets were planned to be placed on the web in 2016.	Yes	Full microdata bases for users are in open access, including the LFS data.
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

Indicator "Availability of microdata bases for users in open access (HHS and LFS)" reworded "Availability of HBS and LFS microdata bases for users in open access".

The end target value is reached.



► Number of statistical tasks resolved on a new technological basis and forwarded to the United Foundation of algorithms and programs (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2007 - 34	All statistical tasks are being resolved on a new technological basis since 2011.	All statistical tasks are being resolved on a new technological basis since 2011.	More than 300
Date	28-Jun-2007	28-Jun-2017	04-Jan-2018	31-Dec-2015

Comments

The end target value was reached in 2010.

► Number of systemic statistical tasks moved to centralized primary statistical data processing (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	6.00	6.00	6.00
Date	04-Dec-2014	28-Jun-2017	04-Jan-2018	31-Dec-2018

Comments

End target value was achieved in 2015.

► Application of internationally accepted statistical methodologies and standards (questionnaires of international organizations listed in Federal Statistical Action Plan and official OECD questionnaire (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	70.00	0.00	76.00	77.00
Date	01-Jul-2013	28-Jun-2017	04-Jan-2018	31-Dec-2018

Overall Comments



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P092429	IBRD-48670	Effective	USD	10.00	10.00	0.00	9.75	0.25	98%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P092429	IBRD-48670	Effective	28-Jun-2007	30-Nov-2007	22-Apr-2008	25-Aug-2012	31-Dec-2018

Cumulative Disbursements

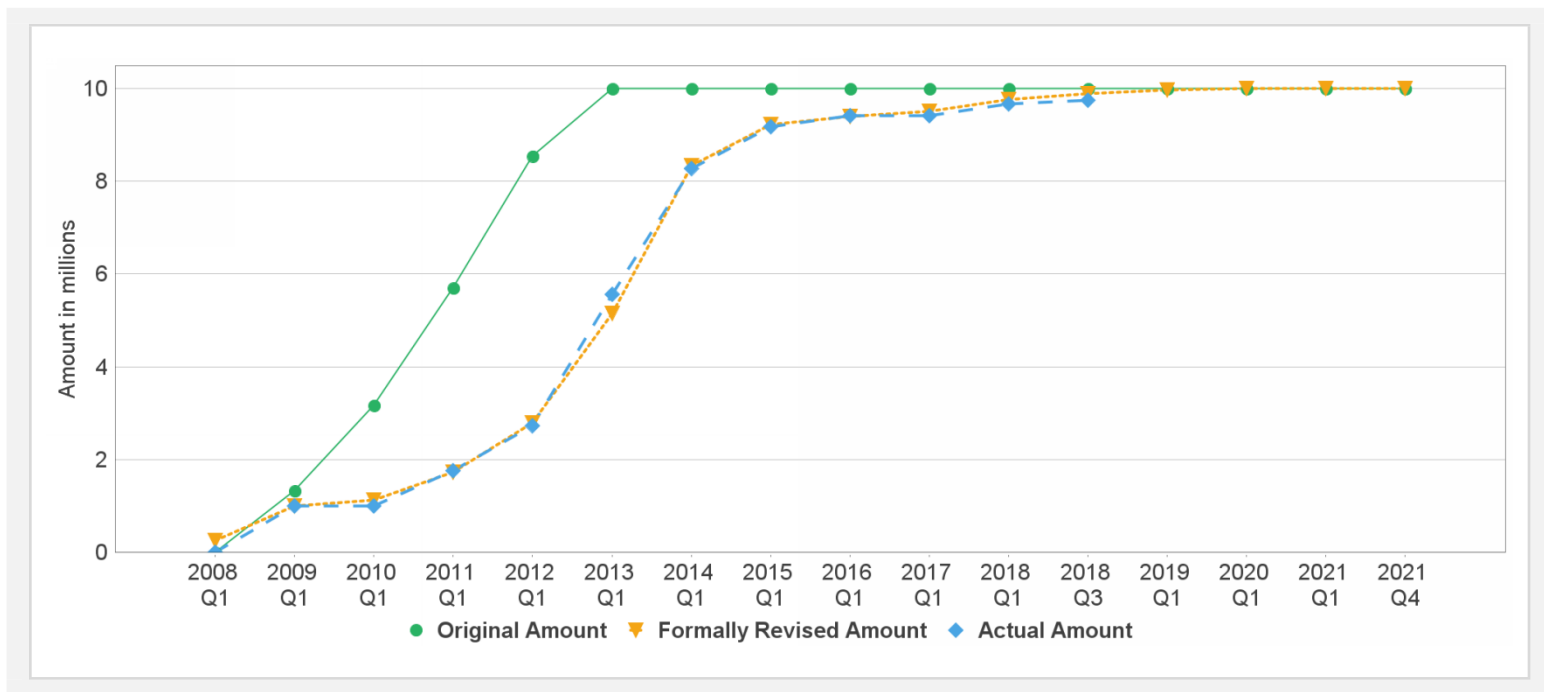

Restructuring History

Level Approved on 17-May-2012 ,Level 2 Approved on 25-Jan-2014 ,Level 2 Approved on 19-May-2015

Related Project(s)



There are no related projects.
