



Emergency Food and Livestock Crisis Response Project (P151215)

AFRICA | Chad | Agriculture Global Practice |

IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 3 | ARCHIVED on 18-Nov-2016 | ISR25738 |

Implementing Agencies: Ministry of Agriculture and Environment

Key Dates

Key Project Dates

Bank Approval Date:14-Oct-2014

Effectiveness Date:02-Mar-2015

Planned Mid Term Review Date:--

Actual Mid-Term Review Date:--

Original Closing Date:30-Apr-2017

Revised Closing Date:30-Apr-2017

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to improve the availability of and access to food and livestock productive capacity for targeted beneficiaries affected by the conflict in the Central African Republic on the Recipient's territory.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Targeted Food Assistance:(Cost \$7.00 M)

Agricultural Production and Livestock Stabilization:(Cost \$11.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions



The targeted food assistance component implemented by WFP has been completed. A total of 32,460 beneficiaries (50% female) received food vouchers (against a target of 31,200) and a total of 2,520 children between the ages of 6 and 59 months received nutritional supplements (200 grams daily of Supercereal Plus during a 2 month period) to combat moderate acute malnutrition. The agricultural production and livestock stabilization component implemented by FAO is ongoing and has experienced delays in implementation. As of April 2016, 5,000 households had received basic technology packages for garden production during the 2015/16 dry season. Results are not yet available for the 2016 rainy season where an additional 10,000 households were targeted to receive for technology packages. The project is scheduled to close April 30, 2017.

Risks

Systematic Operations Risk-rating Tool



Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● High	● High
Macroeconomic	--	● Substantial	● Substantial
Sector Strategies and Policies	--	● Substantial	● Substantial
Technical Design of Project or Program	--	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Substantial	● Substantial
Environment and Social	--	● Substantial	● Substantial
Stakeholders	--	● Substantial	● Substantial
Other	--	● Substantial	● Substantial
Overall	--	● Substantial	● Substantial

Results

Project Development Objective Indicators

► Number of agricultural input packages distributed to beneficiaries in the target areas (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	5000.00	15000.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

► Number of direct beneficiaries of vouchers or direct food transfers (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	32460.00	31200.00
Date	03-Mar-2015	02-Apr-2015	30-Apr-2016	30-Apr-2017

► Number of livestock (cattle) vaccinated (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1500000.00



Date	03-Mar-2015	02-Apr-2015	30-Apr-2016	30-Apr-2017
Comments	Vaccines have been procured by vaccination campaign not yet completed			

► Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	39980.00	116200.00
Date	03-Mar-2015	02-Apr-2015	30-Apr-2016	30-Apr-2017

▲ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	50.00	50.00

Overall Comments

Intermediate Results Indicators

► Direct food transfers (Metric ton, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	6492.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

Comments

No direct food transfers were made. All transfers were made via vouchers. The vouchers were valued at USD 11.25 per person per month. This was a change agreed upon between WFP, the government and the Bank.



► Blanket supplemental feeding (Metric ton, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	30.00	14.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

Comments

Supercereal Plus replaced Plump'Doz due to packaging issues with the latter. The difference in the two products may have allowed the distribution of nearly double the targeted amount. The figure and reason for the larger amount needs to be confirmed with WFP.

► Households receiving breeding stock (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1000.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

Comments

6,500 breeding stock (sheep and goats) have been procured but not yet distributed to beneficiaries

► Animal feed distributed (Metric ton, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	2700.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

Comments

no data yet available



▶ People trained (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	75.00
Date	03-Mar-2015	--	30-Apr-2016	30-Apr-2017

Comments

no data yet available

▲ Decentralized staff trained (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	60.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

▶ People participating in training sessions on conflict resolution (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1000.00
Date	03-Mar-2015	16-Mar-2015	30-Apr-2016	30-Apr-2017

Comments

no data yet available

Overall Comments

Data on Financial Performance**Disbursements (by loan)**


Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P151215	IDA-H9930	Effective	XDR	11.90	11.90	0.00	11.90	0.00	100%



Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P151215	IDA-H9930	Effective	14-Oct-2014	15-Dec-2014	02-Mar-2015	30-Apr-2017	30-Apr-2017

Cumulative Disbursements

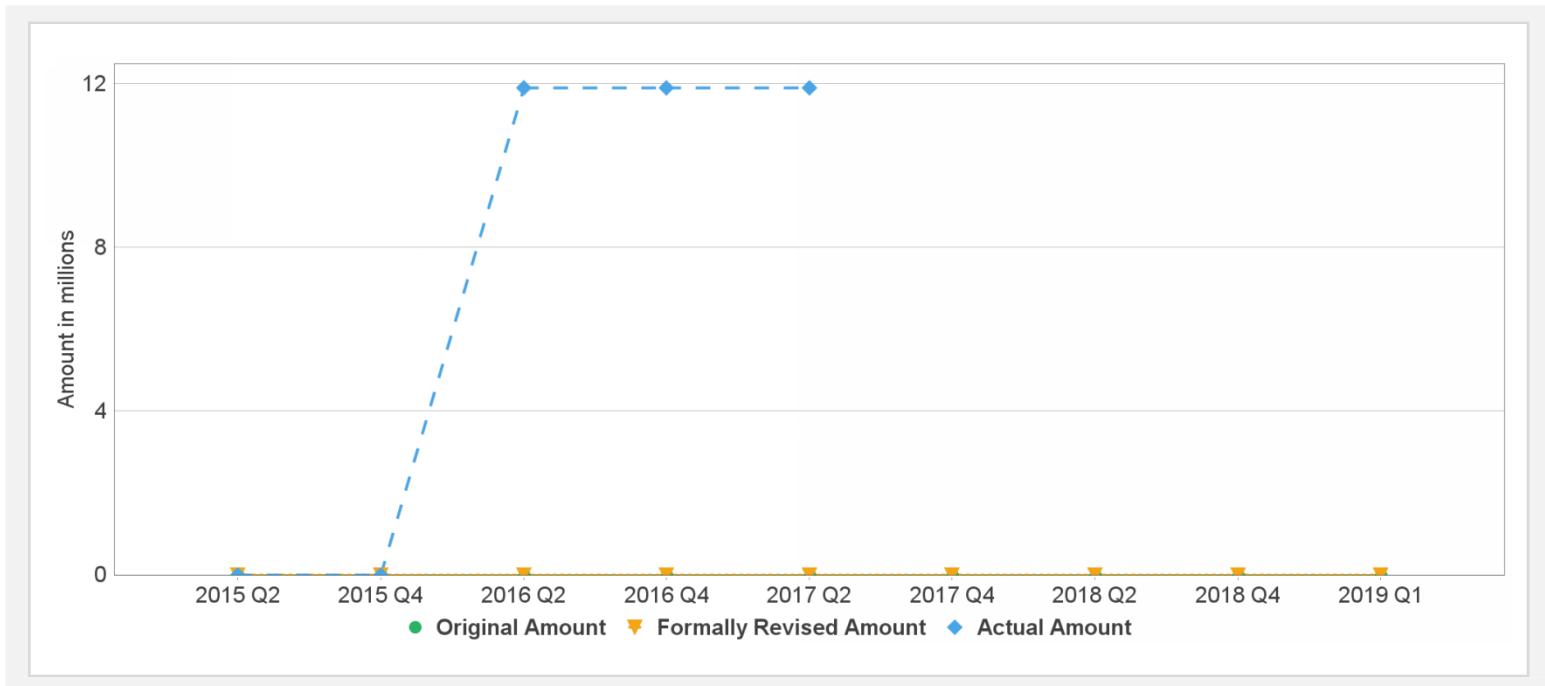

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
