



BF-Youth Employment & Skills Development (P130735)

AFRICA | Burkina Faso | Social Protection & Labor Global Practice |
IBRD/IDA | Investment Project Financing | FY 2013 | Seq No: 7 | ARCHIVED on 22-Jun-2017 | ISR28707 |

Implementing Agencies: Ministry of Economy and Finance, Ministry of Youth, Professional Training, and Employment

Key Dates

Key Project Dates

Bank Approval Date:23-May-2013

Effectiveness Date:03-Mar-2014

Planned Mid Term Review Date:25-Mar-2014

Actual Mid-Term Review Date:28-Jul-2014

Original Closing Date:15-Dec-2018

Revised Closing Date:15-Dec-2018

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective (PDO) is to increase access to temporary employment and skills development opportunities for out-of-school youth.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Labor Intensive Public Works:(Cost \$25.00 M)

Component 2: Skills development:(Cost \$20.00 M)

Component 3: Institutional Capacity Strengthening and Project Management:(Cost \$5.00 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Unsatisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Unsatisfactory	● Moderately Satisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions



The project has been under implementation for three years. Disbursement has picked up. Operational progress is in line to reach or exceed the restructured end targets by project closure.

More precisely, the Labor Intensive Public Works have now reached cumulatively more than 8510 beneficiaries. A cumulative 2442 of first-time apprentices have been trained and by the time of the mission, 495 staff had received further employer requested training. 4145 beneficiaries of diverse (including none) educational backgrounds are being trained in entrepreneurship.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Moderate	● Moderate
Macroeconomic	--	● Moderate	● Moderate
Sector Strategies and Policies	--	● Substantial	● Substantial
Technical Design of Project or Program	--	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Substantial	● Substantial
Environment and Social	--	● Substantial	● Substantial
Stakeholders	--	● Substantial	● Substantial



Other	--	--	--
Overall	--	● Substantial	● Substantial

Results

Project Development Objective Indicators

► Direct project beneficiaries (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,000.00	15,578.00	33,500.00
Date	31-Mar-2013	06-Apr-2016	14-Jun-2017	30-Jun-2018

▲ Female beneficiaries (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	51.44	45.75	30.00

► Youth who completed training programs offered by the Project (disaggregated by program and gender) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	21.85	80.00
Date	31-Mar-2013	06-Apr-2016	14-Jun-2017	30-Jun-2018

► Youth trained who are employed or self-employed one year after completion of training (overall and by sector, in project areas) (Percentage, Custom)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	35.85	60.00
Date	31-Mar-2013	06-Apr-2016	14-Jun-2017	30-Jun-2018

► Number of man days in Labor Intensive Public Works created (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	262,735.00	4,350,000.00	3,174,194.00
Date	31-Mar-2013	06-Apr-2016	14-Jun-2017	30-Jun-2018

Overall Comments

Intermediate Results Indicators

► Roads maintained/rehabilitated (rural) (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	120.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

▲ Roads maintained/rehabilitated (urban) (Kilometers, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	17.00	17.30	60.00



▷ Community woodlots maintained (Hectare(Ha), Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	39.00	355.00

▲ reclaiming floodable areas (aménagement des bas-fonds) (Hectare(Ha), Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	200.00

▲ large diameter wells built (Kilometers, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	37.00

▶ Number of youth employed through LIPW (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,000.00	8,510.00	20,500.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018



▾ Proportion of female participants of LIPW (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	60.43	52.66	30.00

► Out of school youth enrolled in skills development programs (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	7,000.00	13,000.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

▾ Out of school youth enrolled in professional training (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	495.00	2,700.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

► Out of school youth enrolled in apprenticeships (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	2,442.00	3,000.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018



▶ Number of prize winners of a business plan competition (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1,200.00
Date	28-Feb-2017	--	15-Jun-2017	30-Jun-2018

▲ Of which female (out of school youth who are enrolled in skills development programs) (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	31.69	41.93	30.00

▶ Out of school youth who completed in professional training (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	46.67	80.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

Comments

10.82% have finished the programs but are not yet working; 35.85% have found a job.

▲ of which female (Out of school youth who completed in professional training) (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00


► Out of school youth who completed in apprenticeships (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	80.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

▲ of which female (out of school youth who completed in apprenticeships) (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00

► Out of school youth who completed in business development programs (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	17.00	88.00	80.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

▲ Of which female (Out of school youth who completed entrepreneurship /business development programs) (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00



► Number of youth enrolled in the two new training institutions supported by the project in key economic growth sectors (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	700.00
Date	31-Mar-2013	13-Apr-2016	14-Jun-2017	30-Jun-2018

▲ Proportion of female (youth enrolled in the two new training institutions supported by the project in key economic growth sectors) (Percentage, Custom Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	30.00

► Impact Evaluation Studies Conducted (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	N	N	Y
Date	31-Mar-2013	14-Dec-2016	14-Jun-2017	30-Jun-2018

► Beneficiary surveys completed to support on-going training improvement (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	N	N	Y
Date	31-Mar-2013	14-Dec-2016	14-Jun-2017	30-Jun-2018

Overall Comments



Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P130735	IDA-52560	Effective	XDR	33.40	33.40	0.00	10.89	22.51	33%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P130735	IDA-52560	Effective	23-May-2013	18-Jul-2013	03-Mar-2014	15-Dec-2018	15-Dec-2018

Cumulative Disbursements

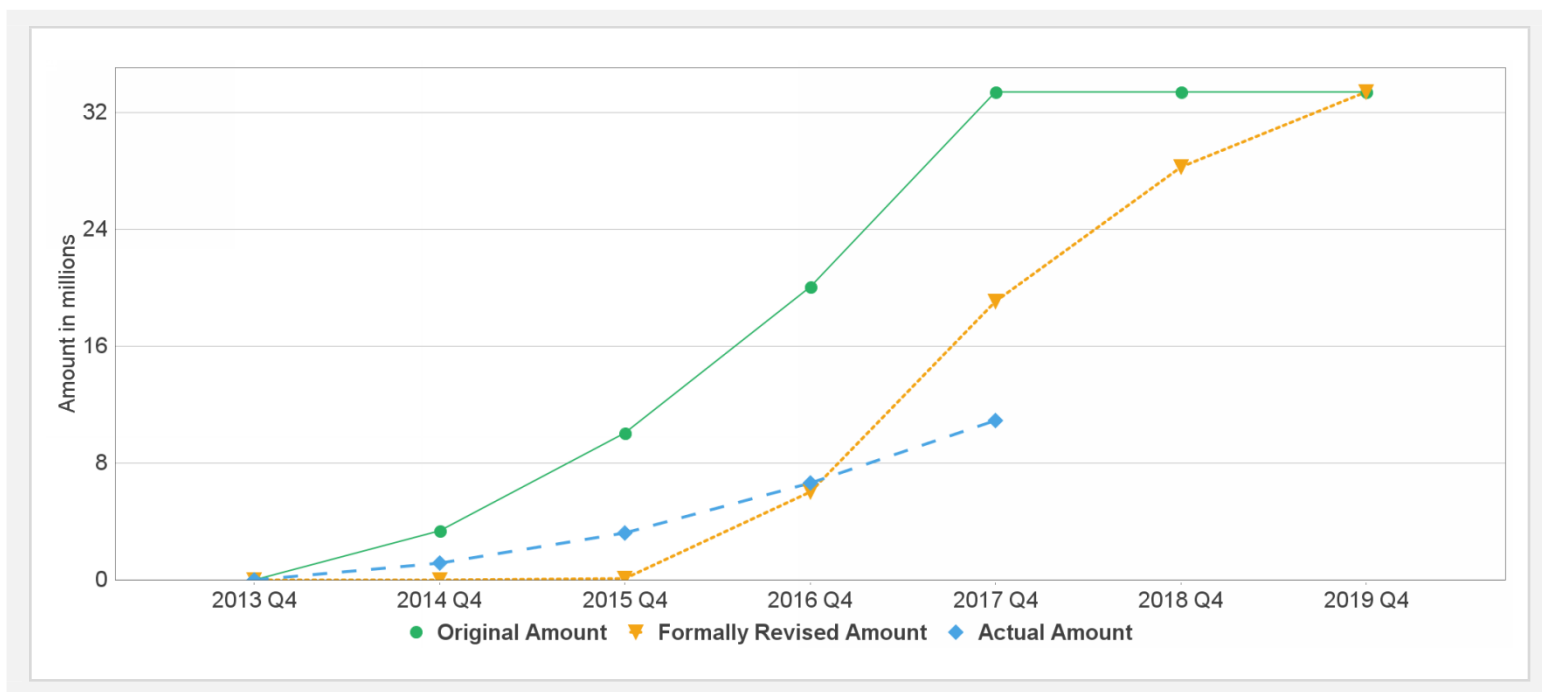

Restructuring History

Level 2 Approved on 14-Jun-2017

Related Project(s)



There are no related projects.
