



Uganda Reproductive Health Voucher Project (P144102)

AFRICA | Uganda | Health, Nutrition & Population Global Practice |
Recipient Executed Activities | Investment Project Financing | FY 2015 | Seq No: 10 | ARCHIVED on 19-Dec-2019 | ISR39810 |

Implementing Agencies: Ministry of Health, Ministry of Finance, Planning and Economic Development

Key Dates

Key Project Dates

Bank Approval Date: 03-Oct-2014

Effectiveness Date: 02-Sep-2015

Planned Mid Term Review Date: 16-Apr-2017

Actual Mid-Term Review Date: 19-Apr-2017

Original Closing Date: 29-Dec-2017

Revised Closing Date: 15-Dec-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to increase access to skilled care among poor women living in rural and disadvantaged areas during pregnancy and delivery.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component One - Package of Safe Delivery Services to Poor Pregnant Women.: (Cost \$9.50 M)
Capacity Building and Project Management.: (Cost \$3.80 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Moderate	● Moderate

Implementation Status and Key Decisions

Uganda Reproductive Health Voucher Project has been implemented successfully the Government of Uganda at total cost of USD 17.3 Million (USD 13.3 from GPOBA Grant and the rest from UNFPA and GoU). The project has achieved and surpassed most of the development objectives, which is to increase access to skilled care among poor women living in rural and disadvantaged areas during pregnancy and delivery. It has supported more than 173,000 women to access improved quality delivery services in 25 districts spread between South West and Eastern Uganda. In the more than 200 contracted health facilities, the project supported improvement in quality and significantly reduced maternal deaths. It provides good lessons on how the government can contract with the private providers to deliver reproductive health services to poor women living in underserved areas.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Substantial	● Substantial
Macroeconomic	--	● Substantial	● Substantial
Sector Strategies and Policies	--	● Moderate	● Moderate
Technical Design of Project or Program	--	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Substantial	● Substantial
Environment and Social	--	● Moderate	● Moderate
Stakeholders	--	● Low	● Low
Other	--	--	--
Overall	--	● Moderate	● Moderate

Results

PDO Indicators by Objectives / Outcomes

Increase access to skilled care among poor women in underserved areas during pregnancy and delivery				
▶ People who have received essential health, nutrition, and population (HNP) services (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	158,322.00	158,322.00	156,400.00
Date	02-Dec-2013	31-Mar-2019	31-Mar-2019	13-Dec-2019
▲ Number of deliveries attended by skilled health personnel (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	158,322.00	173,476.00	156,400.00
Date	02-Dec-2013	31-Mar-2019	30-Sep-2019	13-Dec-2019
Voucher numbers and redemption rate				



▶Number and percentage of vouchers distributed and redeemed for deliveries under the project; (Percentage, Custom Supplement) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	72.00	71.00	70.00
Date	02-Dec-2013	31-Mar-2019	30-Sep-2019	13-Dec-2019

Number and percentage of women attending at least one ANC visits under the project. (Percentage, Custom Supplement) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	90.30	90.30	90.00
Date	02-Dec-2013	31-Mar-2019	31-Mar-2019	13-Dec-2019

Intermediate Results Indicators by Components

Capacity Building and Project Management.				
▶Percentage of voucher mothers satisfied with the services (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	93.00	93.00	90.00
Date	31-Mar-2016	04-Dec-2018	04-Dec-2018	13-Dec-2019
▶Timely verification reports provided (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.00	9.00	12.00
Date	01-Jan-2014	29-Mar-2019	29-Mar-2019	13-Dec-2019
▶Percentage of claims reimbursed timely (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	75.00	75.00	80.00
Date	01-Jan-2014	31-Mar-2019	31-Mar-2019	13-Dec-2019

Component One - Package of Safe Delivery Services to Poor Pregnant Women.				
▶Number and percentage of vouchers distributed and redeemed for postnatal care. (Percentage, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	27.50	71.00	35.00
Date	01-Oct-2013	31-Mar-2019	30-Sep-2019	13-Dec-2019
▲Percentage of pregnant women tested for HIV; (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	75.00	78.50	90.00
▲Number of mothers referred; (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	10,942.00	12,119.00	19,900.00
▶Number of fresh still births (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	431.00	437.00	330.00
Date	30-Dec-2012	31-Mar-2019	30-Sep-2019	13-Dec-2019
▶Number of pregnant women with HIV who receive EMTCT (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3,688.00	3,873.00	8,450.00
Date	01-Jan-2014	31-Mar-2019	30-Sep-2019	13-Dec-2019

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P144102	TF-15995	Effective	USD	13.30	13.30	0.00	13.30	0.00	100%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P144102	TF-15995	Effective	18-Dec-2014	18-Dec-2014	02-Sep-2015	29-Dec-2017	15-Dec-2019

Cumulative Disbursements

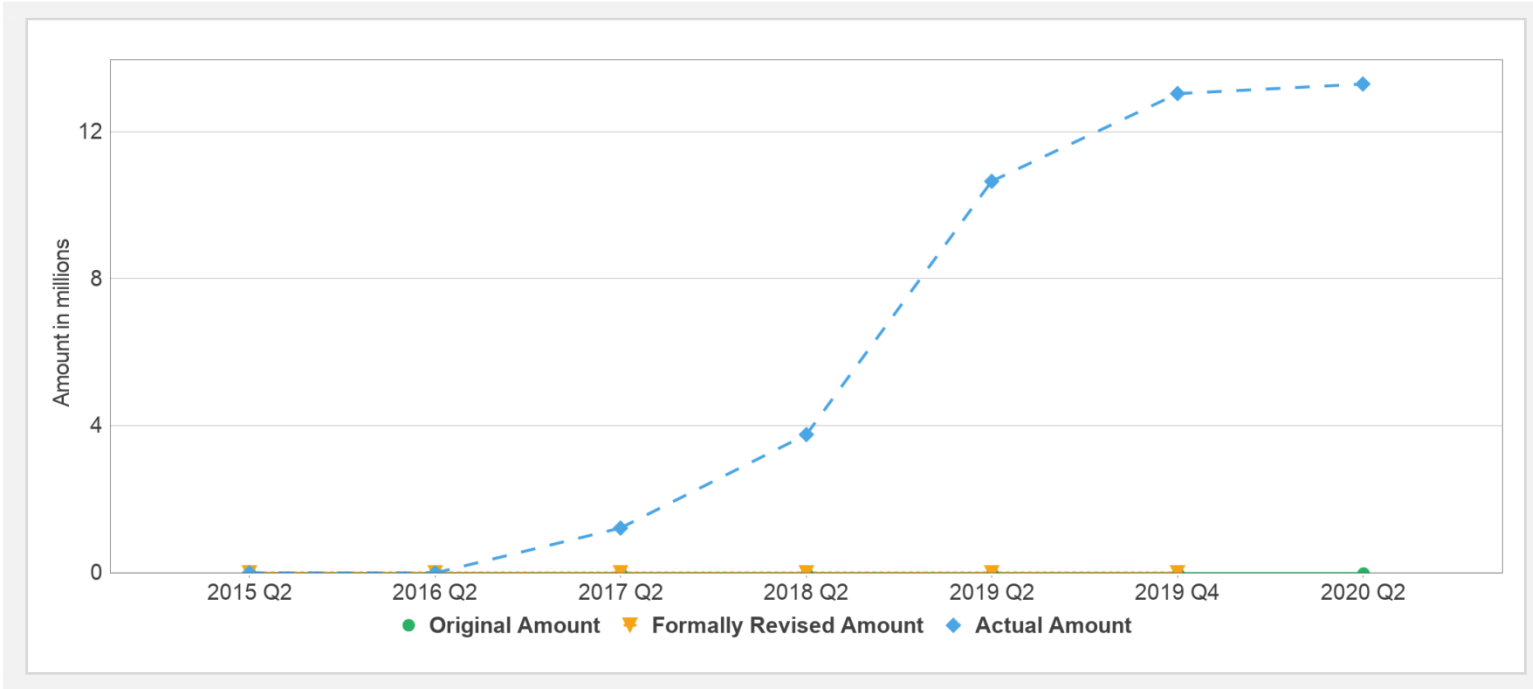

Restructuring History

Level 2 Approved on 03-Oct-2017

Related Project(s)

There are no related projects.
