



## Second Lao Environment &amp; Social Project (former Protected Area and Wildlife Project) (P128393)

EAST ASIA AND PACIFIC | Lao People's Democratic Republic | Environment, Natural Resources & the Blue Economy Global Practice | IBRD/IDA | Investment Project Financing | FY 2014 | Seq No: 14 | ARCHIVED on 29-Jun-2020 | ISR41792 |

Implementing Agencies: Lao People's Democratic Republic, Environment Protection Fund

**Key Dates****Key Project Dates**

Bank Approval Date: 02-Apr-2014

Effectiveness Date: 04-Jul-2014

Planned Mid Term Review Date: 31-Dec-2017

Actual Mid-Term Review Date: 20-Mar-2017

Original Closing Date: 30-Jun-2021

Revised Closing Date: 30-Jun-2021

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

To strengthen the management systems for national protected areas conservation and for enforcement of wildlife laws

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Project Development Objective (If project is formally restructured)

The objective of the Project is to help strengthen selected environmental protection management systems, specifically for protected areas conservation, enforcement of wildlife laws and environmental assessment management.

**Components Table**

Name

Institution Development and Capacity Building:(Cost \$17.40 M)

Management of Wildlife and Protected Areas:(Cost \$17.60 M)

Project Administration and EPF Capacity Building:(Cost \$6.83 M)

**Overall Ratings**

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Implementation Progress (IP)	<input type="checkbox"/> Moderately Satisfactory	<input type="checkbox"/> Moderately Satisfactory
Overall Risk Rating	<input type="checkbox"/> High	<input type="checkbox"/> Substantial

**Implementation Status and Key Decisions**

Implementation progress is largely on track with tangible results becoming apparent in protected areas management, enforcement of wildlife laws, and environmental management, assessment, and planning. The 39 active subprojects have helped improved, to varying degrees, the functional capacity of numerous government agencies that support environmental management in Laos. Some notable steps in the government's monitoring and enforcement role over the past six months include the disclosure of the first set of environmental impact assessment reports for public and



private-sector projects with potentially high environmental or social impacts on the MONRE website for public comment, disclosure of new compliance monitoring reports on both MONRE and EPF websites for 81 hydropower, mining, and roads projects, and daily disclosure of air quality data. However, performance of individual sub-projects remains uneven. The National University of Laos (NUOL) and Provincial Agriculture and Forestry Offices (PAFO) sub-projects continue to maintain their high performance. Areas that are lagging include subprojects aimed at strengthening capacity for wildlife law enforcement, where improvement is still needed in interagency cooperation and the investigation, reporting, and prosecution of illegal activities. Another area that still needs strengthening is protected areas management in two key national parks, including delays in disbursing conservation livelihood development grants to 67 villages within or bordering the protected areas. One reason for these delays are travel and meeting restrictions due to Covid-19, as well as the onset of the 2020 wet season. Efforts are ongoing to address remaining gaps in institutional capacity, ramp up community engagement, improve project efficiency, and further strengthen timeliness and quality of monitoring and evaluation.

## Table 1

### Multiphase Programmatic Approach (MPA) Status

#### Risks

#### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	☐ Moderate	☐ Moderate
Macroeconomic	--	☐ High	☐ High
Sector Strategies and Policies	--	☐ Substantial	☐ Substantial
Technical Design of Project or Program	--	☐ Substantial	☐ Substantial
Institutional Capacity for Implementation and Sustainability	--	☐ Substantial	☐ Substantial
Fiduciary	--	☐ Substantial	☐ Substantial
Environment and Social	--	☐ Moderate	☐ Moderate
Stakeholders	--	☐ High	☐ Moderate
Other	--	--	--
Overall	--	☐ High	☐ Substantial

#### Results

#### PDO Indicators by Objectives / Outcomes

Strengthen capacity on protected area management				
► Increased score on Protected Area Management Effectiveness Tracking Tool (METT) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	11.80	19.40	10.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021



Comments:	<p>The indicator exceeds the end target.          The whole portfolio of LENS2 protected areas (11 protected areas via 10 sub-projects) is now at full implementation stage and showing incremental increases. All PA subprojects except the NEPL NPA subproject (approved in December 2018) have contributed to the actual increase in the METT score. However, it should be noted that METT scores are inherently subjective and the large improvements reflected in the current actual value are based on the scores reported in the PAs own self-assessments. The basis for the large reported score increase from 11.8 to 19.4 has been validated by a consultant hired in early 2020.</p>			
<b>► GEO Indicators are the same with PDO Indicators (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	0.00
Date	31-Dec-2014	31-Dec-2014	31-Dec-2014	30-Jun-2021

<b>Strengthen capacity on wildlife law enforcement</b>				
<b>► Wildlife trafficking cases involving CITES 1 listed species that are referred to the national and/or provincial public prosecutor office (cumulative) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	22.00	24.00	75.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	<p>As of May 2020, 24 wildlife trafficking cases involving CITES 1 listed species have been referred to the public prosecutor office (provincial or national). And, 108 wildlife trafficking cases (involving CITES1 and non-CITES 1 listed species) have been opened for investigation. It is expected that some cases opened for investigation in late 2019 will be referred to the public prosecutor in 2020.</p>			
<b>□ Number of wildlife trafficking cases involving CITES1 and non-CITES listed species opened for investigation (cumulative) (Number, Custom Supplement)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	88.00	88.00	250.00

<b>Strengthen capacity on environmental and natural resource management</b>				
<b>► 5-year provincial or sectoral development plans that include environmental planning, monitoring, assessment, or management components supported by MONRE or MPI (cumulative) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	9.00	20.00
Date	30-Dec-2017	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	<p>ISP has been integrated into the provincial 5-year social-economic development plan of Xayabouly and Khammouane.          GG M&amp;E indicators have been also integrated into sectoral reportings.</p>			
<b>□ Plans supported by MONRE departments on environmental monitoring arrangements (cumulative) (Number, Custom Breakdown)</b>				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	8.00
Date	30-Dec-2017	31-Dec-2018	31-Dec-2018	30-Jun-2021
<input type="checkbox"/> Plans supported by MONRE departments on ISP and/or SEA (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	2.00	7.00
Date	30-Dec-2017	31-Dec-2018	15-May-2020	30-Jun-2021
<input type="checkbox"/> Plans supported by MPI or NIER on GG M&E (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	7.00	5.00
Date	30-Dec-2017	31-Dec-2018	15-May-2020	30-Jun-2021
▶ Up-to-date reports published on relevant government websites including (i) compliance monitoring for Category 2 projects, (ii) state of air and noise quality, (iii) national pollution inventory (cum.) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	18.00	99.00	87.00
Date	30-Dec-2017	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	As of November 2019, 18 reports on noise and air quality have been published on nreri.gov.la. MONRE has also disclosed 81 project compliance monitoring reports (environmental impact category 2 projects) on both MONRE and EPF websites (laoepf.org.la) MONRE has also made extra effort to disclose EIA of investment projects for public comments on dneponre.gov.la			
<input type="checkbox"/> Compliance monitoring reports for hydropower projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	39.00	40.00
Date	30-Dec-2017	30-Apr-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Compliance monitoring reports for mining projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	38.00	24.00
Date	30-Dec-2017	30-Apr-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Compliance monitoring reports for road projects registered in environment impact Category 2 published on the MONRE website (cumulative) (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	4.00	7.00
Date	30-Dec-2017	30-Apr-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> State of air and noise quality report published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	18.00	18.00	7.00
Date	30-Dec-2017	29-Nov-2019	29-Nov-2019	30-Jun-2021
<input type="checkbox"/> National pollution inventory report published on the MONRE website (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	9.00
Date	30-Dec-2017	30-Apr-2019	30-Apr-2019	30-Jun-2021

## Strengthen institutional capacity

## ► Score of functional capacity of EPF and key institutions implementing subprojects (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	35.80	43.90	31.00
Date	31-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	Progress toward achieving the functional capacity indicator target (average of the scores for the participating agencies or institutions) exceeds the end of target, June 2021. EPF continues to support each SDA in their self-assessment and pre-post test tool start being used by SDAs (to measure quality of training delivered and provide quantitative data for self-assessment).			
<input type="checkbox"/> Score of functional capacity of Environment Protection Fund (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	22.00	62.00	67.00	52.00
Date	31-Dec-2015	29-Nov-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Score of functional capacity of Department of Public Relation of the Prime Minister Office (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	33.00	33.00	34.00
Date	31-Dec-2015	31-Dec-2018	31-Dec-2018	30-Jun-2021
<input type="checkbox"/> Average of score of functional capacity of Faculties (NUOL FFS, FSS, FNS, FES and FEB) (number) (annual) (Number, Custom Breakdown)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	38.40	38.40	28.00
Date	31-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Average of score of functional capacity of Protected Area Management Units (NEPL, WMPA and 7 PAFOs) (number) (annual) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	25.70	29.10	31.00
Date	31-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Score of functional capacity of MAF DOF Protected Area Management Division (number) (annual) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	10.00	31.00	56.00	22.00
Date	31-Dec-2014	29-Nov-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Score of functional capacity of National Academy of Public Administration (NAPA) (annual) (Number) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	25.00	40.00	13.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021

### Intermediate Results Indicators by Components

Protected area management system and biodiversity conservation				
▶ Score tracking the development and management of a NPA system (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	32.00	70.00	90.00
Date	30-Dec-2014	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	This indicator is back on track (EOP target is: 90) As of April 2019, the report on Optimization of the NPA Management System (legal, policy, institutions, and financing) have been finalized; decrees establishing Nakai Nam Theun National Park and Nam Et-Phou Louey as National Park approved by to the Prime Minister Office; and seven (7) technical guidelines signed by MAF Minister. <i>Note:</i> Four (4) additional guidelines have been finalized (pending MAF Minister signature) and 3 guidelines are still at finalization stage.			
▶ Village organizations that meet the terms of Conservation Agreements, and as a result, receive grants for implementing their action plans (cumulative) (Number, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	106.00	124.00	190.00
Date	30-Dec-2014	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	This indicator is on track (EOP target: 190) As of May 2020, 124 community conservation agreements have been signed. NE-PL and NNT sub-project have started to implement activities related to this specific indicator. They are expected to disburse village livelihood development funds to all villages in September 2020.			
<input type="checkbox"/> Village organizations with at least 40% female participation (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12.00	79.00	160.00
Date	30-Dec-2014	29-Nov-2019	15-May-2020	30-Jun-2021
<b>► Area within selected PAs where the status of selected wildlife population and threats are measured (annual) (Hectare(Ha), Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	242,000.00	370,960.00	370,960.00	634,000.00
Date	30-Dec-2016	29-Nov-2019	29-Nov-2019	30-Jun-2021
Comments:	This indicator is reported annually. NE-PL sub-project has been implemented. The area within NEPL National Park where the status of selected wildlife population and threats are measured is 163,000 ha so it's expected a sharp increase in the total area.			
<b>► Area within selected PAs where the gross forest loss rate is measured (Hectare(Ha), Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	305,000.00	781,946.00	1,195,145.00	1,250,000.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	The IR indicator is on track As of May 2020, 1,195,514 hectares of 9 PAs and 2 NPAs have been measured			
<b>► Wildlife crime cases detected by law enforcement officers of SDAs supported by the project (cumulative) (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	188.00	2,440.00	3,188.00	3,100.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	The IR indicator exceeds the end target. Around 3,188 cases detected have been reported by wildlife law enforcement agencies (DOFI and POFIs, Customs and Environmental Police).			



Environmental management and pollution control				
▶ Category 1 and Category 2 projects that are under design, construction or operation that have a valid Environmental Compliance Certificate (ECC) (cum.) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	19.00	47.00	54.00	50.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	<p>The IR Indicator is on track:</p> <p>However, Issuance of ECC for hydropower and road projects are unlikely to meet their targets due to the government having a moratorium on hydropower project with a capacity less than 15kw. In addition, PONREs are facing difficulties forcing the road rehabilitation projects to carry out an Initial Environmental Examination (IEE) as mandated in the EIA decree. Moreover, there are far fewer new projects than planned.</p> <p>As of May 2020, the total number of Category 1 and 2 projects with valid ECC is 594.            Category 1 hydropower, mining and road projects with ECC is 93, 278, and 55 respectively            Category 2 hydropower, mining and road projects with ECC is 97, 46 and 25 respectively</p>			
☐ Category 1 hydropower projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	35.00	60.00	79.00	50.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
☐ Category 1 mining projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	11.00	88.72	111.00	50.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
☐ Category 1 road projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	46.33	57.00	50.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
☐ Category 2 hydropower projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	60.00	62.00	85.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
☐ Category 2 mining projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target





Value	10.00	15.00	17.00	50.00
Date	30-Dec-2016	29-Nov-2019	15-May-2020	30-Jun-2021
□ Category 2 road and railway projects with ECC (cumulative) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9.00	12.00	50.00
Date	30-Dec-2016	31-Dec-2018	15-May-2020	30-Jun-2021
▶ Score tracking the development of national, provincial or sectoral guiding documents and planning tools that integrate environment into development planning (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	55.00	60.00	90.00
Date	30-Dec-2017	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	<p>The IR indicator is on track:</p> <p>Substantial progress has been made: the National Green Growth Strategy has been developed and endorsed by Government on Nov. 2018 and finally promulgated by PM Office later in January 2019. The SEA guidelines has been developed and approved by MONRE Minister later in December 2018. The ISP Decree was completed in early 2019.</p> <p>The ENR M&amp;E guidelines was completed, approved in July 2017 (Departmental Decision) and printed in April 2018.</p> <p>During the reporting period, ISP has been integrated into the 5-year social-economic development plan of Xayabouly and Khammouane. Consequently, the score increase from 55 to 60.</p> <p>MPI and MEM are in the early stage of SEAs development.</p>			
▶ Score tracking the design and adoption of pollution management instruments (point) (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	30.00	30.00	80.00
Date	30-Dec-2017	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	<p>The IR indicator is on track even though the it's still 30 points behind the annual target.</p> <p>Some progress have been made during the year, the Decision on National Environmental Standard has been approved (promulgated in February 2017). The Pollution Prevention and Control Regulation has been reviewed by a vice minister of MONRE. It is expected to be submitted to the MONRE minister for approval and signature after which it will gain another 30 points. National Pollution Control planning documents [Vision to 2030, 10-Year Strategy (2016-2025), and 5-Year Action Plan (2016-2020)] are at advanced stage. However, it's unlikely that the 10-Year strategy will be completed by the sub-project closing date because it has to be reviewed by the National Assembly which will prolong the process of getting it approved.</p>			
Institutional capacity enhancement and sustainable financing development				
▶ Staff of SDA and SDA partner institutions that received formal short courses or participate in study tours under the project (cumulative) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	8,203.00	10,815.00	3,000.00
Date	30-Dec-2015	29-Nov-2019	15-May-2020	30-Jun-2021
Comments:	The indicator is on track: the annual target has been exceeded (3,000)			
<input type="checkbox"/> Female staff (cumulative) (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2,028.00	2,657.00	600.00
Date	30-Dec-2015	29-Nov-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Financing mobilized by EPF each year from (a) public sources and (b) private sources (annual) (Amount(USD), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	800,000.00	1,327,028.56	620,000.00	1,600,000.00
Date	30-Dec-2014	19-Dec-2019	15-May-2020	30-Jun-2021
Comments:	<p>The annual target for 2020 is unlikely to be achieved.  As of May 2020, US\$ 510,000 have been collected from the private sector and US\$ 110,000 earned from interest and lending revenue from project credits (non-World Bank supported)  However, EPFO has raised \$400,000 which they will receive from the Implementation of the Governance Forest Landscape and Livelihood Project supported by GIZ. The fund will be used for project administration. Moreover, it is also expected that after completion of the EPF accreditation process for GCF small grant, about \$10M grant fund can be made available starting 2022.</p>			
<input type="checkbox"/> Funds from public sources (annual) (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	350,000.00	391,231.55	110,000.00	700,000.00
Date	30-Dec-2014	19-Dec-2019	15-May-2020	30-Jun-2021
<input type="checkbox"/> Funds from private sources (annual) (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	450,000.00	935,797.01	510,000.00	900,000.00
Date	30-Dec-2014	19-Dec-2019	15-May-2020	30-Jun-2021

## Performance-Based Conditions

### Data on Financial Performance

#### Disbursements (by loan)




Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P128393	IDA-53830	Effective	USD	12.50	12.50	0.00	11.50	0.00	100%
P128393	IDA-56200	Effective	USD	15.00	15.00	0.00	8.90	5.84	60%
P128393	IDA-H9150	Effective	USD	4.50	4.50	0.00	4.23	0.00	100%
P128393	TF-16619	Effective	USD	6.83	6.83	0.00	5.01	1.82	73%

#### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P128393	IDA-53830	Effective	02-Apr-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2021
P128393	IDA-56200	Effective	29-Apr-2015	04-Jun-2015	01-Oct-2015	30-Jun-2021	30-Jun-2021
P128393	IDA-H9150	Effective	02-Apr-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2021
P128393	TF-16619	Effective	14-May-2014	14-May-2014	04-Jul-2014	30-Jun-2021	30-Jun-2021

#### Cumulative Disbursements

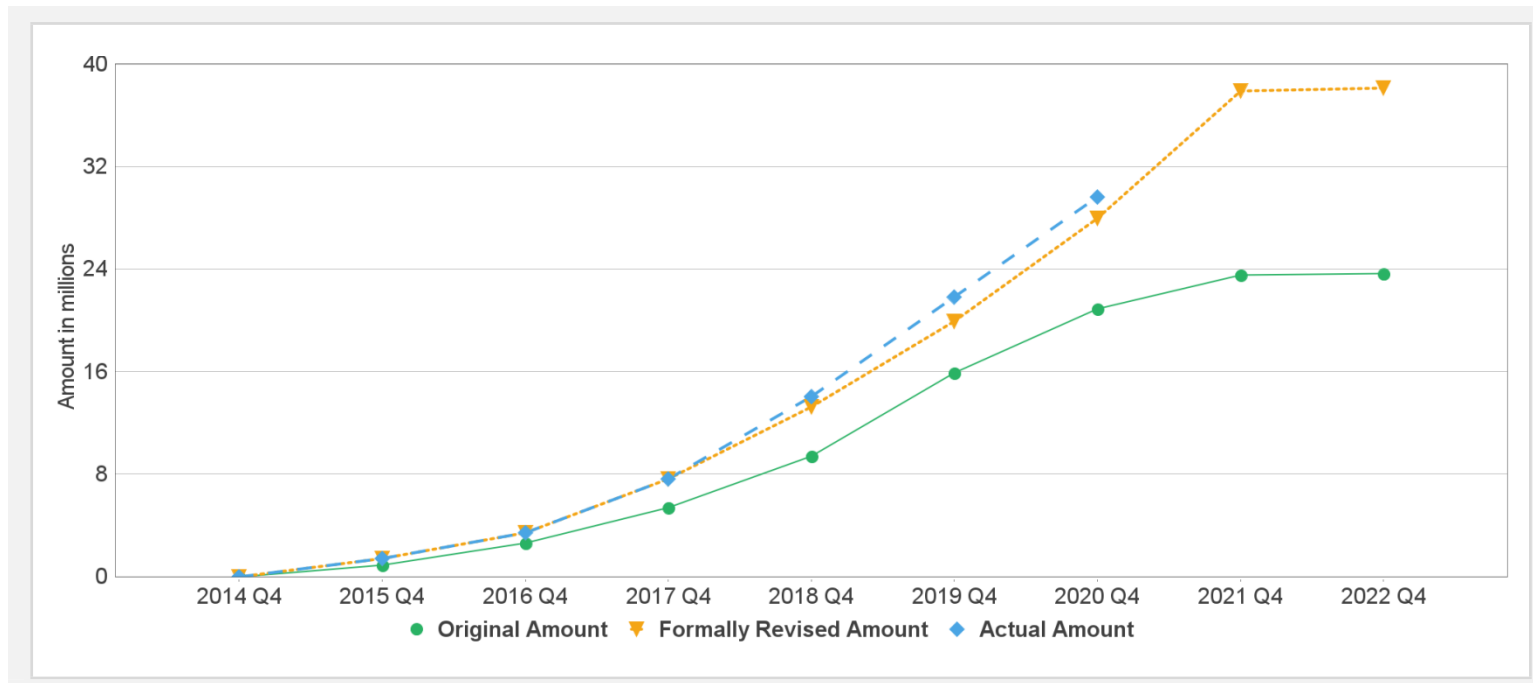

#### Restructuring History

Level 2 Approved on 08-Feb-2018



---

**Related Project(s)**

P128392-Second Lao Environment & Social Project (formaly Protected Area and Wildlife) ,P152066-Second Lao Environment and Social Project (Additional Financing to the Protected Area and Wildlife Project)

---
